

**STEP 10**


Cast basement slab with heave protection boards below

**STEP 11**

Cast liner wall to full height on the sides of the contiguous piled wall

Cast liner wall to half height and prop against basement slab

Remove inclined prop to mass underpin to allow continuation of liner wall

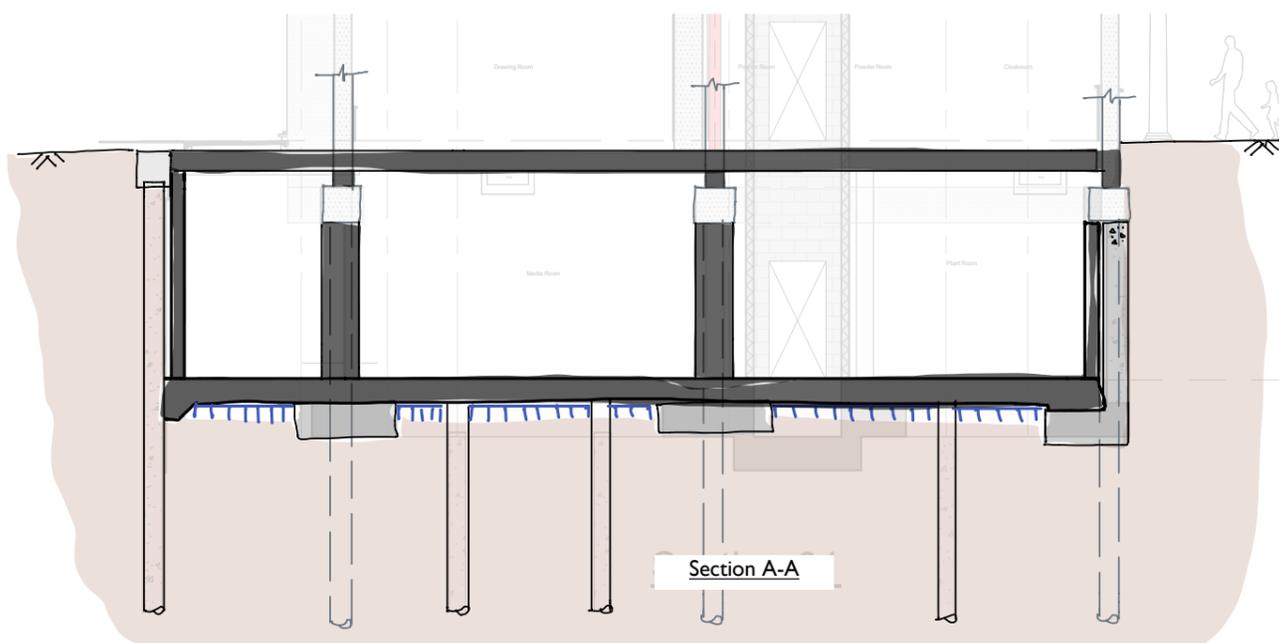

**STEP 12**

Cast mass concrete columns to internal piles on to strip footings

Remove temporary vertical props after mass concrete columns to internal piles have gained full strength

**STEP 13**

Backfill behind external excavations

Cast infill parts of ground floor slabs

Notes

- Not to scale
- For information only
- Final construction sequence by main contractor

**WEBB  
YATES** ENGINEERS

020 3696 1550  
london@webbyates.com  
www.webbyates.com

Drawing No.  
J5106-S-SK-0034

Project  
Maresfield Gardens

Status  
S9

Drawing Title  
Construction sequence (4 of 4)

Date  
23.01.24

Drawn by  
NW

Scale  
NTS

Revision  
00
