



Report	Arboricultural Method Statement (AMS) and Tree Protection Plan (TPP)
Descriptor	An Arboricultural Method Statement and Tree Protection Plan derived from the Arboricultural Impact Assessment
Address	British Museum Great Russell Street, London WC1B 3DG
Ref No	250223
Client	William Horton Capital Planning & Programme Management The British Museum Great Russell Street, London WC1B 3DG
Instructed	George Hake ECP Project Manager
Documents referenced	<ul style="list-style-type: none"> • SW001-ABA-1000-X_01-DDG-C-9000 (Client-provided) • SW001-ABA-1000-X_01-DDG-C-9001 (Client-provided) • SW001-ABA-1000-X_01-DDG-C-9002 (Client-provided) • SW001-ABA-1000-X_01-DDG-C-9003 (Client-provided) • SW001-ABA-1000-X_01-DDG-C-9004 (Client-provided) • SW001-WWA-1040-C-DDG-A-1911 (Client-provided) • SW001-TBM-XX-XX-DR-V-1684 (Tower Crane Layout) (Contractor-provided) • SW001-TBM-XX-XX-DR-V-1705 (Tower Crane Dismantle Outline) (Contractor-provided) • Tree Survey Report and Tree Constraints Plan Ref. 231005 • Arboricultural Impact Assessment Ref. 231005 • Arboricultural Method Statement Ref. 231005 • Arboricultural Impact Assessment Ref. 250113
Prepared	B. Yarwood
Reviewed	13.02.25
Date completed	O.R.B.

Contents

1: INTRODUCTION	3
1.1 ASPECTS DEALT WITH WITHIN THIS METHOD STATEMENT:	3
1.2 ASPECTS NOT DEALT WITH WITHIN THIS METHOD STATEMENT	3
2. BACKGROUND INFORMATION	3
2.1 NAMES AND CONTACT NUMBERS OF PARTIES CONCERNED	3
2.2 AVAILABILITY OF THIS METHOD STATEMENT.....	4
3: SUPERVISION AND MONITORING	4
3.1 MONITORING AND SUPERVISION	4
3.2 SITE MANAGEMENT.....	4
4: SCHEDULE OF TREE WORK	5
4.1 TREE WORKS TO BE CARRIED OUT PRIOR TO PROPOSED WORKS	5
5: SEQUENCE OF EVENTS	6
6. INSTALLATION OF STEM PROTECTION	7
7. CREATION OF STORAGE AREA	7
8. CRANE MOVEMENTS	7
9. ARBORICULTURAL SUPERVISION OF TRENCHES	8
9.1 USE OF HAND TOOLS AND HAND-HELD MACHINERY ONLY.....	8
9.2 METHODOLOGY FOR EXCAVATING AROUND AND PROTECTING ROOTS.....	8
10: GENERAL SITE CONDITIONS AND TREE PROTECTION MEASURES	9
APPENDIX 1: LIMITATIONS OF ARBORICULTURAL METHOD STATEMENT	10
APPENDIX 2: STEM PROTECTION – TREE BOXES	11

ATTACHMENTS

Tree Protection Plan – Ref. 250223

1: Introduction

1.1 Aspects dealt with within this Method Statement:

The Arboricultural Method Statement (AMS) is a methodology for the implementation of any aspect of development that has the potential to result in loss of or damage to a tree identified as suitable to be retained.

The AMS takes into consideration construction operations undertaken in the vicinity of the trees. It will deal with such issues as site access, intensity of construction activity, space needed for works, location of temporary storage of materials and location of service runs.

This AMS includes with it a Tree Protection Plan (TPP). The TPP outlines trees to be retained, removed, preliminary location of barriers and type of barrier to be installed. This method statement contains a timetable indicating when and how specific works adjacent to trees should be carried out.

This is an updated AIA based on information gathered from the Tree Survey Ref:231005, and Arboricultural Impact Assessment Ref: 231005.

1.2 Aspects not dealt with within this Method Statement

Please also refer to Appendix 2.

This report does not deal with issues relating to Subsidence or Heave either as a result of retention or removal of trees. It does not consider the water demands of the trees present to enable decisions as to foundation type and depth. It is considered that such considerations are best dealt with in a different report having liaised with the structural engineer. This can be provided on request.

2. Background Information

2.1 Names and Contact numbers of Parties concerned

Contact Name	Company/ Organisation	Role	Contact details
William Horton	Capital Planning & Programme Management The British Museum	Project Manager	whorton@britishmuseum.org 07872 858308
TBC	WRIGHT & WRIGHT ARCHITECTS	Architect	020 7428 9393
TBC	Alan Baxter	Engineer	aba@alanbaxter.co.uk 020 7250 1555
TBC	TBC	Contractor	TBC
Oliver Booth	Writtle Forest Consultancy Ltd	Arboricultural Consultant	o.booth@writtleforest.co.uk 01277 355970
TBC	London Borough of Camden	Local Authority Tree Officer	0207 974 4444

2.2 Availability of this Method Statement

The Site Manager and appointed Contractor will each hold a copy of the document, including the Tree Protection Plan. Copies of this document will be made available for contractors visiting site.

3: Supervision and Monitoring

3.1 Monitoring and Supervision

Arboricultural supervisory works and monitoring visits must be confirmed by formal correspondence circulated to all relevant parties, including the council. These records of site visits will provide proof of compliance.

Seven days' notice is required prior to the commencement of works requiring supervision.

3.2 Site Management

All tree protection measures detailed in this document must be fully understood by all the parties involved in the development. Clarification or modifications to the consented details must be recorded and circulated to all parties in writing. These documents should then form the basis of any supervision arrangements between the Arboricultural Consultant and the proposer, as agreed with the Local Planning Authority where applicable.

It is the Site Manager's responsibility to ensure that the requirements set out within the Arboricultural Method Statement are known and understood by all site personnel. Copies of pertinent documents should be kept on site at all times. The site manager will brief all personnel who may have an impact on any trees and relay specific tree protection requirements.

This methodology should be a part of all site induction procedures and written into appropriate site management documents. The following pertinent points should be explained to all personnel who could have an impact on trees;

1. The specification of the Tree Stem Protection.
2. The requirement for Tree Stem Protection to be sufficiently robust to prevent incursion by construction activity.
3. Why it is essential that the Tree Stem Protection remain throughout the works.
4. The importance of the 'exclusion zones' around retained trees.
5. The potential damage caused to trees and new tree planting by compaction of soils and the requirement for ground protection.

4: Schedule of Tree Work

4.1 Tree works to be carried out prior to proposed works

Tree Number	Species	Works required
T1	Bay Laurel	Cut back by up to 1m to facilitate installation of Tree-Box.
T2	London Plane	Crown reduce height and spread by 3.5m.
T8	London Plane	Initiate high pollard at a height of approx. 12m. (Permission granted by Camden Council on the 25 th November 2024, application Ref: 2024/4686/T)
T10	Sycamore	Cut back by 2m to facilitate crane movements in the area. Note: This is a third-party tree, liaison and permission required from owner if access and climbing of tree required to carry out pruning.
T11	Cherry	Cut back by 2m to facilitate crane movements in the area. Note: This is a third-party tree, liaison and permission required from owner if access and climbing of tree required to carry out pruning.
T23	Field Maple	Reduce crown to the north and the west by up to 1.5m to suitable growth points. Note: This is a third-party tree, liaison and permission required from owner before carrying out pruning.
T24	Field Maple	Reduce crown to the north-west by up to 1.5m to suitable growth points. Note: This is a third-party tree, liaison and permission required from owner before carrying out pruning.

5: Sequence of Events

Sequence	Brief outline of events	Arboricultural input required	Estimated Timings
1.	Carry out tree work as detailed in section 4.1 above.	Yes – <ol style="list-style-type: none"> 1. To meet with the contractor (TBC) before works commence to discuss tree works. 2. Site visit to check that tree works have been completed satisfactorily. 	February 2025
2.	Installation of Tree Boxes, signage and clear working area for crane operations.	Yes - To ascertain viability of working area and protection to the trees. Working area for crane operations TBC.	Late February/ Early March 2025.
3.	Installation of scaffolding to facilitate works to façade of West Wing building.	None.	Late March/ April 2025.
4.	Works to West Wing building.	None.	Late March/ April 2025.
5.	Demolition of temporary buildings to internal West Rd.	Yes – To review demolition methodology.	Between June-September 2025.
6.	Installation of new below ground utilities along the western side of main building.	Yes - To supervise and monitor works to ensure minimal disruption and damage to any discoverable roots. (Areas requiring supervision are highlighted on the TPP). Note: Seven days’ notice is required by the arboriculturist prior to the commencement of each stage of works requiring supervision.	Between May-October 2025.
7.	Demolition of existing energy centre	Yes – To review demolition methodology.	Estimated December 2025 onwards.
8.	Construction of new SWEC building, including utilization of a crane.	None.	December 2025 onwards.
9.	Construction of a sub-station on 6no. concrete pad foundations to the east of the main building with associated trenching to allow for new services to be installed.	None.	TBC. Estimated December 2025 onwards.

Sequence	Brief outline of events	Arboricultural input required	Estimated Timings
10.	Installation of new services/ improvement of existing services below ground to the east of the main building.	Yes – <ol style="list-style-type: none"> To review plans prior to commencement of works. To supervise and monitor works to ensure minimal disruption and damage to any discoverable roots. (Areas requiring supervision are highlighted on the TPP). <p>Note: Seven days’ notice is required by the arboriculturist prior to the commencement of each stage of works requiring supervision.</p>	TBC. Estimated December 2025 onwards.
11.	Re-inspection of retained trees.	Yes - Site visit to carry out the inspection of retained tree within one month of the completion of works.	Annually.

A construction programme relating to all works on the east side of the main building is currently in development. This will need to be reviewed by the arboriculturist and may in turn necessitate a review of the AIA, AMS and TPP documents.

6. Installation of Stem Protection

The installation of Stem Protection (Tree-Boxes) prior to commencement of the works are shown as of the TPP and relate to T1, T2, T23 and T24. The Stem Protection will remain in-situ throughout the main construction and only removed on completion of the proposed works. A methodology for the installation of Tree Boxes can be found in Appendix 2.

6.1 Arboricultural Consultant Role

1. Review trees, post tree works to check that the works have been completed satisfactorily.
2. Review Stem Protection to ensure they are installed satisfactorily.

7. Creation of Storage Area

On the east side of the build, once the portacabins are removed, an area to the south can be established for storage of materials as required. It will be necessary to ensure that the base of this area is as of existing hard stand.

The establishment of this area must be out of the drip line of tree canopies T23 and T24.

8. Crane Installation/ Movements

Movement of materials as of demolition and construction relating to the SWEC building will be assisted with a 35m tower crane. It is understood that this will be installed vertically in situ using a mobile crane located in the courtyard area east of T2. The crane will be supported by piled foundations. The mast, prior to installation, will be laid on the hardstanding between the southwest gate and T2. The same area, as indicated on the TPP, will be used as a crane pick up area, where materials will be lifted from

transport vehicles. Crown reduction works, as detailed in 4.1, shall allow clearance to facilitate these movements. It is understood that the materials will then be slewed anticlockwise to the construction area. The dismantling of the tower crane following completion of the build, shall follow the reverse of this procedure.

A banksman will be required for all lifting operations and should be briefed as to the importance to be mindful of tree canopies.

9. Arboricultural Supervision of Trenches

Works that may affect tree roots are associated with movement of existing services and installation of new services, namely new surface water drainage, combined drainage, below ground and surface level channel drains, gulleys and manholes. From historic investigation as to rooting activity of trees in the area, six areas are highlighted where roots maybe encountered during excavations. These areas are highlighted within the TPP and works within them shall be undertaken under the supervision of an attending arboriculturist. Seven days' notice will be required by the arboriculturist before each stage of excavation works commence.

9.1 Use of Hand tools and Hand-held machinery only

It will generally be necessary to use hand held tools when excavating to ensure minimal damage to tree roots. This will include the use of hand operated concrete breakers. Only the concrete that needs to be excavated to enable the installation of the services will be removed. The remaining hard standing will function as ground protection in the course of the excavation. Concrete will be broken up and then removed with hand tools.

Most roots will utilise the area between the soils and the concrete, as the temperature gradients between the strata will lead to elevated water resource. Digging will commence with hand tools. Where roots are encountered then an Airspade will be used to expose the root.

Care will be taken by the operative to ensure that the outer surface of the root tissue is not damaged by the Airspade. It will be the decision of the Consulting Arboriculturist as to whether to progress works with a mini digger, if it is deemed that no roots will be encountered in the dig consequent to the initial excavation by hand.

All back fill of excavation must be carried out by hand around areas where there are protected roots.

9.2 Methodology for excavating around and protecting roots

1. Excavations within the areas as identified on the TPP are to be carried under Arboricultural Supervision using hand tools and air-spade only, unless directed by the attending arboriculturist.
2. Excavation is to be of minimal dimensions and depth. Significant Roots (>25mm Ø) encountered are to be retained, protected and worked around. Smaller roots (<25mm Ø) are to be pruned back using a sharp tool such as secateurs leaving as small a wound as possible, only if required to facilitate excavation. Pruning cuts will be preferentially made at growth points.
3. Details of any roots (>25mm dia.) or significant root mass are to be logged to inform future management of the surrounding trees.
4. Exposed retained roots will be wrapped in hessian with hydro gel crystals and inert compost material to prevent drying out and desiccation.
5. Excavation to be carefully backfilled with the removed material and lightly compacted. Areas around roots must not be compacted with any machinery.

10: General Site Conditions and Tree Protection Measures

Storage of Materials

Designated areas for storage of materials and site office will be decided by the Site Manager before any works can commence. It is advisable to consult with the Arboriculturist regarding the locations of the storage areas and site office.

Discharge of Contaminants

No materials that are likely to have an adverse effect on tree health, such as oil, bitumen or cement will be discharged within the RPA of any of the trees to be retained. It is advised that the disposal of all waste materials is carried out in an appropriately sustainable fashion.

Contingency Plans

Should there be any contamination of soils either within or adjacent to the RPA these should be dealt with as quickly as possible with a proprietary emergency clean up kit. The situation should then be assessed as to whether it is appropriate to remove soils. An Arboriculturist should be consulted before a decision is made. The protection barriers erected should be able to be removed relatively easily to access the area in event of an emergency.

Access to the area of proposed works

Main access to the site is understood to be from the south via West Road. It is considered that these would be the only access point into the site for the purposes of carrying out the development as proposed. If there are any other proposed access points into the site, this should be agreed prior to use with the Arboriculturist.

Cranes and Lifting Equipment

All lifting equipment, including cranes if utilised, should be so positioned that they operate without contact with the retained trees. Care must be taken so that the arc of the boom fitted to the lifting equipment is sufficiently clear of the retained trees.

Boundaries/ Scope of the Site

The appointed Arboricultural Supervisor must be consulted if the boundaries of the site are extended or if excavations/ storage/ construction related to this development is to be carried out on other parts of the wider area, outside of the development site as indicated on the Tree Protection Plan.

Appendix 1: Limitations of Arboricultural Method Statement

Limitations of the Report

Please also refer to sections 1.2 and 1.3 at the beginning of this report.

- The report is based on information provided by third parties and the specifications and recommendations is dependent upon information provided therein.
- This report does not consider the possible implications to any present or future built structures other than those considered within the report.

Findings of the Survey and the Report

- Validity, accuracy and findings of the report will directly relate to the accuracy of information provided at the time of the tree survey.

Timing of the Survey and the Report

- The considerations/ findings in this method statement are valid for one year.
- Such considerations/ findings will become invalid if any building works are undertaken, soil levels are altered or tree work undertaken outside of the scope of works as detailed and presented at the time of compiling this report.
- If there are any alterations to either the property or soil levels, or if tree works are carried out, it is recommended that a new tree report is undertaken.

Trees in relation to other Properties:

- This report/survey only considers the trees in relation to the site as identified.
- It does not comment on possible effects of trees on neighbouring properties, including in relation to subsidence or heave, or with regard to possible hazards presented by trees surveyed.
- Neighbouring owners of trees that are identified as posing a possible risk to the property/site in question should seek their own advice as to possible effects of the recommendations given within this report.
- Damage to, or possibility of damage to, any other structure that is not referred to within the report is not considered unless otherwise specified. This includes both neighbouring structures and any other structure on the property.

Trees in Relation to Subsidence, Heave and Direct damage

- This report does not deal with issues relating to subsidence or heave in relation to any built structures and surrounding vegetation whether the structure or vegetation falls within the boundaries as considered or lies beyond the boundaries.
- The report does not consider issues relating to subsidence or heave in relation to any proposed built structures or future vegetation whether within the boundaries as considered or beyond the boundaries
- It is prudent to consider the effects of heave on any property if trees are removed.
- Similarly, the issue of direct damage (when the roots of a tree have physical contact with a structure) is not considered within this report.

Trees subject to statutory controls:

- If the trees are covered by a Tree Preservation Order or are located in a conservation area it will be necessary to consult the local authority before any pruning works, other than certain exemptions, can be carried out.
- The works specified above are necessary for reasonable management and should be acceptable to the local authority. However, tree owners should appreciate that the local authority may take an alternative point of view and have the option to refuse consent.

Trees are subject to changes outside man's control:

- Trees are living organisms subject to changes outside man's control. Trees and environment alter with the seasons it is as well to inspect trees whilst in full leaf and when out of leaf.
- If there are any harsh or unexpected weather conditions, or heavy storms it is also prudent to inspect trees.
- Changes to ground water conditions will affect the root growth of a tree. Such changes are not always the result of man's influence and other factors may be involved.

Limitations of use of copyright:

- All rights in this report are reserved. Its content and format are for the exclusive use of the addressee in dealing with this site. It may not be sold, lent, hired out or divulged to any third party not directly involved in this site without the written consent of Writtle Forest Consultancy Ltd.

Appendix 2: Stem Protection – Tree Boxes

Before the commencement of any works on site (other than those set out in the schedule of tree works, contained in this document), protective vertical barriers must be erected. The location of the barriers is illustrated on the Tree Protection Plan.

The barriers are to be erected to exclude construction activity in the RPAs of retained trees.

The barriers will remain in place until completion of the main construction phase and then only removed with the agreement of the consulting Arboriculturist.

Other than works detailed within this method statement or approved in writing by the local planning authority, no works shall take place within the exclusion zones defined by the protective fencing. No vehicles will be allowed to enter areas to be protected by the barriers.

Specification of Stem Protection

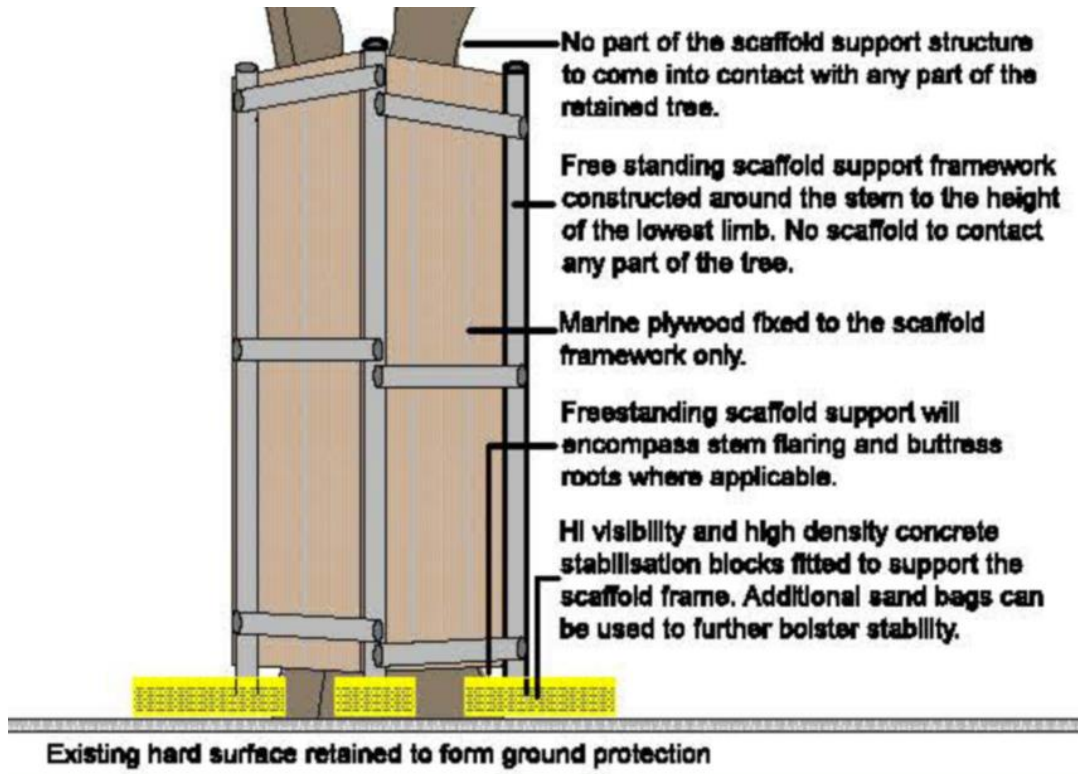


Fig. 1: Example of Stem Protective on hard surface areas.
