
							2012										2013					
Line	Name	Duration	Start	Finish	August	September	October	November	December	January	February	March	April	М	ay I	June		July	Augu	ust	September	Octo
	NdHe		Start	F1111511			1 8 15 22	29 5 12 19 2	6 3 10 17 24 31	7 14 21	28 4 11 18 25 4				20 27 3	10 17 2) ₁ 5 ₁ 12	19 26 2	16 16 9	
					1412	-10 -8	-6 -4	-2 1 3	5 7	9 11	13 15 1	17 19	21 23	25 27	29	31	33 35	37	39	41 43	45	47 4
1	WHOLE LIFE PROGRAMME Pre Construction Works	25w	06/08/12	08/02/13	1																	
					+						77											
2	Enabling Works	18w	15/10/12	01/03/13			2				+++++++++++++++++++++++++++++++++++++++	+								-		
	Construction Works - 60 Beds		04/03/13																			
4 5	RE-BUILD EXISTING BUILDINGS Internal wall removal/install steelwork (progressively floor by floor)	25w 3w	04/03/13 04/03/13	23/08/13 22/03/13							4											
6	Form / infill openings	5w	04/03/13	05/04/13							6											
7	Access scaffolding erected to exsting buildings Erect temporary roof over North Block	4w 4w	04/03/13 25/03/13	29/03/13 19/04/13							7	8										
													-									
9 10	North Block Structure Infill Construct foundations	22w 2w	25/03/13 25/03/13	23/08/13 05/04/13								9								-		
11	Underslab ducts and drainage inc sleeper walls	2w	01/04/13	12/04/13								11										
12 13	Lower ground slab Strip existing roof	1w 3w	15/04/13 22/04/13	19/04/13 10/05/13																		
14	Construct new floor	4w	13/05/13	07/06/13										14						-		
15	Roof carcassing and coverings inc RW goods	4w	10/06/13	05/07/13											1!	5						
16 17	Masonry works to roof level inc lift shaft / upper slabs / steelwork New windows and doors	8w 6w	17/06/13 15/07/13	09/08/13 23/08/13												16	17					
18	Scaffold strike date		23/08/13	23/08/13																18		
19	Key Date - Northern Block Watertight		23/08/13	23/08/13			+ $+$ $+$ $+$ $+$													19	+ +	+
20	South Block Structure Infill	16w	08/04/13	26/07/13									20									
21 22	Construct foundations Underslab ducts and drainage inc sleeper walls	2w 2w	08/04/13 15/04/13	19/04/13 26/04/13			+ $+$ $+$ $+$ $-$		+++				21			+			+		+	++
23	Lower ground slab	2w 1w	29/04/13	03/05/13										3								
24	Masonry works to roof level inc lift shaft / upper slabs / steelwork	8w	06/05/13	28/06/13										24		+ + +						+
25 26	Roof carcassing and coverings inc RW goods New windows and doors	4w 4w	01/07/13	26/07/13 26/07/13													25				+ $+$ $+$	+++
27	Scaffold strike date		26/07/13	26/07/13														27				
28	Key Date - South Block Watertight		26/07/13	26/07/13												+		28			+++	+
29		13w 2d	04/03/13	04/06/13							29											
30 31	West Extension Load out piling rig and excavator to LG area	7w 4d 2d	04/03/13 04/03/13	25/04/13 05/03/13						-	30			┥			+ +				+	++
32	B/O existing surfacing in pile locations (use extg for piling mat)	2a 1w	04/03/13	12/03/13																		
33	Piling works (1.75 / day)	2w 2w	08/03/13	21/03/13								33										+++
34 35	Trim and cap piles inc ground beams Underslab ducts and drainage works	2w 2w	22/03/13 29/03/13	04/04/13 11/04/13								34										+
36	S,R,&C lower ground slab	3w	05/04/13	25/04/13									36									
37	East Extension	11w 3d	15/03/13	04/06/13								37										+++
38	B/O existing surfacing in pile locations (use extg for piling mat)	1w	15/03/13	21/03/13								38 💻 🚺										
39 40	Piling works (1.75 / day) Trim and cap piles inc ground beams inc HD bolts	3w 3d 4w	22/03/13 03/04/13	16/04/13 14/05/13			+ $+$ $+$ $+$ $-$					39				+			+		+	+
41	Remove ramp	2w	24/04/13	07/05/13									41									
42		6w	17/04/13	28/05/13									42									
43	S,R,&C lower ground slab	6w	24/04/13	04/06/13									43									+++
44		27w 2d	26/04/13	04/11/13									44									
45 46	West Extension Steelwork to roof level inc floors	11w 4w	26/04/13 26/04/13	11/07/13 23/05/13									- 45 • 46	*								+++
47	Roof coverings inc RW goods	4w	24/05/13	20/06/13											47							
48 49	Masonry works inc access scaffolding Windows and doors	8w 2w	10/05/13 28/06/13	04/07/13										48			19					+
50	Scaffold strike date	211	11/07/13	11/07/13													50	5				
51	Key Date - West Extension Watertight		20/06/13	20/06/13												51					+	$++\mp$
52	East Extension	21w 4d	05/06/13	04/11/13											52							≟ + + +
53	steel frame to roof level inc floors	6w	05/06/13	16/07/13											53							\square
54 55	Roof coverings inc RW goods Masonry works inc access scaffolding	6w 10w 3d	17/07/13 14/08/13	27/08/13 25/10/13												+		54	55 🗖			
56	Windows and doors	5w	01/10/13	04/11/13																		56
57 58	Scaffold strike date Key Date - East Extension Watertight		04/11/13	04/11/13			+ $+$ $+$ $+$ $+$ $+$ $+$ $+$ $+$ $+$									+ $+$					+ $+$ $+$	58
59 60	SERVICES AND FINISHES SERVICES AND FINISHES - 47Nr (Main Blocks)	44w 42w 4d	08/04/13	21/02/14 13/02/14									60									
61	Advance services distribution	42W 40 11w	08/04/13	21/06/13									61									
					-14 -12		-6 -4	-2 1 3	5 7	9 11	13 15 1	17 19	21 23	25 27	29	31	33 35	37	39	41 43	45	47 4
Line	Name	Duration	Start	Finish	6 13 20			29 5 12 19 2	6 3 10 17 24 31	7 14 21	28 4 11 18 25 4	4 11 18 25	1 8 15 22	29 6 13	20 27 3	10 17 2	24 1 8	15 22 29) ¹ 5 ¹ 12	19 26 2	0 10 1	23 30 7 1
LING	INGILIE			1 11 1311	August	l September	October	November	December	January	February	March	April	М	ay I	June		July	Augu	ust I	September	. I Oct
Dest	- 4 Tal.						2012		aromm- Tal-								2013			<u></u>	0.05:1	000
Proje	ict Title: i2 - 54 Mount Pleasant, London								ogramme Title:		GRAMME							ogramme N			2-0519	· 002
For:					V		WHOLE LIFE PROGRAMME									ate Prepare	ed:	10/0	8/2012			
L	ondon Borough of Camden						WILLMOTT I HOUSIN										Re	ev.Commen	nt:	issue	e 2	
<u> </u>	ect ref LI:\Bids\SHEFEORD\2012 - Shefford Tenders\SH12-01								sant Camdon Hoste													

Project ref U:\Bids\SHEFFORD\2012 - Shefford Tenders\SH12-019 Mount Pleasant & Holmes Rd Hostels\02BIDS\PLANNING\ZK programme\lssue 7_Mount Pleasant, Camden Hostel_stage2_ZS rev 2.pp



								2012								13									
Line	Name	Duration	Start	Finish	August	l Septemb		ctober	November	December	January	February I	March	ı Ap		May		June	July		August		otember		
	Name			1111311		27 3 10 17	24 1 8	ן 29 _ا 22 _ا 15	5 12 19 1	26 3 10 17 24 31	7 14 21 28	4 11 18 25 4	11 18 25	1 8 1			1 27 3 1					.6 2 9	16 23	30 ₁ 7	
					-14 -12	-10 -8	-6	-4 -2	1	3 5 7	9 11	13 15 1	17 19	21 2	23 25	27	29 3	31 33	35 3	37 3 9	41	43	45	47	
62 63	Lift installation Plantroom installation	12w 14w	02/08/13 27/05/13	24/10/13 30/08/13										**		63				62			4w	A	
64	Key Date - Power on		27/09/13	27/09/13																			64	Et.	
65	Pre commissioning works	2w	22/11/13 06/12/13	05/12/13 13/02/14																			++-	\square	
66 67	Testing and commissioning works Services and finishes x 6 units	8w 13w	21/06/13	13/02/14														67			╞╤╤╋	<u> </u>	╞	\square	
68	Internal stud partitions	1w 3d	21/06/13	02/07/13														68							
69 70	Carpentry 1st fix - linings / noggins / patresses 1st fix electrical and plumbing	1w 2d 1w 2d	26/06/13 03/07/13	04/07/13														69					++-	\square	
71	Plasterboarding and plastering works	2w	12/07/13	25/07/13															71						
72	Pre-plumb - soil stack / bath / kitchen	2d	26/07/13	29/07/13																2				\square	
73	2nd fix carpentry inc kitchen installation 2nd fix services	2w 2w	26/07/13 26/07/13	08/08/13 08/08/13										**						3		++-	++-	\square	
75	Mist coat / wall tiling	2d	09/08/13	12/08/13																75					
76	Pre-paint inspection and snagging Final decorations	1w 1w	13/08/13 20/08/13	19/08/13 26/08/13																7	76		+	\square	
78	Final fix services and carpentry	3d	27/08/13	29/08/13																	78				
79	Floor coverings	3d	30/08/13	03/09/13																	7	79			
80 81	Snagging / clean / handover works Client snagging	1w	04/09/13	10/09/13 10/09/13																	+	80	++-	\square	
82	De snagging works	1w 2d	11/09/13	19/09/13																		82			
83	Client re-inspections		19/09/13	19/09/13																			83	\square	
84 85	Services and finishes x 6 units Services and finishes x 6 units	13w 13w	28/06/13 05/07/13	26/09/13 03/10/13														84	5			##	⊒		
86	Services and finishes x 6 units	13w	12/07/13	10/10/13															86			+++	 =		
87	Services and finishes x 6 units	13w	19/07/13	17/10/13															87						
88 89	Services and finishes x 6 units Services and finishes x 6 units	13w 13w	26/07/13 02/08/13	24/10/13 31/10/13										•••						82			—	—	
90	Services and finishes x 5 units	13w	09/08/13	07/11/13																90			-	Ħ	
91	Communal / stairs / clean / snag / de-snag	10w	13/09/13	21/11/13																		91			
92	SERVICES AND FINISHES - 13Nr (East Extension)	17w 4d	08/10/13	21/02/14	eeeeee									.			-							92	
93	Advance services distribution	6w	08/10/13	18/11/13																				93	
94 95	Services and finishes x 6 units Internal stud partitions	13w 1w 3d	29/10/13 29/10/13	10/02/14 07/11/13																	+		++-	\vdash	
96	Carpentry 1st fix - linings / noggins / patresses	1w 2d	01/11/13	11/11/13																				\square	
97	1st fix electrical and plumbing	1w 2d	08/11/13	18/11/13																					
98 99	Plasterboarding and plastering works Pre-plumb - soil stack / bath / kitchen	2w 2d	19/11/13 03/12/13	02/12/13																			+		
100	2nd fix carpentry inc kitchen installation	2w	03/12/13	16/12/13																					
101	2nd fix services	2w	03/12/13	16/12/13 18/12/13										**									++-	\vdash	
102 103	Mist coat / wall tiling Pre-paint inspection and snagging	2d 1w	17/12/13 19/12/13	08/01/14										••							+		++		
104	Final decorations	1w	09/01/14	15/01/14																					
105 106	Final fix services and carpentry Floor coverings	3d 3d	16/01/14 21/01/14	20/01/14 23/01/14																			++-		
100	Snagging / clean / handover works	1w	24/01/14	30/01/14																				\square	
108	Client snagging		30/01/14	30/01/14																					
109 110		1w 2d	31/01/14 10/02/14	10/02/14 10/02/14																			++-		
111	Services and finishes x 7 units	13w	05/11/13	17/02/14																					
112	Communal / stairs / clean / snag / de-snag	10w	02/12/13	21/02/14																			++-	\vdash	
113	EXTERNAL WORKS	19w	28/10/13	21/03/14		╺┥╍┿╍┝╸								-			╞┽╍┾	╺┝┥╸┽	╺┝┥╸┽		+	╺┿╍┿∊		peþ	
114	Remaining FW and SW drainage works inc connections / attenuation	8w	28/10/13	20/12/13																			<u> </u>		
115 116	Prepare levels and hardcore areas Paths, pavings and edgings	8w 8w	04/11/13	10/01/14 24/01/14																	+++	++	++-	\vdash	
117	External fixtures and fittings	8w	02/12/13	07/02/14																					
118	Dismantle hoist (as per the logistical layouts)	1w 4d	10/02/14	20/02/14									+									+	+	\vdash	
119 120	Landscaping works Remove all accommodation and make good areas	8w 2w	09/12/13 10/02/14	14/02/14 21/02/14									+++							+	++	++	++-	\vdash	
121	Test & Commission	4w	24/02/14	21/03/14																		\mp			
122	Project Completion		21/03/14	21/03/14																	┼┼╋	++	++-		
				21703/14	-14 -12	-10 -8	-6	4 2	1	3 5 7	9 11	13 15 1	7 19	21 2	23 25	27	29 3	31 33	35 3	37 39	41	43	45	47	
					6 13 20 2		· · · ·	15 22 29			7 14 21 28				15 22 29 6			0 17 24 1			12 19 2				
Line	Name	Duration	n Start	Finish	August	Septemb		ctober	November	December	January	February	March	Ap		May		June	July	200	August	1	otember		
					, iuguoi	ooptoind		2012		Provinibul	vanuary	· voiduly	marvit	Λ	•••	may		20							
	ados	I	1	1	1													20							
Codes Client General Services and Finishes Externals																_									
						Re	e build			Dem	olitions			Supe	erstructu	ire			Kev	Dates		I			
						I.C	, source			Dom	0110113			Capo					noy	20105					
Project Title:							Programme Title:									Programme No.: SH12-0519- 002									
	2 - 54 Mount Pleasant, London									WHOLE LIF							Date Prepared:								
For:	ondon Borough of Comdon						WILL		ON											10/08/2012					
"	London Borough of Camden							HOTT DIX											Rev.Con	Rev.Comment:			issue 2		

Project ref U:\Bids\SHEFFORD\2012 - Shefford Tenders\SH12-019 Mount Pleasant & Holmes Rd Hostels\02BIDS\PLANNING\ZK programme\lssue 7_Mount Pleasant, Camden Hostel_stage2_ZS rev 2.pp

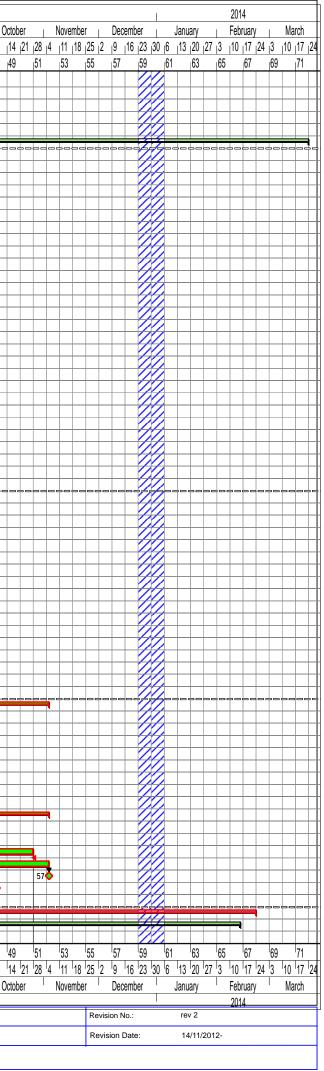
