


Asbestos contaminated soil in the ground and spoil

Time-line

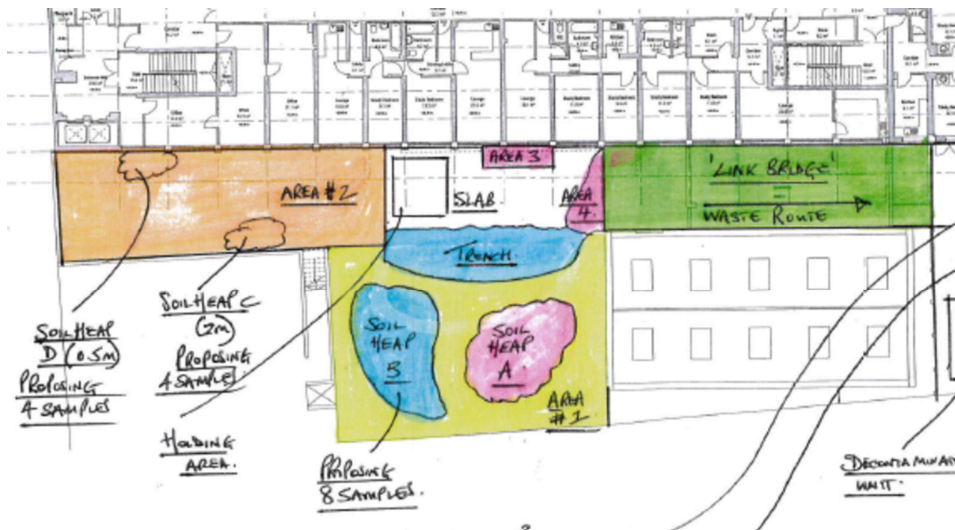

Asbestos Area 3

16/11/2016

Discovered suspected asbestos in the ground. Called and emailed Arcadis for direction

18/11/2016

AAWoods visited to investigate suspected asbestos in area 3. Took samples.

22/11/2016

Results from AAWoods - 4/5 samples positive with asbestos. Advised of 14day notification period may be required.

AAWoods prepared scope of works and cost

24/11/2016

Arcadis emailed Lucion for advise.

05/12/2016

AAWoods returned tender based on Lucion's scope of works and approved by Arcadis

Asbestos Area 1 - soil heap A

16/12/2016

4 samples taken by GreenSheilds

19/12/2016

Results from GreenSheilds

Asbestos Area 1 & 2 - soil heap B,C & D

20/12/2016

16 samples taken by AAWoods

GT put together action list moving forward and issued to Arcadis

GT advised that all groundworks to cease (treat spoil A as contaminated) and wait for Arcadis to confirm which company to remove spoil

GT requested Lucion to produce consultancy review of soil sampling and report with recommendations

AAWoods submitted scope of works and costs to remove spoil as contaminated waste

21/12/2016

GT sent copy of costs to Arcadis

GT sent copy of scope of works to Lucion to check validity and possible streamlining

Arcadis confirmed to go ahead with 16no samples

04/01/2017

Meeting between GT, Arcadis and Lucion to decide next move.

Sent results from AAWoods to Lucion

05/01/2017

Lucion emailed confirming that CAR2012 does not apply after studying results.

Asbestos in link bridge

23/11/2016

Sheilds attended to remove the asbestos in the ventilation room

Internal Asbestos

04/01/2017

Issued R&D report to Arcadis and requested for instruction to remove

09/01/2017

Received confirmation from Arcadis to proceed
