

Wind and Watertight Repairs

3 May 2023

Transworld Investments Ltd

<http://www.cubedltd.co.uk>

Project manager

Project dates

5 Jun 2023 - 7 Feb 2024

Completion

0%

Tasks

19

Resources


0

Roof and façade repairs
311 Gray's Inn Road
LONDON
WC1X 8PX


Tasks

Name	Begin date	End date
START ON SITE	05/06/2023	05/06/2023
Erect Scaffold Front	06/06/2023	15/06/2023
Erect Scaffold Side	16/06/2023	22/06/2023
Erect Scaffold Rear	23/06/2023	04/07/2023
Shroud to Scaffold	05/07/2023	05/07/2023
Structural inspection	06/07/2023	19/07/2023
Structural repairs, (TBC)	20/07/2023	02/08/2023
Parapet Caps	03/08/2023	30/08/2023
Parapet and roof top brickwork	31/08/2023	20/09/2023
Roof asphalt and tiling repair	21/09/2023	04/10/2023
Flat roofing	05/10/2023	11/10/2023
Repoint front ele	05/10/2023	08/11/2023
Repoint side ele	09/11/2023	13/12/2023
Repoint rear ele	14/12/2023	03/01/2024
Window overhaul	21/09/2023	08/11/2023
Window decoration	09/11/2023	03/01/2024
Snagging Cleaning	04/01/2024	24/01/2024
Strike scaffold and shroud	25/01/2024	05/02/2024
Completion	06/02/2024	06/02/2024

Gantt Chart

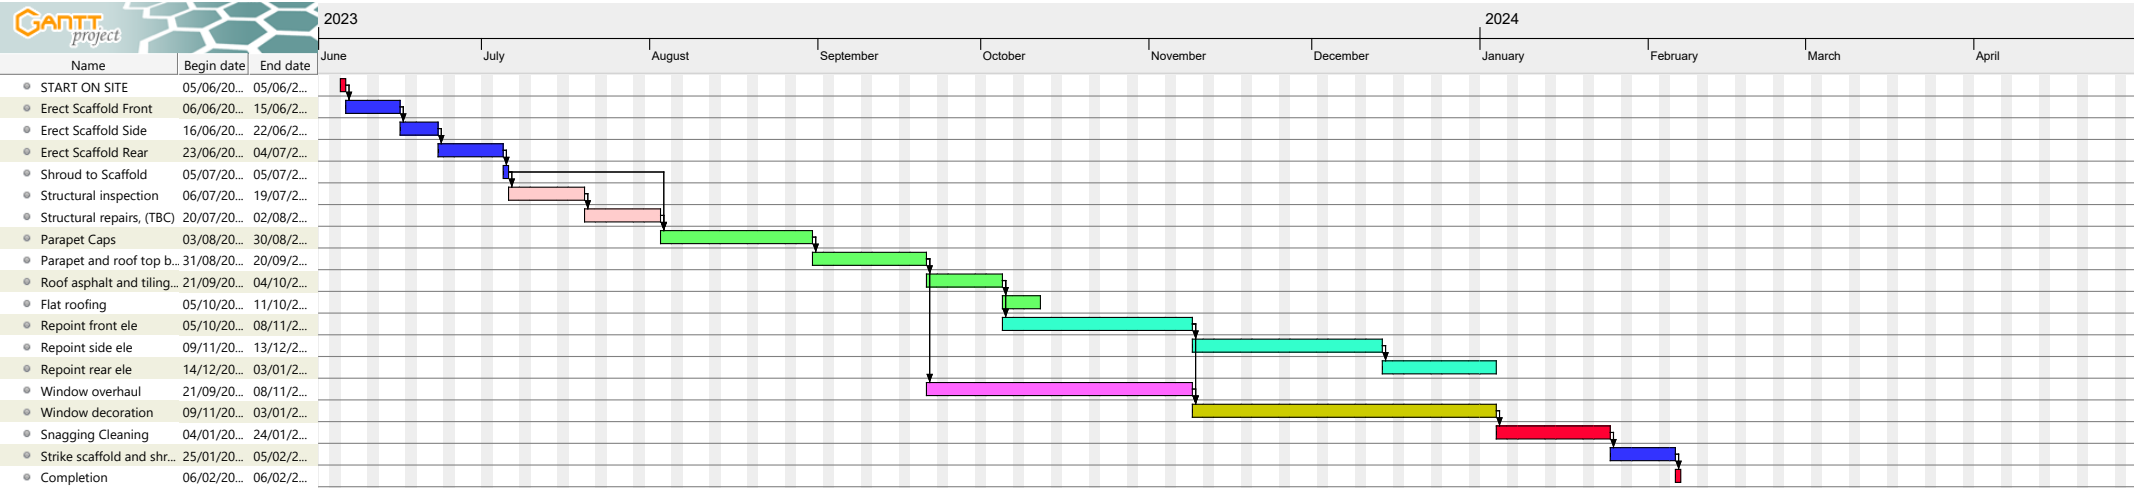

Resources Chart

		2023												2024			
Name	Default role	June	July	August	September	October	November	December	January	February	March	April					
