

Wind and Watertight Repairs

Transworld Investments Ltd

17 Nov 2023

<http://www.cubedltd.co.uk>


Project manager	
Project dates	13 Nov 2023 - 17 Jul 2024
Completion	0%
Tasks	19
Resources	0

Roof and façade repairs
311 Gray's Inn Road
LONDON
WC1X 8PX

Tasks

Name	Begin date	End date
START ON SITE	13/11/2023	13/11/2023
Erect Scaffold Front	14/11/2023	23/11/2023
Erect Scaffold Side	24/11/2023	30/11/2023
Erect Scaffold Rear	01/12/2023	12/12/2023
Shroud to Scaffold	13/12/2023	13/12/2023
Structural inspection	14/12/2023	27/12/2023
Structural repairs, (TBC)	28/12/2023	10/01/2024
Parapet Caps	11/01/2024	07/02/2024
Parapet and roof top brickwork	08/02/2024	28/02/2024
Roof asphalt and tiling repair	29/02/2024	13/03/2024
Flat roofing	14/03/2024	20/03/2024
Repoint front ele	14/03/2024	17/04/2024
Repoint side ele	18/04/2024	22/05/2024
Repoint rear ele	23/05/2024	12/06/2024
Window overhaul	29/02/2024	17/04/2024
Window decoration	18/04/2024	12/06/2024
Snagging Cleaning	13/06/2024	03/07/2024
Strike scaffold and shroud	04/07/2024	15/07/2024
Completion	16/07/2024	16/07/2024

Gantt Chart

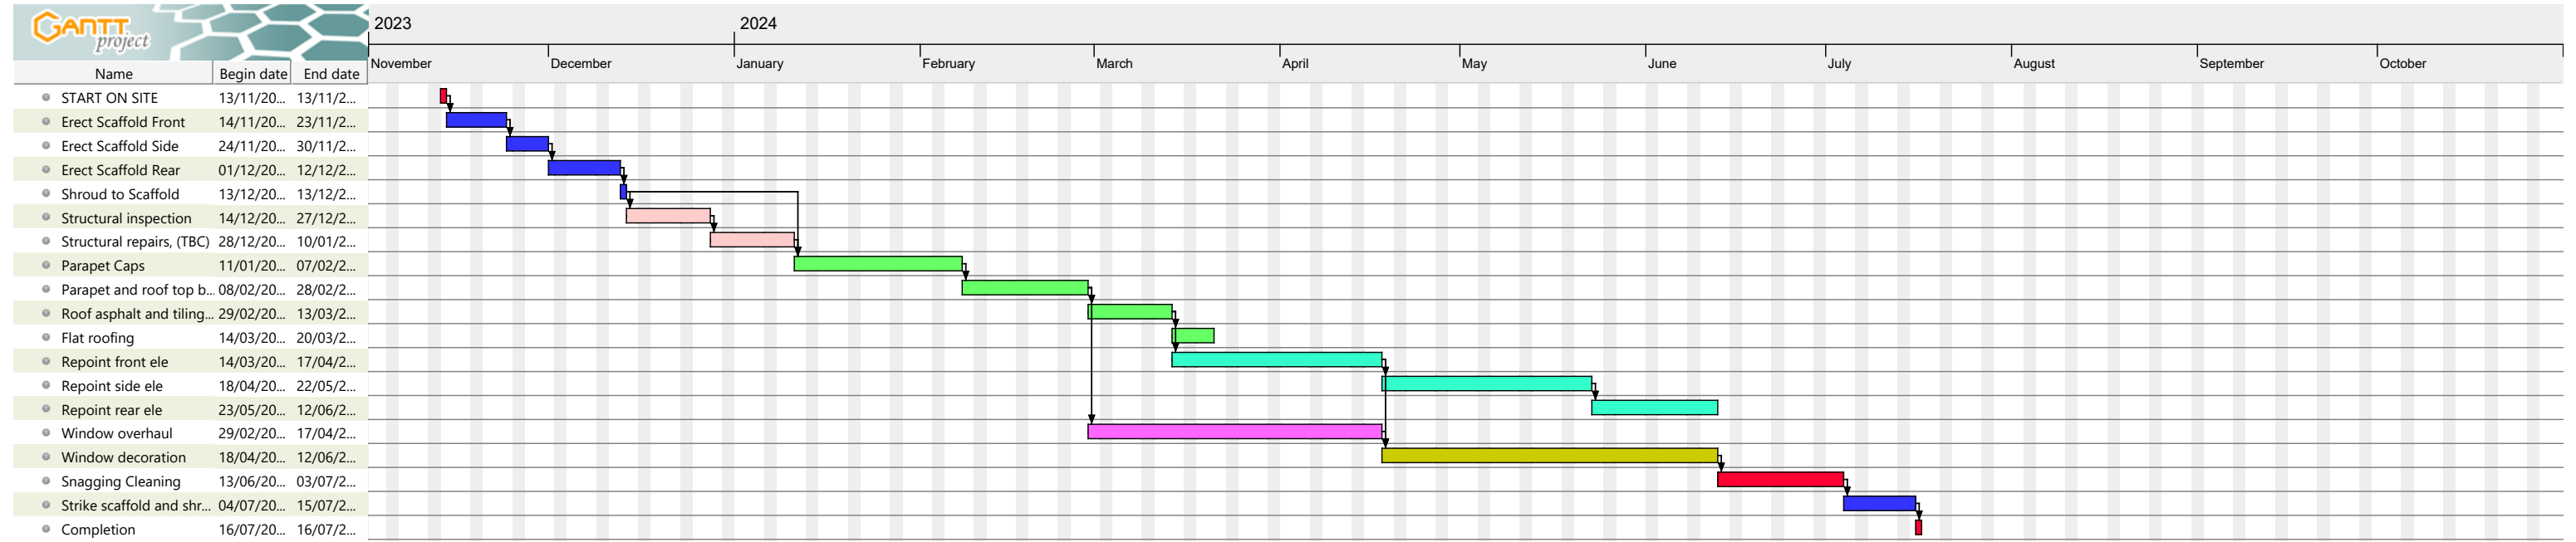

Resources Chart

		2023		2024									
Name	Default role	November	December	January	February	March	April	May	June	July	August	September	October
