

ALLARBORICULTURE

23 Southernhay Avenue, Bristol, BS8 4TJ

07375110399 | 0800 107 3652

e – info@allarboriculture.co.uk

ARBORICULTURAL IMPACT ASSESSMENT AND METHOD STATEMENT

BS5837:2012

On behalf of:
Rooms Outdoor
Flat A, 75 Belsize
Park Gardens,
London, NW3 4JP

Prepared by:
Kristian
Chesterman BSc
(Hons)

Report Reference:
AAAIA75BE

Report Date:
30th July 2024

Contents

Chapters	Content	Page no.
1.0	Instruction	3
2.0	Statement Of Purpose	3
3.0	Associated Documents	3
4.0	Site Description	3
5.0	Vegetation Description	3
6.0	Arboricultural Impact Assessment	4
7.0	Method Statement	6
Appendix 1	Tree Survey Schedule	
Appendix 2	Protection	
Appendix 3	Tree Protection Plan	

1.0 Instruction

All Arboriculture has been instructed by Rooms Outdoor to undertake a tree survey in accordance with BS5837:2012 *Trees In relation to design, demolition and construction – Recommendations*, and to produce an Arboricultural Impact Assessment, Arboricultural Method Statement and Tree Protection Plan. The instruction was received on the 17th July 2024. The tree survey was carried out on the 24th July 2024.

2.0 Statement of purpose

The purpose of this report is to provide local planning authorities with sufficient arboricultural information to consider the effect of the proposed development on nearby trees, and to demonstrate that trees have been carefully considered throughout the development process.

The report includes an arboricultural method statement that describes how work will be undertaken to provide adequate protection of retained trees.

3.0 Associated documents and drawings

This report should be read in conjunction with the following documents and drawings:

1. Planning Application Pack
2. British Standards Institute - BS5837:2012 *Trees in relation to design, demolition and construction – Recommendations*
3. Tree Protection Plan – AATPP75BE

4.0 Site description

The site is in the urban area of Belsize Park and is a ground floor flat. The proposal is the demolition of existing shed and the erection of a new garden room, decking and pergola. The site falls under the jurisdiction of Camden Council and a search on their website shows the site is within the Belsize Park conservation area but it was unclear if there are any Tree Preservation Orders on or close to the site.

5.0 Vegetation description

The vegetation consists of 1 category B tree and 1 category C tree. Some tree protection measures and working methodology (in accordance with BS 5837:2012) will ensure they are not detrimentally affected during construction.

6.0 Arboricultural impact assessment

Table 1: Summary of impacts	
Tree removal	None
Facilitation pruning	T2
Demolition within RPA	T1, T2
New surfacing within RPA	T1, T2
New structures within RPA	T1, T2

Building construction in relation to tree roots: No tree removal is required for the implementation of the proposed.

For the demolition, the existing shed will be demolished by hand / small machinery using the ‘top down, pull back’ method.

For the proposed garden room, hand dug concrete piles and ground beams will be used to avoid large roots with a diameter of 25mm or more in the event these are discovered. All works within and close to the RPA's of T1 and T2 will be carried out by hand and under arboricultural supervision. The pile locations can be excavated using an air spade to avoid undue damage with work halted if large roots (>25mm dia.) are discovered. Any exposed roots should be wrapped in Hessian and only pruned with the written consent of the LPA tree officer.

The same method will be used for the pergola and decking.

The utility trench as shown on the Tree Protection Plan will run close to the boundary wall. The trench will be carefully hand dug to a depth of 1m and width of 30cm. All works will be carried out under strict Arboricultural Supervision and any exposed roots will be wrapped in Hessian to prevent dessication.

Building construction in relation to tree crowns: The minor facilitation pruning T2 will be required to give adequate clearance of the proposed by crown lifting low branches as this tree has not been managed for some time.

A green roof for the proposed was considered but due to the shading of both T1 and T2, it would only be feasible if both trees were cyclically pruned and currently, this is not the case.

Tree root and canopy protection: The RPA (Root protection area) of the retained tree should be protected during the development phase with heras fencing and/or ground protection to ensure heavy machinery is not operated, or materials stored within the rooting area. This can be detrimental to the trees, causing soil compaction and root die back. The protection of the RPA and canopy spread is detailed in the Arboricultural Method Statement below.

Special surfacing: Special surfacing will not be required.

Materials delivery, storage and handling: Materials should not be handled or stored within the RPAs of retained trees; the load exerted can result in soil compaction and leachate from spills can be toxic to trees.

Surface drains, soakaways and services: It is important that services, surface drains and soakaways avoid the RPAs of retained trees as roots can be damaged during trench excavations. The location of services should therefore be agreed with the local planning authority prior to the development phase commencing.

7.0 Arboricultural method statement

Implementation and phasing of the proposed development: Prior to any building work commencing on site, a meeting will be held with the tree officer and site manager present. During the meeting details regarding the location of heras fencing and ground protection will be discussed and a time to reconvene in order to assess the heras fencing and ground protection will be agreed. The schedule of events during the development phase will be as follows:

Heras fencing will be installed as indicated in plan AATPP75BE.

During the development phase, the arboricultural consultant will be notified and asked to supervise any excavating within the RPA's of retained trees.

Tree protection barriers: Protective fencing will be installed prior to the commencement of any development activity and will be retained in the positions shown on the tree protection plan (AATPP75BE). The fencing will be to the BS 5837:2012 'Trees in relation to design, demolition and construction – recommendations' (section 6.2) i.e. preformed galvanised steel mesh panels ('Heras' or similar) facings on a driven braced scaffold pole framework. It will be retained at the locations shown until construction is completed. It may be moved or removed only with notice to and consent from the local planning authority.

Ground protection: Temporary ground protection to be installed within RPA of T1 and T2 should be capable of supporting pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile membrane.

Storage and handling of materials: This site has sufficient space for materials to be stored and handled.

Contractors parking: There is sufficient space on Belsize Park Gardens for parking.

Welfare facilities: Toilets and hand washing facilities shall be made available within the property.

Surface drains, soakaways and services: RPAs will be avoided in the drainage design however, in the unlikely event that existing cables need to be unearthed within an RPA, the method for doing so will accord with the recommendations in the NJUG Publication: Volume 4: Issue 2: 16/11/2007: Guidelines for the planning, installation and maintenance of utility apparatus in proximity to trees. Trenches will be dug by hand and any roots over 2.5cm in diameter will be retained undamaged. Smaller roots may be cut back to the proximal face with a clean, sharp pair of secateurs. The trench backfill around the roots shall be a granular material that can be compacted to the point where it can bear the new surfacing without subsiding but without abrasion of tree roots and without raising the soil bulk density to the point where root growth cannot take place. Should it be necessary, this operation will be overseen by the project arboriculturist.

Supervision: The project arborist will attend the site to inspect the heras fencing and ground protection and ensure that it has been laid out as prescribed in the method statement and meets the requirements of BS5837:12. Any excavations close to or within the RPA of retained trees will be overseen by the project arborist. It is the responsibility of the site manager to inform the arboricultural consultant when inspections are required for example, when heras fencing and ground protection is ready to be inspected.

Tree works: The minor facilitation pruning T2 will be required to give adequate clearance of the proposed. All tree work shall be carried out in accordance with BS 3998:2010 Tree Work – Recommendations by suitably qualified personnel.

Tree planting: It is respectfully suggested that if additional tree planting is required then this should be secured through an appropriately worded planning condition.

Sequencing of works

1. Carry out tree work operations. All tree works are to be carried out by a competent and experienced arborist to current British Standards.
2. Installation of Tree Protective Fencing and Ground protection as shown on the TPP.
3. Arboricultural Consultant to check Tree Protection at this stage.
4. Main construction phase
5. Remove tree protection when all construction activity has ended.
6. Carry out landscaping works if required.
7. Completion

Contacts

Architect and Agent:

Name:

Tel:

E:

Arboricultural Consultant:

Name: K Chesterman

Tel: 07375110399

E: info@allarboriculture.co.uk

APPENDIX 1 - Tree Schedule Schedule

Tree No	Species	Height (m)	Trunk Diameter (cm)	Crown spread (m)		Crown height above ground (m)	Life stage	General observations	BS 5837 cat	Root protection area (m)
1	Leyland Cypress <i>Cupressus × leylandii</i>	15	52	4	4	2	Early Mature	Previously reduced. Off site tree.	C	6.2
				4	4					
2	London Plane <i>Platanus × acerifolia</i>	22	110	6	6	5	Early Mature	Previouslt reduced. Ivy clad. Co dominant.	B	13.2
				6	6					

APPENDIX 1 - Tree Schedule Schedule

Survey Key

Diameter (mm)

Stem diameter in millimetres measured at 1.5m above ground level. Where the stem is divided below 1.5m, measurement is taken as directed by BS:5837 Annex

C. RPA - Root Protection Area

RPA circle radius is determined from Annex D of BS:5837. R- Radius

A – Area

Branch Spread (m)

Radial crown spread in metres, measured for each of the four cardinal points of the compass from the centre of the trunk. Low branches

N E
W S

Height above ground in metres of the lowest branch and use of the 4 cardinal points of the compass.

Age class

(NP) Newly planted – a tree within 3 years after planting

(Y) Young – a tree within its first one third of life expectancy

(EM) Early Mature – a tree within its second third of life expectancy

(M) Mature – a tree in its final one third of life expectancy

(OM) Over Mature – a tree having reached its maximum life span and is declining in health and size due to old age

(V) Veteran – a tree in the second or mature stage of its life and has important wildlife and habitat features including; hollowing or associated decay fungi, holes, wounds and large dead branches.

(A) Ancient – a tree in the ancient or third and final stage of their life that is of interest biologically, aesthetically or culturally because of its age, size and condition

Physiological Condition

GOOD – a tree in a healthy condition with no significant problems

FAIR – a tree generally in good health with some problems that can be remediated POOR – a tree in poor health with significant problems that can't be remediated DEAD – a tree without sufficient live material to sustain life

Structural Condition

An assessment of the structural/safe condition of the tree categorised into:

GOOD – a tree in a safe condition with no significant defects

FAIR – a tree in a safe condition at present but with defects or with significant defects that can be remediated POOR – a tree with significant defects that can't be remediated.

EC - Estimated remaining contribution in years (based on the species and its current condition)

<10 Up to 10 years

10+ 10 years or more

20+ 20 years or more

40+ 40 years or more

Category (Tree quality assessment)

Category U – Tree in poor condition that cannot realistically be retained for longer than

10 years Category A – Trees of high quality

Category B – Trees of moderate quality Category


C – Trees of low quality

APPENDIX 2 – Protective Fencing

Protective fencing should be erected before any construction commences on site. It should also be in position to protect important trees prior to demolition.

Protective fencing should stay in position until all construction activity has finished.


‘Fencing should be established at the minimum distance set out in British Standard 5837:2012 ‘Trees in relation to design, demolition and construction - Recommendations’. Excavations should not encroach into the fence position and it is appropriate to keep at least 0.5m between the fence and any changes in level.

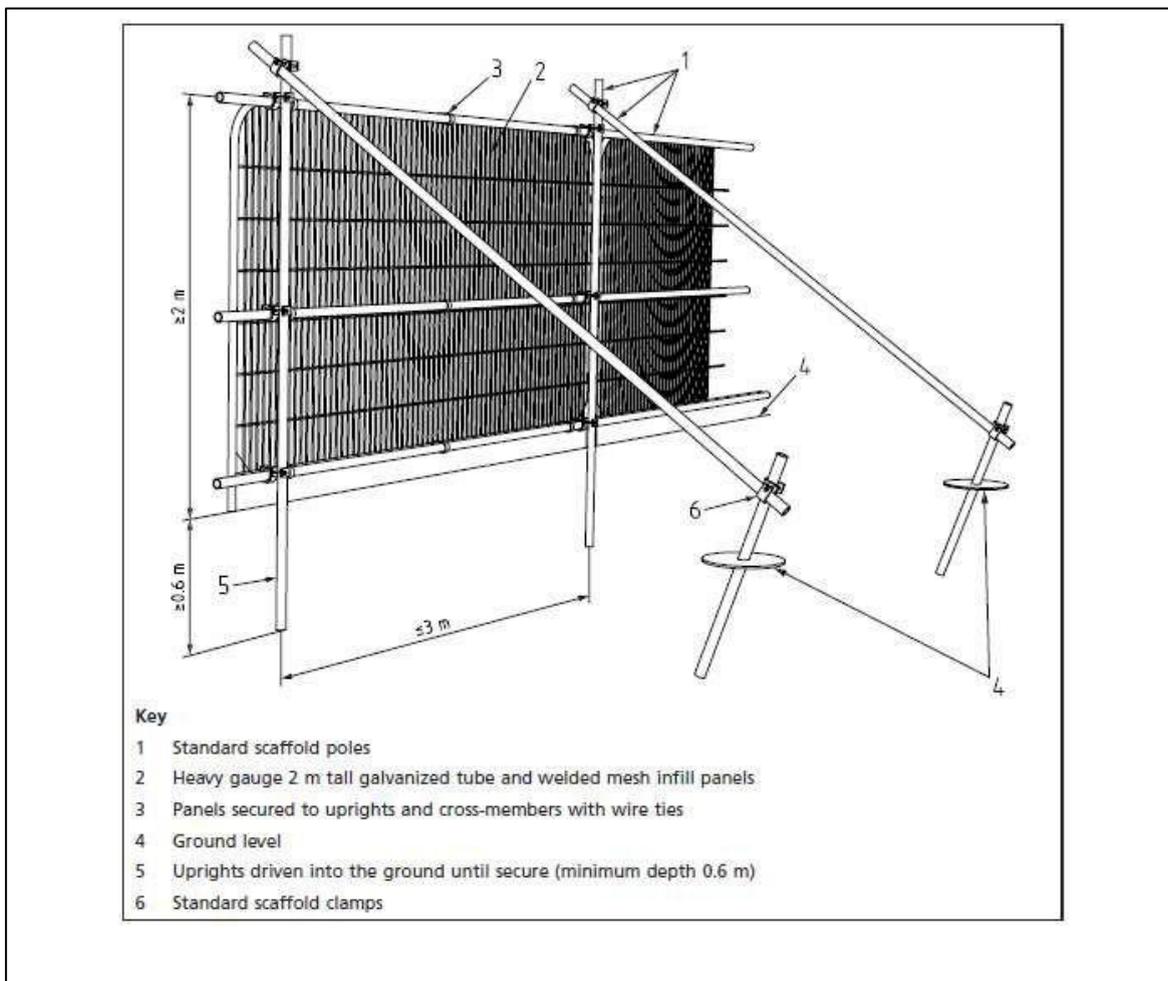

APPENDIX 2 – Ground Protection


Where ground protection measures are necessary, they can be provided by laying a geotextile mat onto the existing ground level and adding to this compressible materials, such as bark mulch or sharp sand to form a safe, level surface. Onto this surface is laid scaffold boards which become the working surface for the duration of the construction phase.

Where scaffolding is proposed above the area requiring protection the footway can be suspended above ground level using the upright scaffold poles onto which horizontal supports can be attached and then boards used to form the footway surface. A geotextile mat should be laid on the ground beneath to prevent contamination from materials dropped through the footway.

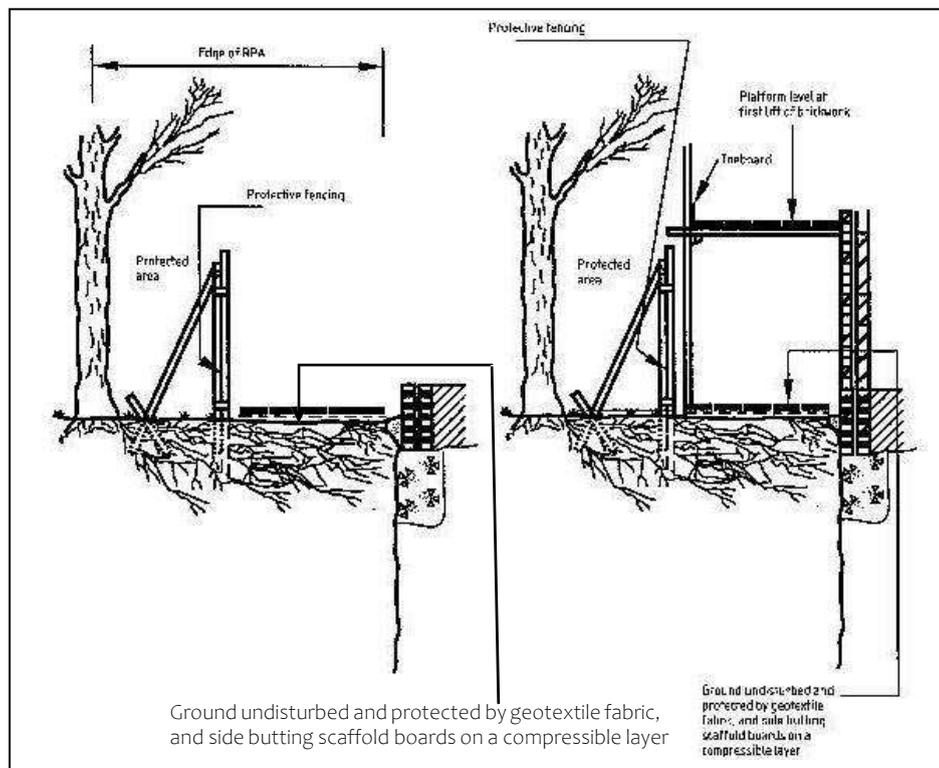

APPENDIX3–Tree Protection Plan

Protective fencing:
 Protective fencing should be erected before any construction commences on site. It should also be in position to protect important trees prior to demolition. Protective fencing should stay in position until all construction activity has finished.
 'Fencing should be established at the minimum distance set out in British Standard 5837:2012 'Trees in relation to design, demolition and construction - Recommendations'. Excavations should not encroach into the fence position and it is appropriate to keep at least 0.5m between the fence and any changes in level.

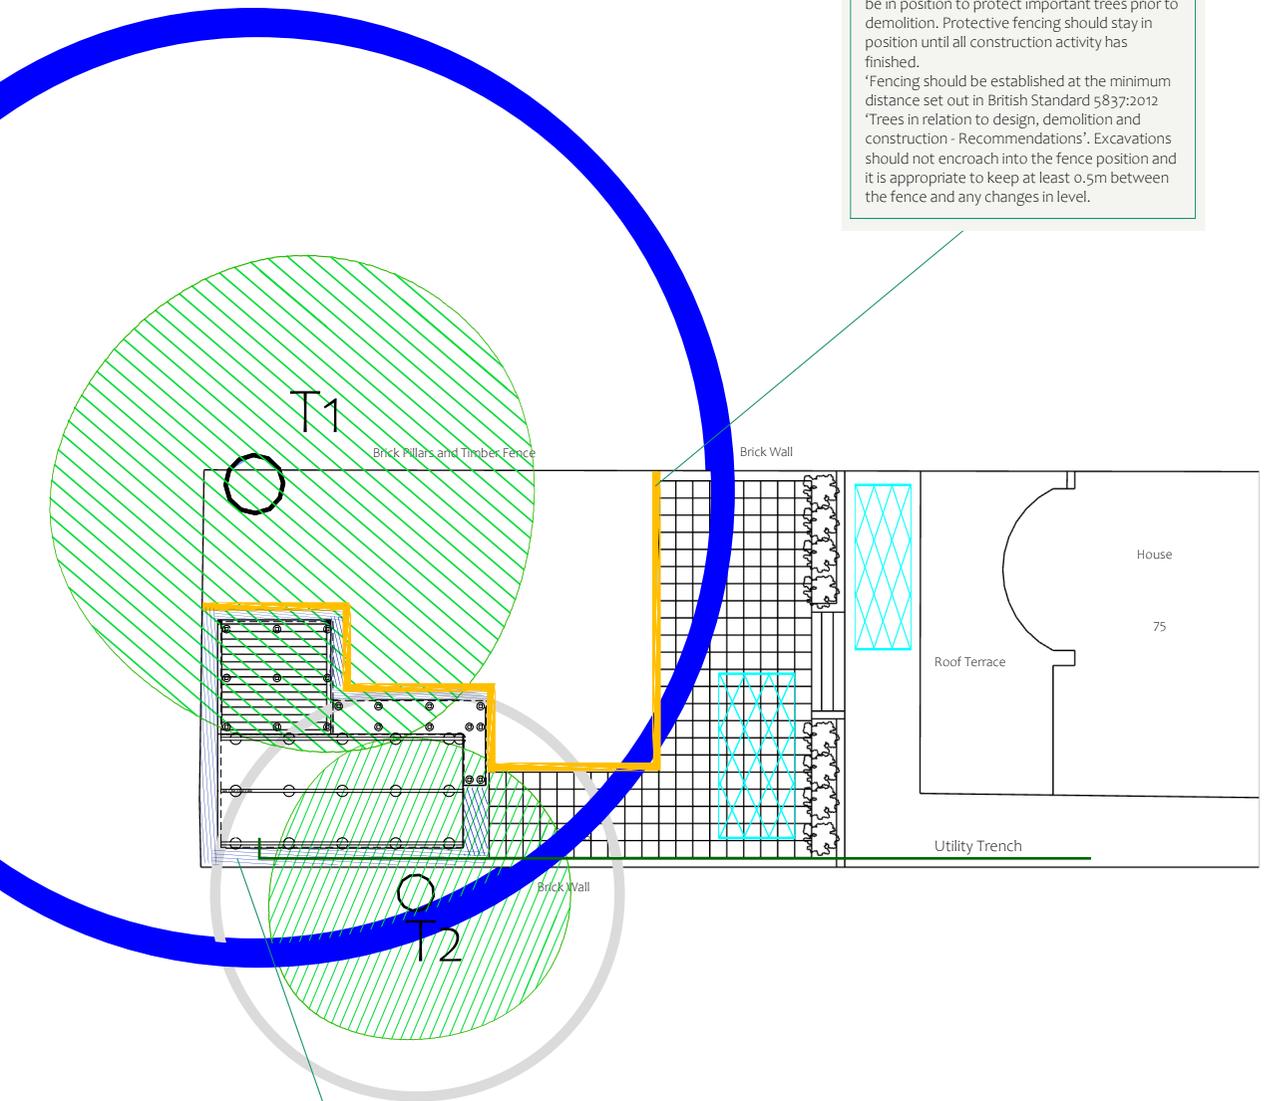

Ground protection:
 Temporary ground boarding capable of supporting pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, so as to form a suspended walkway, or on top of a compression resistant layer (e.g. 100 mm depth of woodchip), laid onto a geotextile membrane.

- RPA for Cat A* tree
- RPA for Cat B* tree
- RPA for Cat C* tree
- RPA for Cat U* tree
- ▨ Tree Canopy
- ▨ Material storage
- Heras Fencing
- ▨ Ground Protection




All Arboriculture
 23 Southernhay Avenue Bristol
 BS8 4TJ



Client: Rooms Outdoor
 Consultant: Kristian Chesterman

Site: Flat A, 75 Belsize Park Gardens,
 London, NW3 4JP

Title: Tree Protection Plan

Scale at A4	Date:	Document Ref.
1:200	30/07/2024	AATPP75BE
