

Inspection undertaken prior to any works commencing on site, and before any machinery brought on

to the site.

Adjacent to the tree roots located within 600mm from the finished ground level. No roots found within 2.5m of proposed extension.

An established protection area set out the tree. Which determined the root protection area. Cal was undertaken by measuring the stem diameter of a tree at 1.5 metres above ground level and of this radius from the centre of the tree. lculation to determine the root area multiply this by 12 and draw a circle

If root are found then Heras fencing on scaffolding poles around the protection zone, erected. as recommen ed in BS5837:2005, will be

Area outside tree root area to be hand dug within the identified protection retaining as many as possible. zone 0 f any tree and car around roots,

Only roots measuring less than 25mm in diameter shall be cut using sharp cutting/pruning tools whe leave as small a wound as possible. Any work to roots with a greater diameter requires consent fro en roots. Always a om the council. a clean cut

bue

All ground around tree will be reinstated any exposed tree roots with sand and reinstate tree pits Compaction around tree to be kept to a minimum in the immediate tree root area. with good quality top soil.

No excavating machinery shall be permitted within Otherwise dig only by hand.

Never cut roots over 25mm in diameter. the root protection zone. Trenchless <u>₹</u>

and the moving and use of heavy mechanical plant †o ţ be kept to

No storing of spoil or building material, including chemicals and fuel, near to trees

machinery shall be chained to the tree, no notices shall be nailed to their trunks or lean paving

REV

DATE

crown during construction a fence will be erected one metre out side of the cro spr bea. of the tree

The crown is measured from the centre or the stem in four directions; North, East, South and West

One metre on to each of the attained measurement which will give the minimum distance that protecat at to ensure the protection of the crown. fencing needs to be installed

olume the survival of

the Local Planning Authority. Signs should be

radius on Greenfield sites. o demonstrate the position of the tree

site

out correctly.

No works shall proceed until the appropriate Tree Protection Barriers

any retained tree.

materials

components, vehicles or structures shall be attached to or supported by the retained tree.

No mixing of cement or use of other materials or substances shall take place within displacement of those materials or substances could cause then to enter a RPA a RPA, 9 close enough to a RPA that · seepage 윽

SITE


London NW3 7PG


41 Ferncroft Avenue

Proposed Demolition of Exisitng erection of Single Dwelling with , Internal and External works.

Garge Associa

or variations to the approved works or tree protection schemes

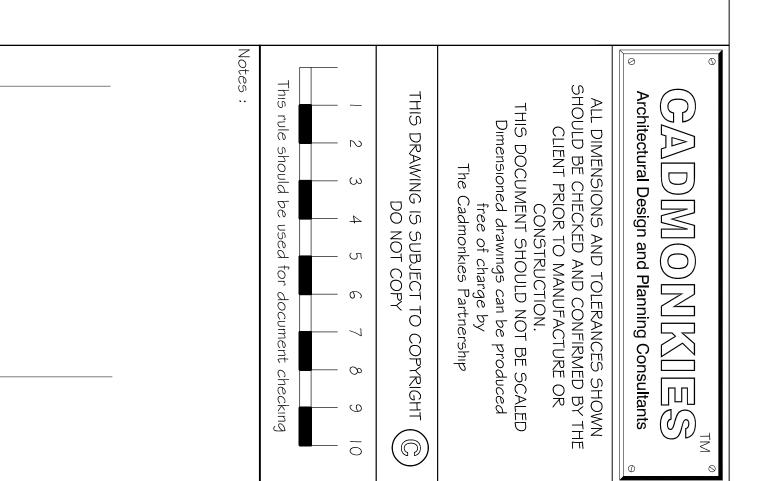

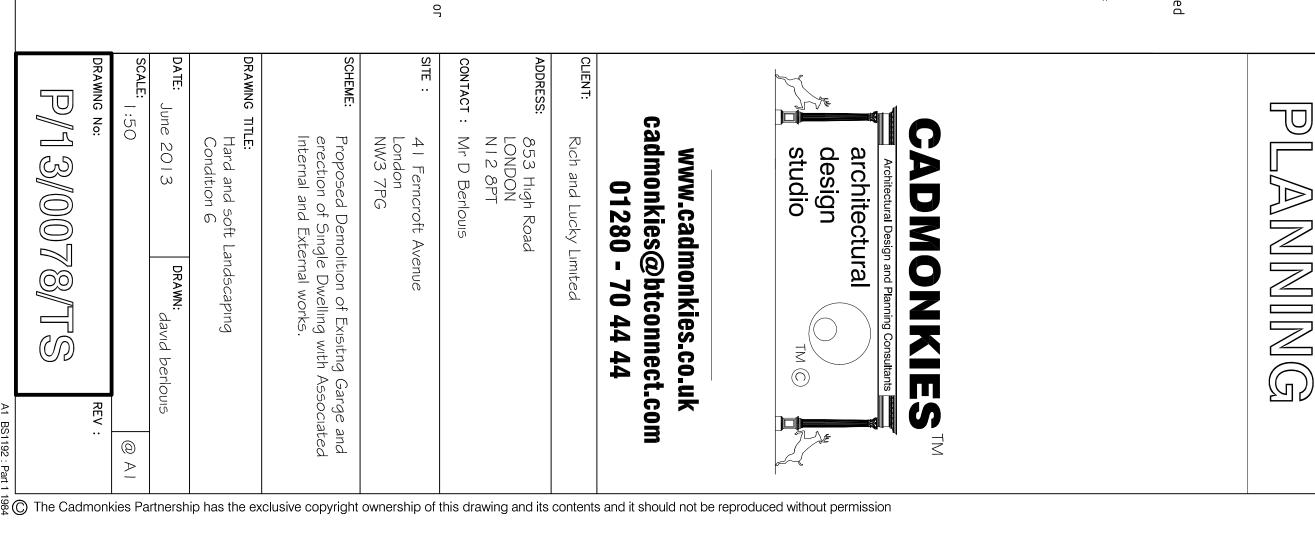

P/13/0078/

SCALE: 1:50

DATE:

June 2013

david berlouis

0

 \geq

DRAWING

© TILE:
Hard and soft Landscaping
Condition 6
