


Lift Pit Building 4, on 6 Erskine Road 12.03.15

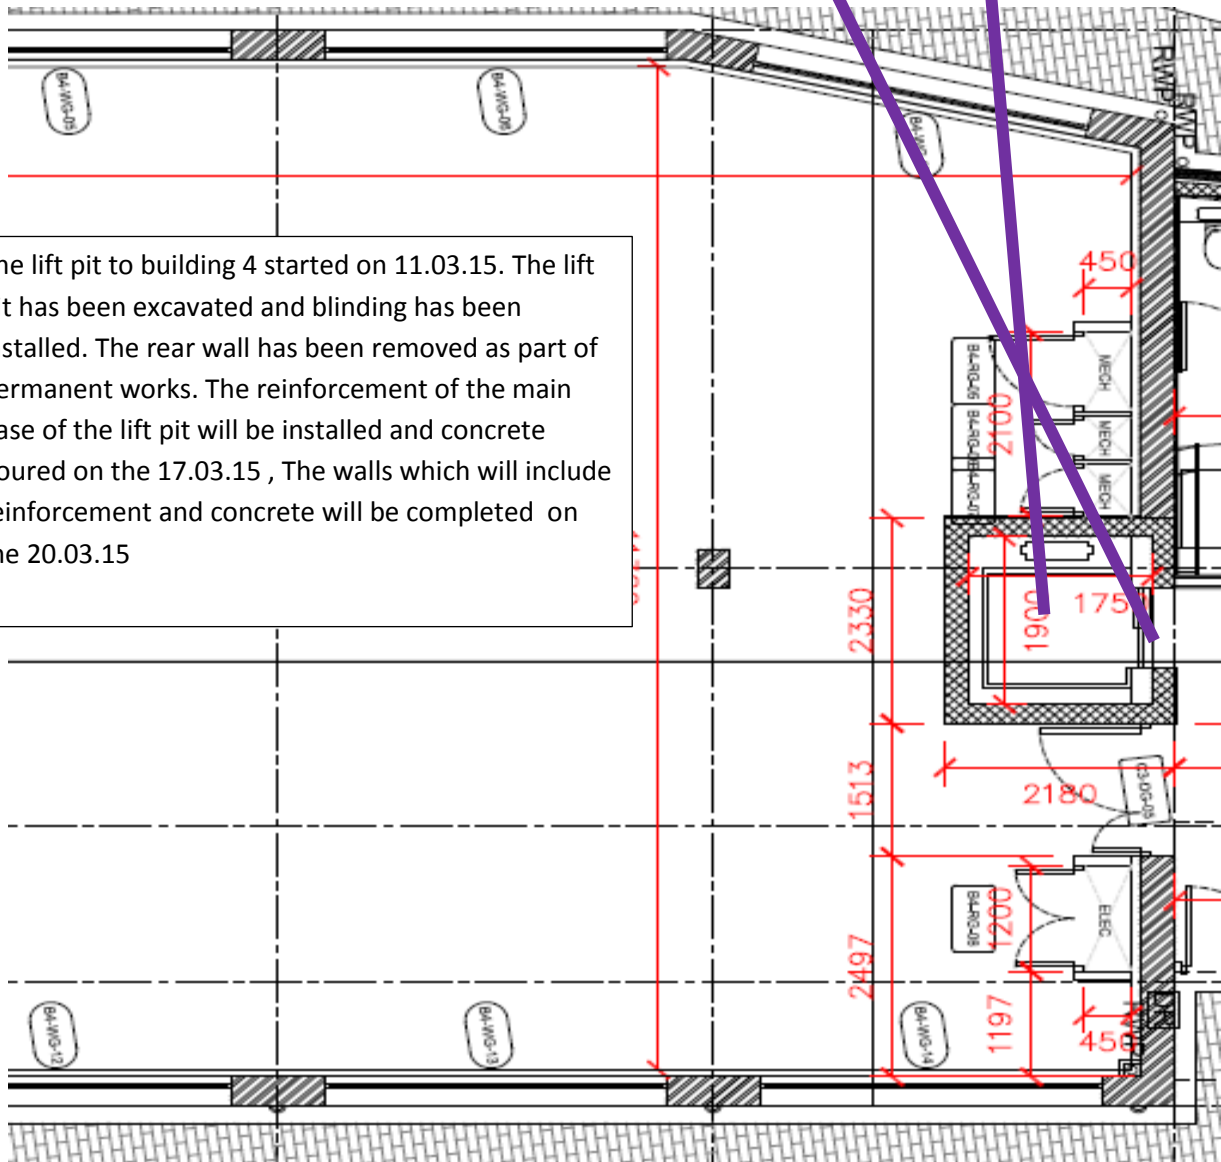

The lift pit to building 4 started on 11.03.15. The lift pit has been excavated and blinding has been installed. The rear wall has been removed as part of permanent works. The reinforcement of the main base of the lift pit will be installed and concrete poured on the 17.03.15 , The walls which will include reinforcement and concrete will be completed on the 20.03.15
