

Protective Fencing

To be erected prior to the commencement of all works on site, and retained in place throughout construction.

Default specification: To comprise either 2.4m wooden site hoarding; or a 2.3m high scaffolding framework comprising of vertical and horizontal framework, well braced to resist impacts, with uprights to be spaced at a maximum of 3.0m intervals and driven into the ground by a minimum of 600mm. On to this, standard anti-climb welded mesh panels are to be securely fixed to each other with at least two scaffold clamps and to the scaffold framework with wire.

Secondary Specification: To comprise of 2m tall welded mesh panels on rubber or concrete feet. Panels are to be joined together using a minimum of two anti-tamper couplers, installed so that they can only be removed from inside the fence. The panels should be supported on the inner side by stabilizer struts, which should be attached to a base plate and secured with ground pins.

All weather notices should be erected at regular intervals on the weld mesh panels with words such as "Construction exclusion zone - Keep out".

Tree Protection Area

KEEP OUT

Do not move this fence

(TOWN & COUNTRY PLANNING ACT 1990)
TREES ENCLOSED BY THIS FENCE ARE PROTECTED BY PLANNING CONDITIONS AND/OR ARE THE SUBJECT OF A TREE PRESERVATION ORDER.
CONTRAVENTION OF A TREE PRESERVATION ORDER MAY LEAD TO CRIMINAL PROSECUTION

ANY INCURSION INTO THE PROTECTED AREA MUST BE WITH THE WRITTEN PERMISSION OF THE LOCAL PLANNING AUTHORITY



ARBTECH
Arbtech Consulting Limited
Unit 3, Well House Barns, Chester, CH4 0DH
01244 660558
www.arbtech.co.uk

Trunk Protection

Protective trunk Wrapping:
To be attached to the trunks of retained trees prior to the commencement of all works on site, and retained in place throughout construction. To comprise of a minimum of three wrappings of clean dry hessian around the trunk from ground level up to 2.3m high and held in place using sisal. Onto the hessian a minimum of three wraps of chestnut palling and is to be held in place by 2.50mm mild steel galvanized wire in three locations and fixed into place using fencing staples fixed into the chestnut palling.

Protective hoarding:
To be erected prior to the commencement of all works on site, and retained in place throughout construction. To comprise of 2.4m wooden site hoarding constructed upon a timber frame work situated around the outside of the planting pit. Where the timber frame is constructed around the tree trunk a minimum of 4 layers of clean dry hessian is to be wrapped around the trunk to protect the bark.

All weather notices should be erected at regular intervals on the weld mesh panels with words such as "Construction exclusion zone - Keep out".

Ground boarding

New temporary ground protection should be capable of supporting any traffic entering or using the site without being distorted or causing compaction of underlying soil.

Note The ground protection might comprise one of the following:

- for pedestrian movements only, a single thickness of scaffold boards placed either on top of a driven scaffold frame, as to form a suspended walkway, or on top of a compression-resistant layer (e.g. 100mm depth of woodchip), laid onto a geotextile membrane;
- for pedestrian-operated plant up to a gross weight of 2t, proprietary inter-linked ground protection boards placed on top of a compression-resistant layer (e.g. 150mm depth of woodchip), laid onto a geotextile membrane;
- for wheeled or tracked construction traffic exceeding 21 gross weight, an alternative system (e.g. proprietary system or pre-cast reinforced concrete slabs) to an engineering specification designed in conjunction with arboricultural advice, to accommodate the likely loading to which it will be subjected.

Manual Excavation

Excavation within the RPAs will be initially undertaken by hand under direct on-site arboricultural supervision to a minimum of 600mm deep of any excavation, whether for proposed foundations, hard surfacing or underground services. The soil is to be loosened with the use of a fork or pick and then cleared with the aid of an air-spade and air-vac. All roots to be cut out will be clearly severed with the use of a hand saw or secateurs. The edge of the excavation closest to the retained trees will be covered over with damp hessian to prevent drying out, and where necessary be shuttered to prevent soil collapse or contamination by concrete. If appropriate soil beneath the depth 600mm may be sheet piled, regular piles or individual piles. Any deeper excavations may be undertaken by a machine provided it works from outside the RPA or has appropriate ground protection in place to move and work upon.


Arboricultural Supervision

The arboricultural consultant will be required to attend site to directly supervise all demolition and construction works that have to be undertaken within the root protection areas. This will include:

- Pre-commencement site meeting.
- Location of protective measures.
- Manual excavation of service trench and fence posts within RPAs of tree nos.3 and 4.
- Installation of 'No Dig' hard surfacing.
- Any excavations within or adjacent to RPAs, including foundations, hard surfacing or underground services.
- Removal of protective measures and arboricultural sign off.

Arboricultural Method Statement

Please refer to Arbtech Consulting Ltd. Tree Schedule and Arboricultural Method Statement, for full details on all surveyed trees and how all aspects of the the development may be implemented without detriment to retained trees.

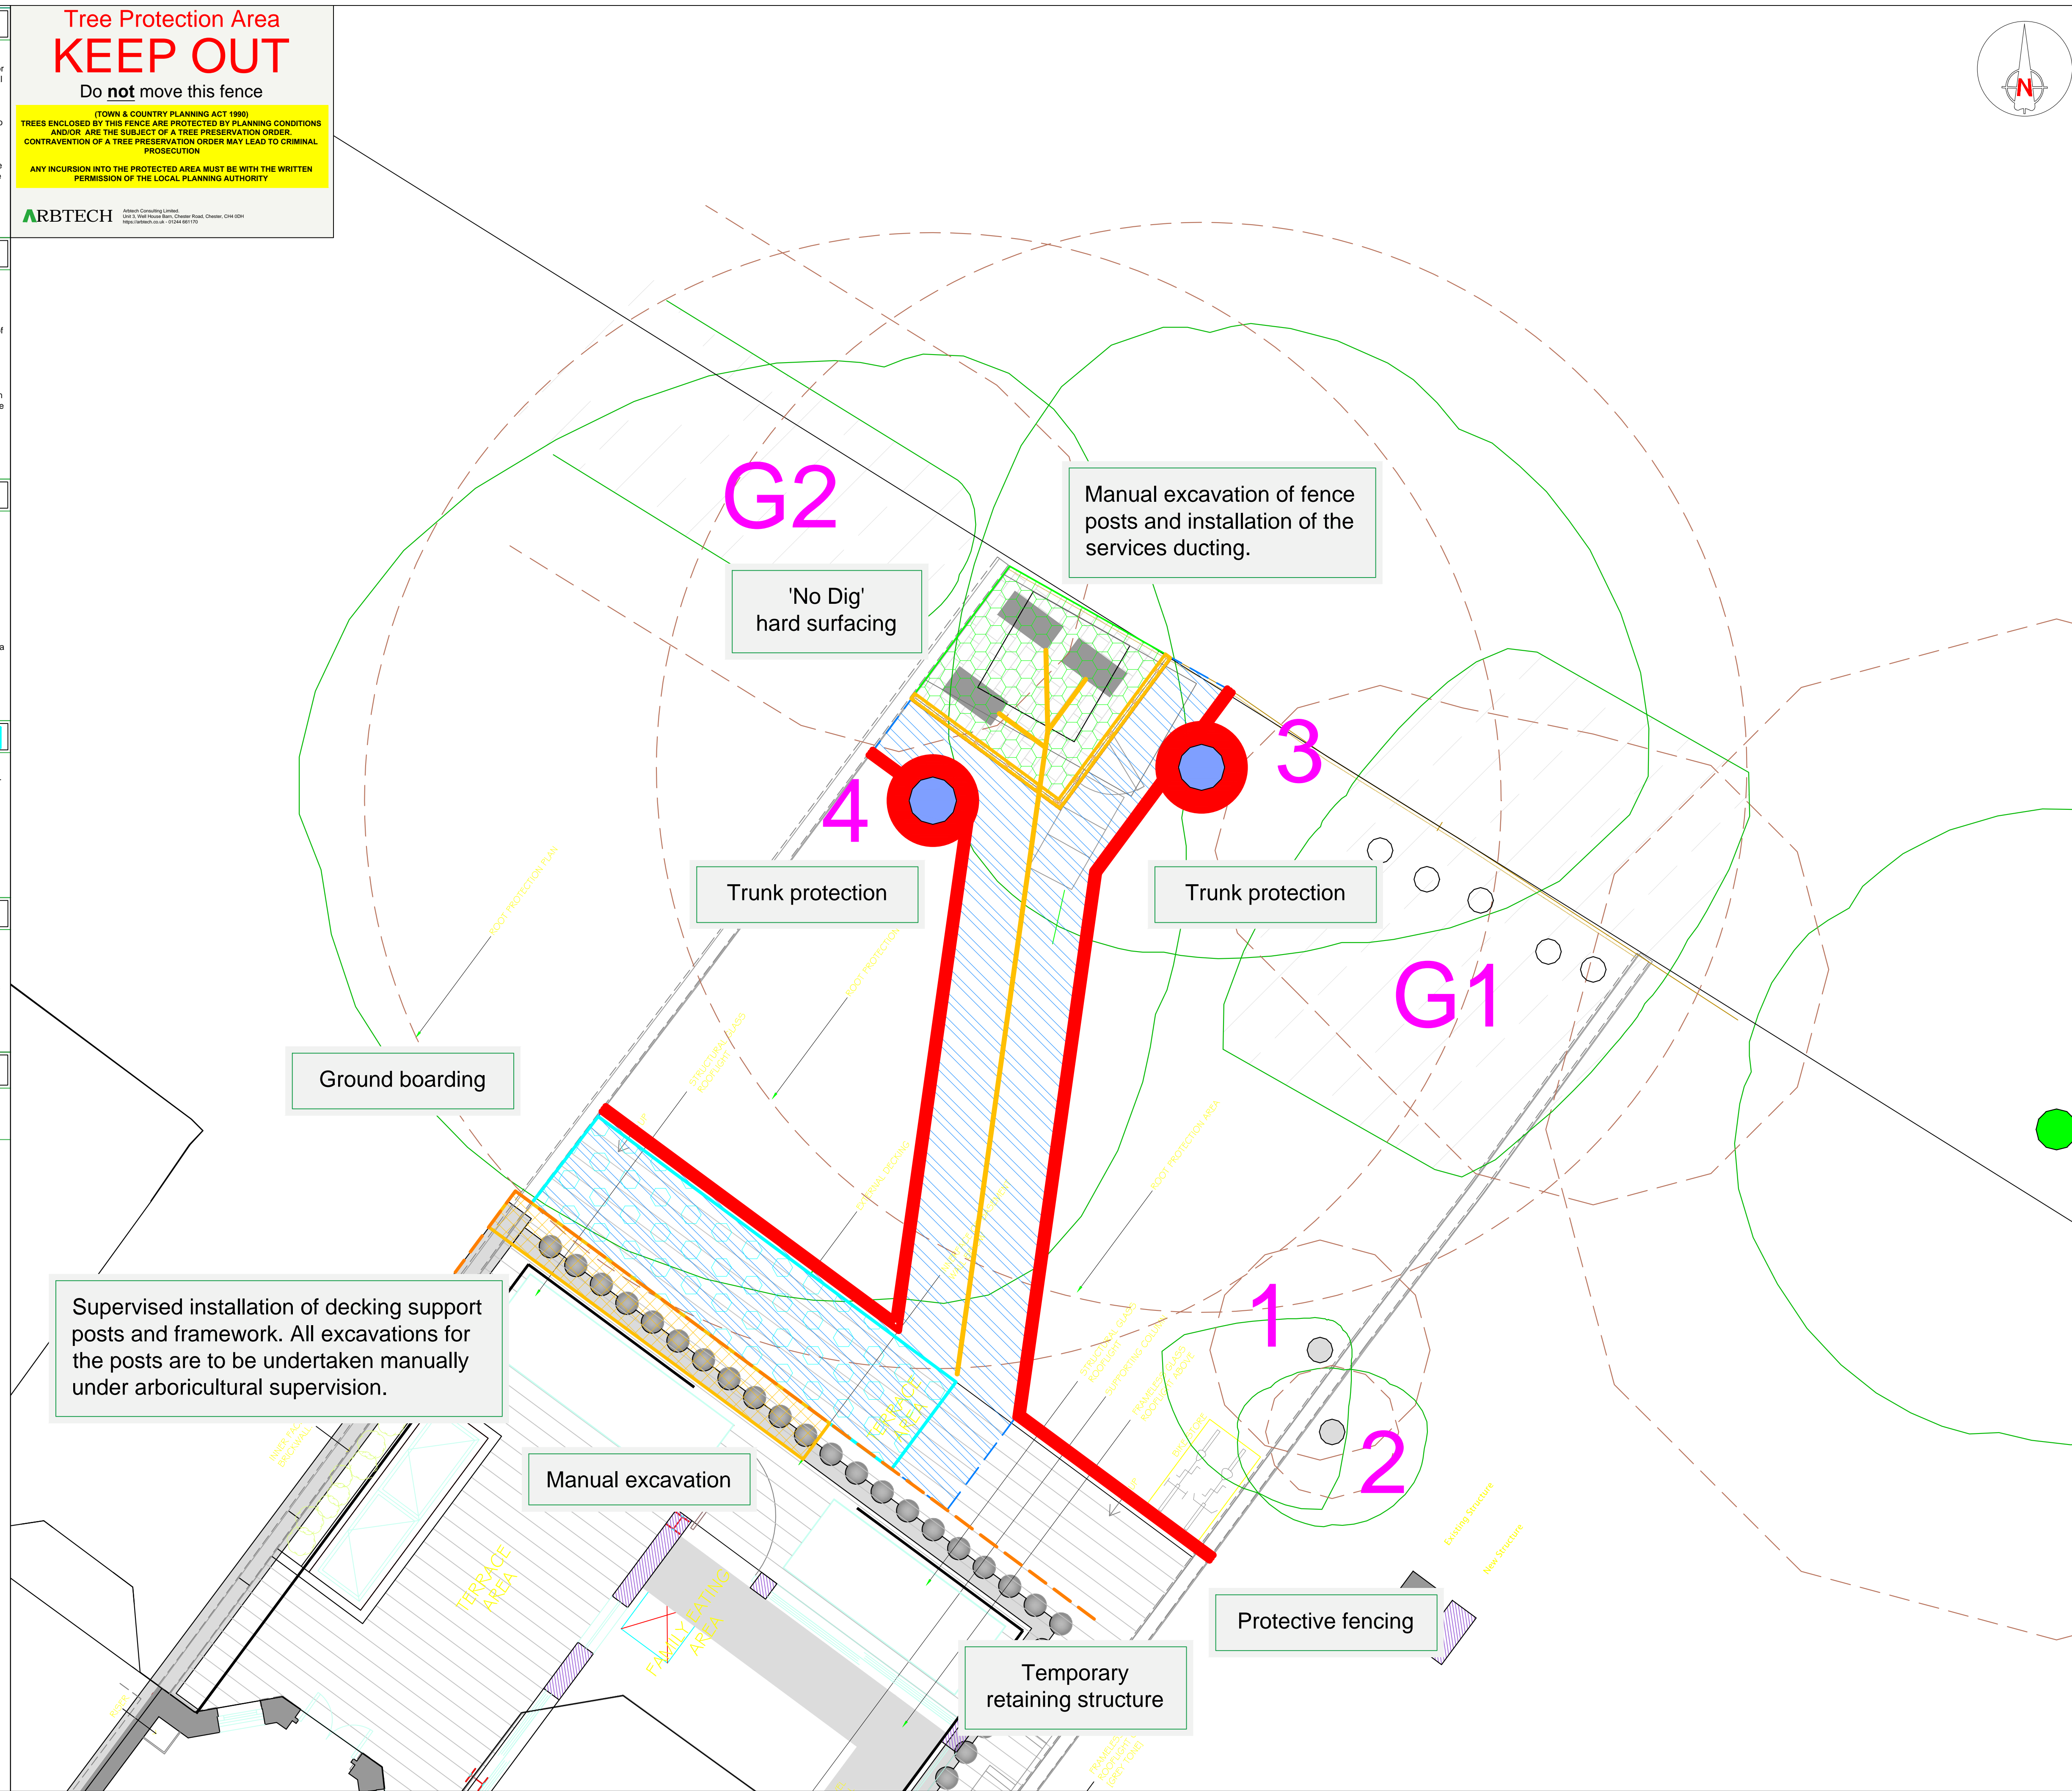

Unit 3, Well House Barns, Chester, CH4 0DH
www.arbtech.co.uk, email@arbtech.co.uk, 01244 660558

Project:

55 Lancaster Grove,
London,
NW3 4HB.

Client:

Mr and Mrs Etingen

Drawing:

Tree Protection Plan

Based on:

FIS_011 B; 8412/009 & FIS_41 A

Drawing No:

Arbtech TPP 02

Rev:

Mar 2016

Scale:

1:50 @ A0

Drawn:

MGM

Key:

Tree Nos.:	1	Tree Canopies:		Trunks:	
RPAs:		Category 'A' trees:		Category 'B' trees:	
Protective fencing:		Ground boarding:		Trunk protection:	
Temporary retaining system:		Manual excavation:		Supervised installation of decking:	
No Dig hard surfacing:					

All dimensions should be checked on site. No dimensions are to be scaled from the drawing. Please notify us of any discrepancies before. Arbtech Consulting Ltd. cannot be held responsible for inaccuracies in the base drawing in which this plan is based. This drawing is designed to reflect the principles of the layout or design only, and relates only to the protection of individual trees. This drawing is not to be read as a definitive part of the engineering or construction design or method statement. An architect or structural engineer should be consulted over any matters of construction, detailing or specification for any standards or regulatory requirements relating to proposed structures, hard surfacing or underground services. This drawing was produced in colour - a monochrome copy should not be relied upon. © Arbtech Consulting Ltd. 2013
