



STAGE 0
SCALE
1/100

CHECK EXISTING GROUND CONDITIONS BEFORE COMMENCING ANY TEMPORARY WORKS. DEMOLISH THE EXISTING GROUND FLOOR SLAB CAREFULLY IN ACCORDANCE WITH THE CONTRACTORS METHOD STATEMENT

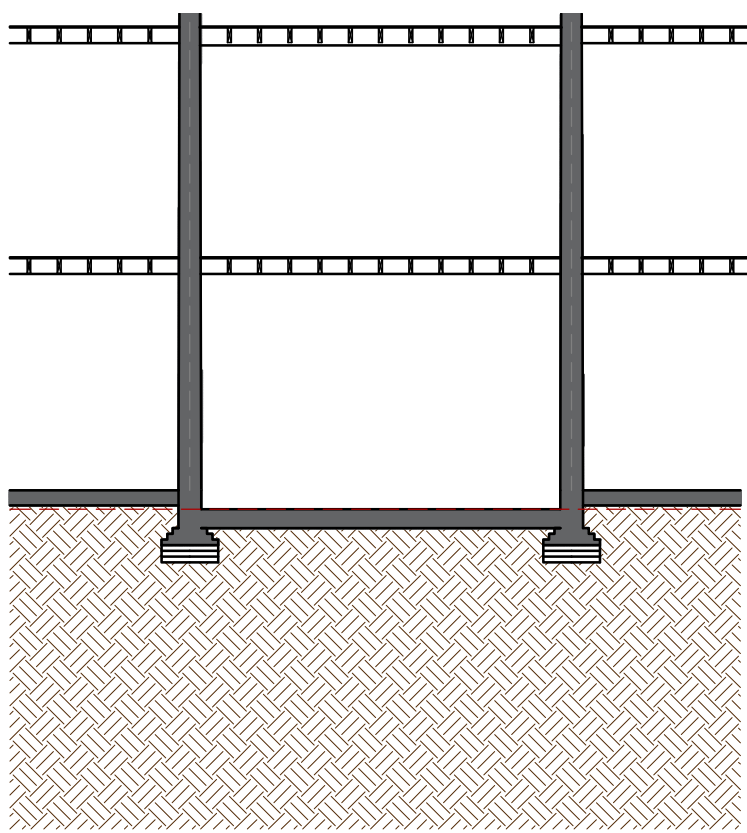


STAGE 1
SCALE
1/100

EXCAVATE THE REQUIRED PINS AS PER SEQUENCE SHOWN ON DRAWINGS STRU1001, USING TRENCH SHEETS AND ACROW PROPS TO SUPPORT SIDES OF THE EXCAVATION AGAINST THE CENTRAL SOIL MASS TO RESIST SLIDING FORCES.

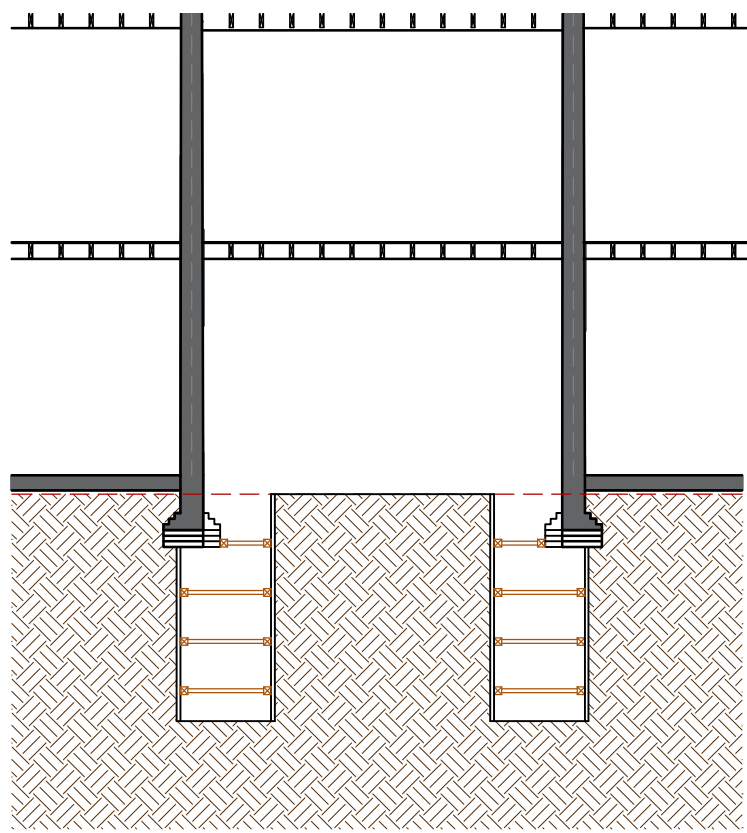


STAGE 2
SCALE
1/100

INSTALL THE REINFORCEMENT INCLUDING DOWEL BARS USING THE SPACERS AND TIE WIRES AS PER THE STRUCTURAL ENGINEERS DRAWINGS AND CALCULATIONS. CAST THE REINFORCED CONCRETE BASE.

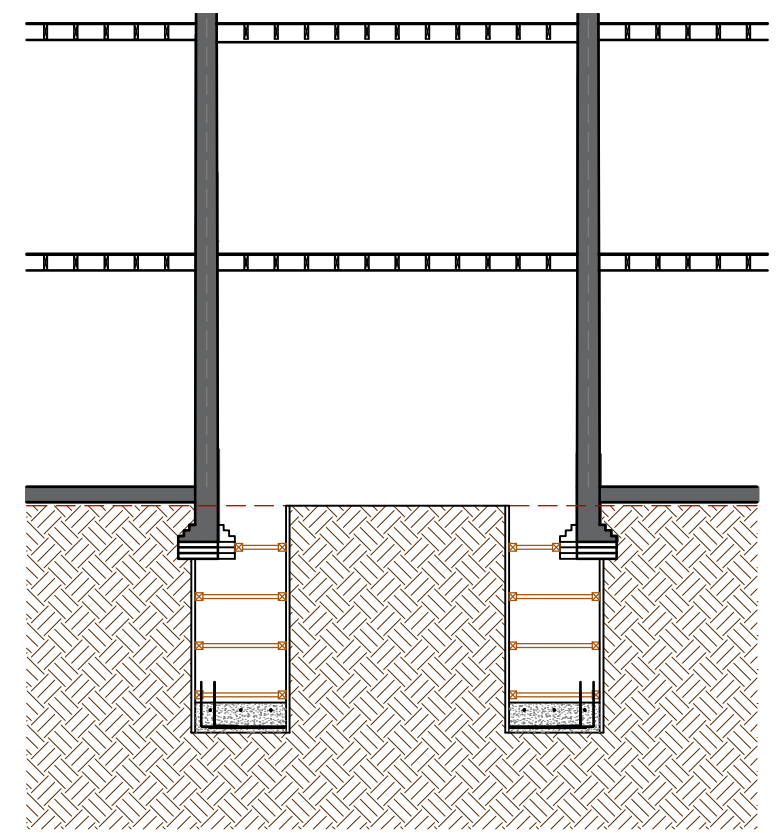


STAGE 3
SCALE
1/100

ERECT THE SHUTTER FOR THE STEM READY FOR CONCRETING AND CAST THE CONCRETE.

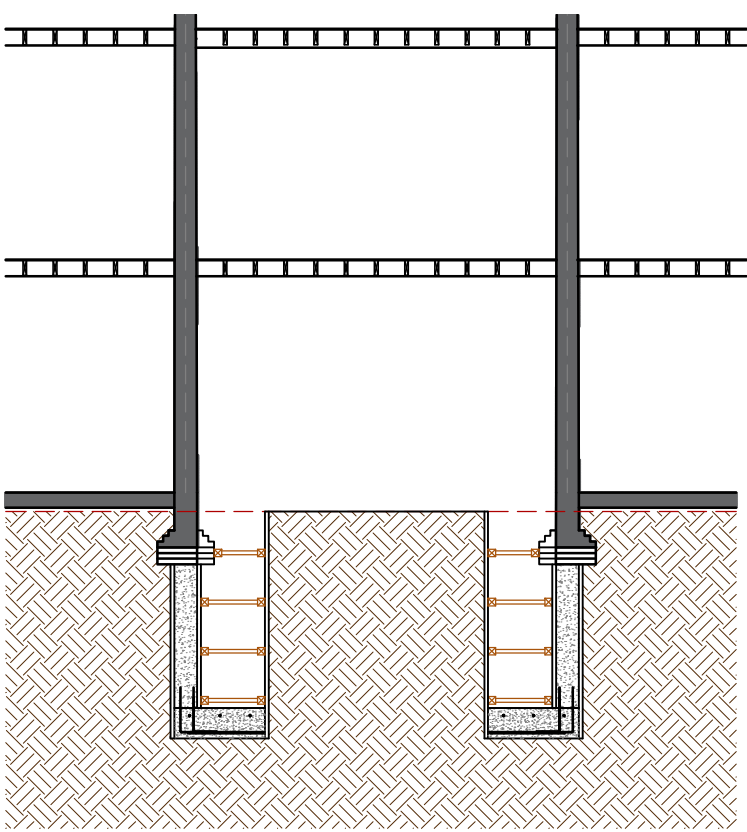


STAGE 4
SCALE
1/100

FOLLOW STAGES 1 TO 3 FOR COMPLETION OF ALL THE PINS. PROP UNDERPINNING USING A JACKING BEAM SYSTEM BY 'MAYBEY' OR SIMILAR APPROVED IF REQUIRED BY THE TEMPORARY WORKS DESIGN. EXCAVATE THE CENTRAL BERM TO FORMATION LEVEL TO THE REQUIRED LEVELS.

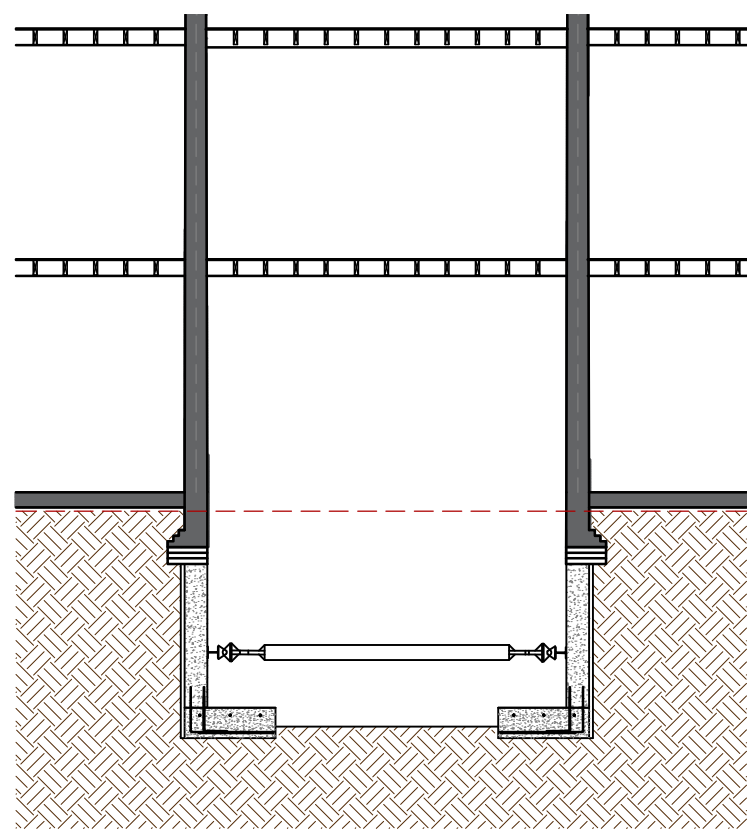


STAGE 5
SCALE
1/100

CAST THE BASEMENT SLAB, LET THE CONCRETE CURE AND THEN REMOVE THE TEMPORARY PROPS.

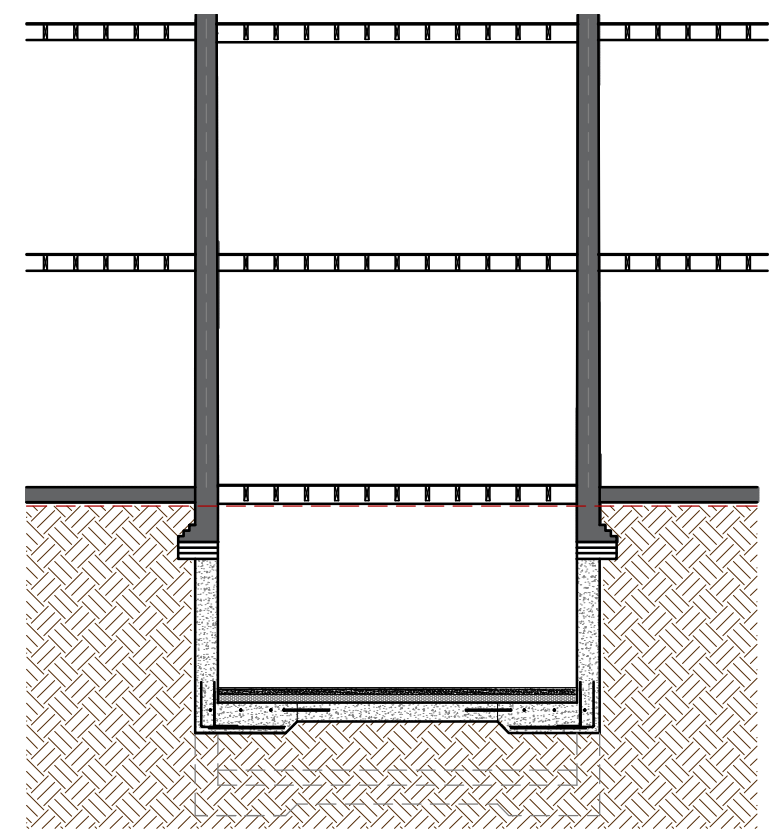

DISCIPLINES: ARCHITECTURAL STRUCTURAL CIVIL MECHANICAL ELECTRICAL LANDSCAPE

CONTRACTOR :



FRIDUM LTD
Design + Build and Structural
Engineering Consultants

T : 020 8090 4802
E : info@fridum.com
W : www.fridum.co.uk
Brentano House, Unit 5
The Exchange, Brent
Cross Gardens,
London, NW4 3RJ

DRAWING STATUS :	FOR APPROVAL
CLIENT NAME :	MR. MATT GODFREY
PROJECT TITLE :	EXTENSION AND ALTERATIONS AT 76 FLEET ROAD - LONDON- NW3 2QT
DRAWING TITLE :	CONSTRUCTION SEQUENCE FOR UNDERPIN SECTION

REV.	DATE	INITIALS	DESCRIPTION
1			
0	27-11-'15	LRP	FOR APPROVAL
REVISIONS			

PROJ. NO :	FR0343	DWG. NO :	FR - TMP - 1001
SCALE :	AS SHOWN (A3)	DATE :	27-11-'15
DESIGN :	LRP	REVISION NO :	0
DRAW :	LRP	CHECKED :	AC
		APPROVED :	AC
