


Section M - M' Shows the relationship between the rear garden of neighbouring Property, The Lodge, on the Western Boundary of the site.

On Site Existing G.L (102.360) On Site Proposed G.L (102.20) Top of Proposed Fence Level (104.21)

Proposed Construction Sequence
Existing Tree to be felled and removed. Existing timber fence to be removed. Install sheet piling from 102.00 reinforced retaining wall. added in 1m long sections. New underpinned concrete retaining wall to be formed in an underpin sequence. excavation of proposed basement. Sheet piling to be Replacement post and timber fence to sit on top of new collapse of adjacent party wall during demolition and to be replaced initially with sheet piling to prevent See also Symmetrys Temporary Retaining Works Drawing TO1 (Section 9-9). The existing timber fence All engineering to Symmetrys design and specification garden wall through Tree Root Protection Area. (RPA). against sheet piling. Hand dig foundations for internal new substructure including casting new retaining wall level. Excavate to required formation level and install

## Section N - Existing

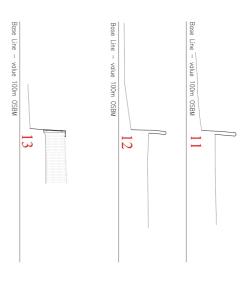

Images to the right show views of the existing northern boundary wall between the site and No.3 Ellerdale Road. Wall the be rebuilt.





