




1. MOBILISATION AND SITE SET UP

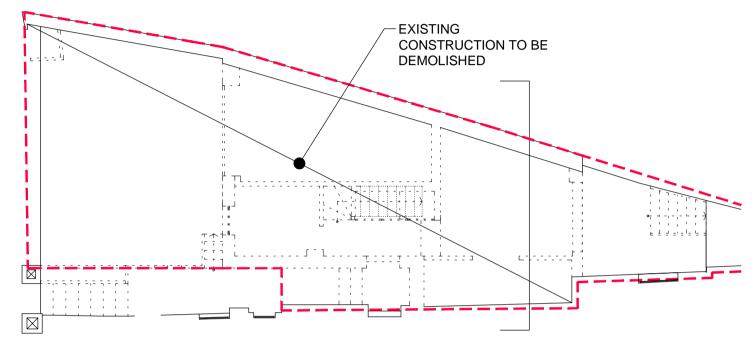


2. EXISTING STRUCTURE DEMOLISION

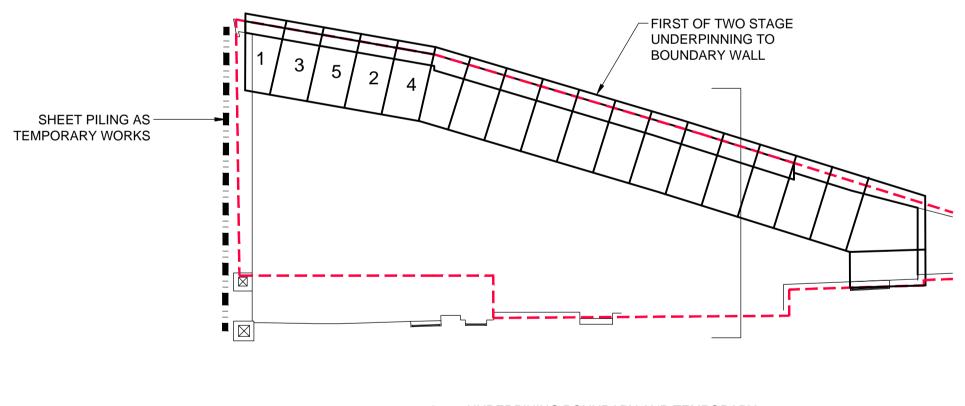

3. UNDERPINING BOUNDARY AND TEMPORARY WORK TO FRONT ELEVATION

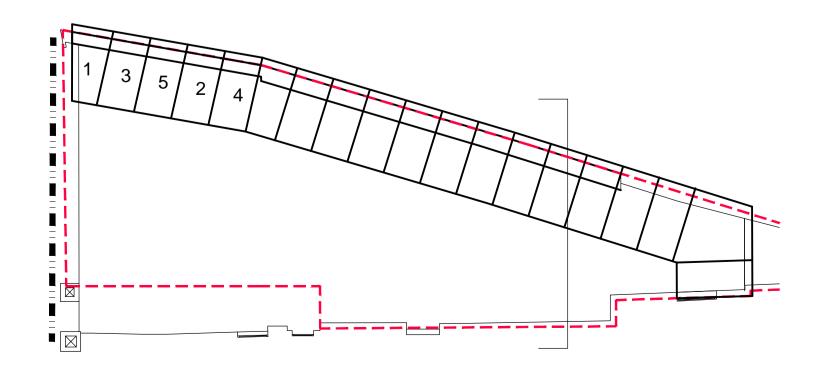

4. <u>COMPLETE SECOND STAGE UNDERPINNING</u>

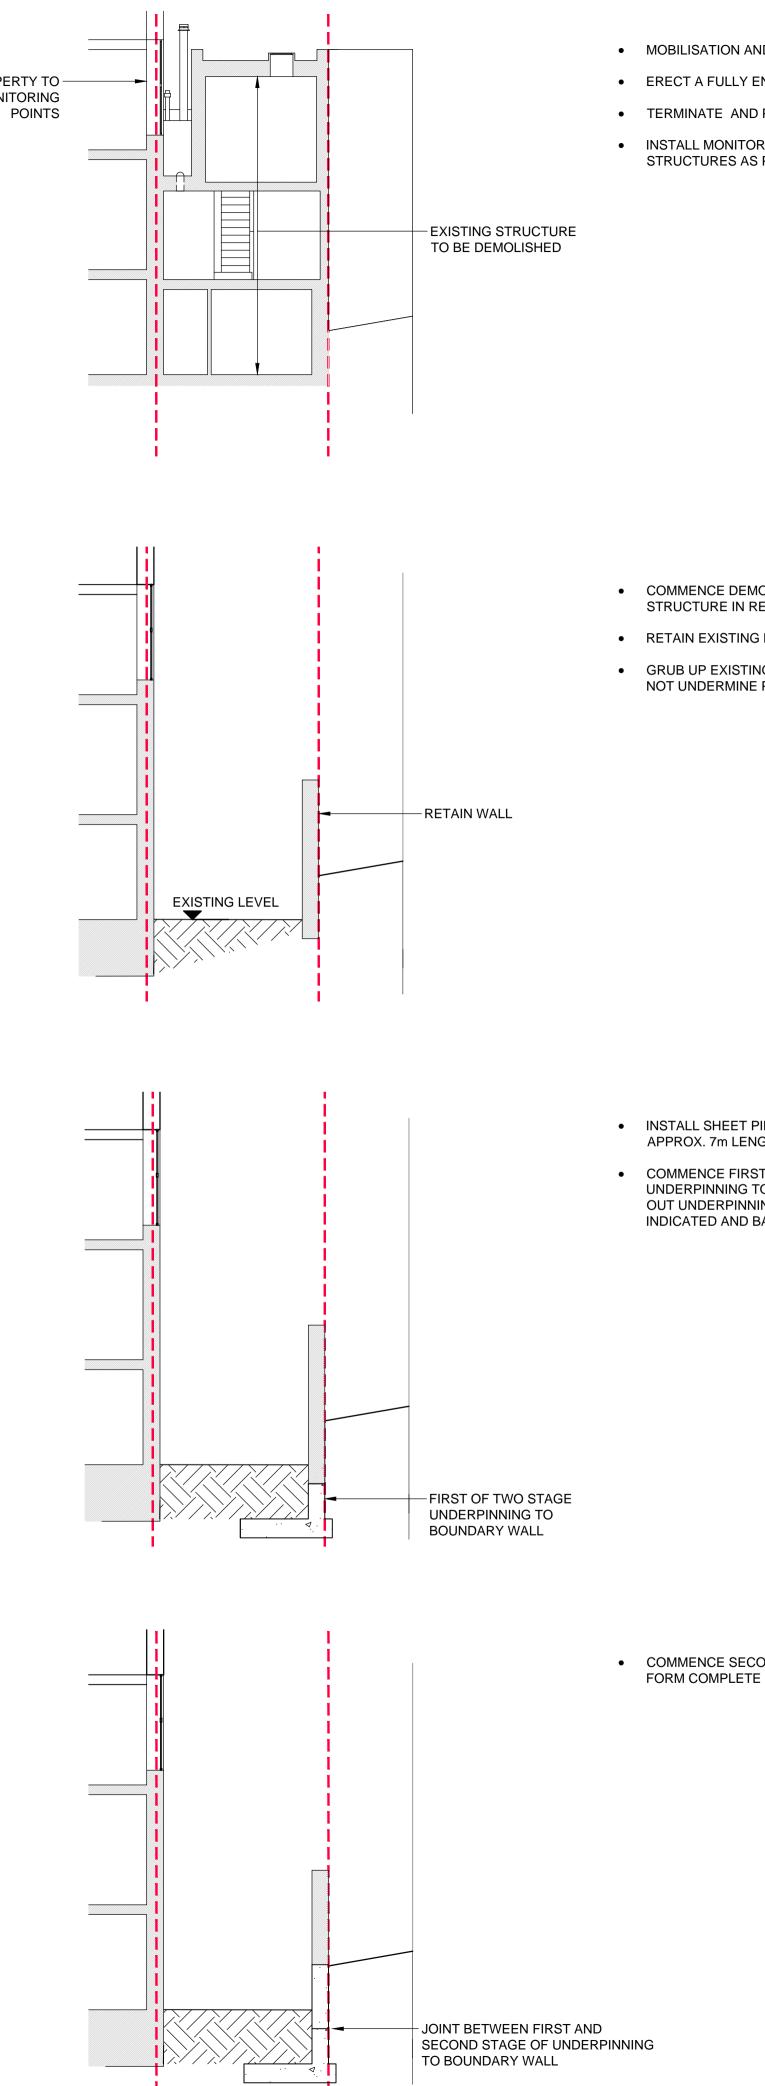

- MOBILISATION AND SITE SET UP
- ERECT A FULLY ENCLOSED SITE HOARDING
- TERMINATE AND PROJECT SERVICES
- INSTALL MONITORING SURVEY POINTS ON ADJACENT STRUCTURES AS PER MONITORING SPECIFICATION.

- COMMENCE DEMOLITION OF EXISTING COACH HOUSE STRUCTURE IN REVERSE ORDER OF CONSTRUCTION
- RETAIN EXISTING BOUNDARY WALL TO SIDE ELEVATION
- GRUB UP EXISTING LOWER GROUND FLOOR SLAB DO NOT UNDERMINE PAVEMENT

- INSTALL SHEET PILING AS TEMPORARY WORKS TO APPROX. 7m LENGTH ELEVATION WITH BELSIZE SQUARE
- COMMENCE FIRST STAGE OF TWO STAGE REINFORCED UNDERPINNING TO REMAINDER OF BOUNDARY. CARRY OUT UNDERPINNING ON A SEQUENTIAL SEQUENCE AS INDICATED AND BACKFILL.

 COMMENCE SECOND STAGE OF UNDERPINNING TO FORM COMPLETE REINFORCED CONCRETE WALL.

GENERAL NOTES

- 1. THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTS, ENGINEERS AND SPECIALIST DRAWINGS AND SPECIFICATIONS
- 2. DO NOT SCALE FROM THIS DRAWING IN EITHER PAPER OR DIGITAL FORM. USE WRITTEN DIMENSIONS ONLY.

NOT FOR CONSTRUCTION

P1	21.09.17	ISSUED FOR INFORMATION	JAB	КН
Rev	Date	Description	Drawn	Check
Consulting Structural Engineers Consulting Civil Engineers London • Cambridge • Norwich 1-5 Offord St London N1 1DH Telephone 020 7700 6666 www.conisbee.co.uk				
	wing Sta FORM	IATION		
Pro	ject		ate SEI	P 2017
	50A BELSIZE SQUARE		cale	NTS
LC	ONDON NW3 NH4		rawn	MA
Title)	E	ngineer	КН
	ONSTRUCTION SEQUENCE HEET 1		Project No 170013	
Drawing No 170013-X-XX-DR-S-1000			Revision P1	
