
Prog No.: SH-S19A- Rev.: Rev. date : 19/01/2021   Issue date : 19/01/2021				Space House Standalone Application for Planning Permission & Listed Building Cons														ns	e							
Line	Name	Start	Finish	Duration	Contractor		F 25   15	M 8	A 29 1	M 9_10	] 31	202 21	J	A 2 2	S 3 13	3 4	0  25	N 15	D 6	J 10	F 31 2	<u>м</u> 21, 14			M 16	
1	Construction Phase Works, overall	01/02/21	29/03/23	113w																						
2	Enabling works (summary)	01/02/21	15/09/21	33w	Erith	2																				
3	Main Contract Phase (summary)	15/09/21	29/03/23	80w	BAM										3											
4	Enabling Works Programme Highlights	01/02/21	15/09/21	33w																						
5	Strip-out Works	01/02/21	05/08/21	26w	Erith	5																				
6	Implementation of extant PP (2019/2773/P & LBC 2019/2790/L	01/03/21	01/03/21				6																			
7	Demolitions, Phase 1 (exist PP consent ref. 2019/2773/P and LBC ref. 2019/2790/L	01/03/21	15/09/21	28w	Erith		7																			
8	Demolitions, Phase 2 (subject to new standalone application for planning permission and listed building consent)	19/04/21	30/07/21	15w	Erith				8																	
9	UKPN façade & internal demolitions (*subject to new standalone application for planning permission and listed building consent)	29/03/21	14/05/21	6w	Erith			9																		
10	Planning Timeline	25/01/21	18/06/21	21w																						
11	a) New standalone application for planning permission and listed building consent, submission	25/01/21	25/01/21			11																				
12	Determination period	25/01/21	26/03/21	9w		12			ļ										,     							
13	Anticipated date of decision	26/03/21	26/03/21					13											1 1 1 1							
14	b) Section 73/Section 19 Application, submission	26/02/21	26/02/21				14																			
15	Determination Period	26/02/21	18/06/21	16w			15			///																
16	Anticipated date of decision	18/06/21	18/06/21								16	6														
						4	25 15	Q	20 1	9 10	21	21	12	ງ່   າ	2 12	2 1	י ר <u>י</u> ר	' 1'E'	6	10	21 '	)1 1	<u> </u>	25	16	٢
Line	Name	Start	Finish	Duration	Contractor	י ד ן	- F	0 M	29 1	M c	)] ]	21	12	<u>ζ</u> 2	.) Ι3   ς	די ע 	0	N CT I	U D	10	F	Δ1 1' Μ	<b>1 1</b> 	<u>2</u> 5 A	M	U
							1	11				202	1	11	5		~	11			1			<u>،</u>		
Prep	ared by: CF Manager :CW		Rev comme	ent:																						_

Project Ref. C:\Box\67502 - Instructions\Seaforth Land\Space House\Programme\210119 Revised Application Jan 2021.pp

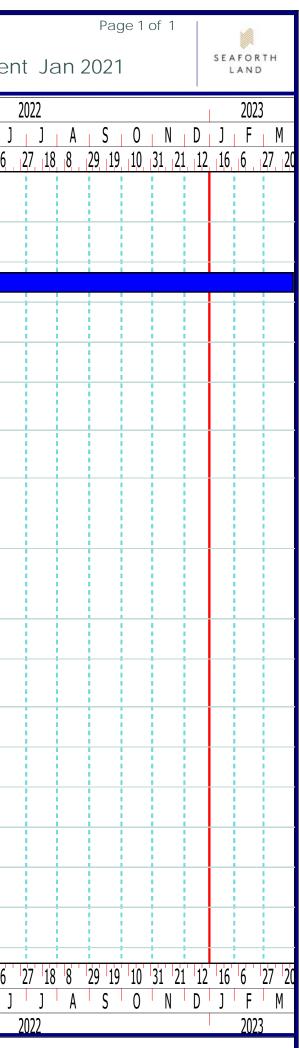

Printed: 17:17:57 / 19/01/2021
