


Notes

THIS DRAWING IS COPYRIGHT OF FORM.


DO NOT SCALE FROM THIS DRAWING WORK ONLY TO FIGURED DIMENSIONS.

THE CONTRACTOR IS TO VERIFY ALL DIMENSIONS ON SITE BEFORE COMMENCING WORK. ALL ERRORS AND OMISSIONS ARE TO BE REPORTED TO THE ENGINEER.

THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECT'S, SERVICES ENGINEERS AND ENGINEERS DRAWINGS AND SPECIFICATIONS.

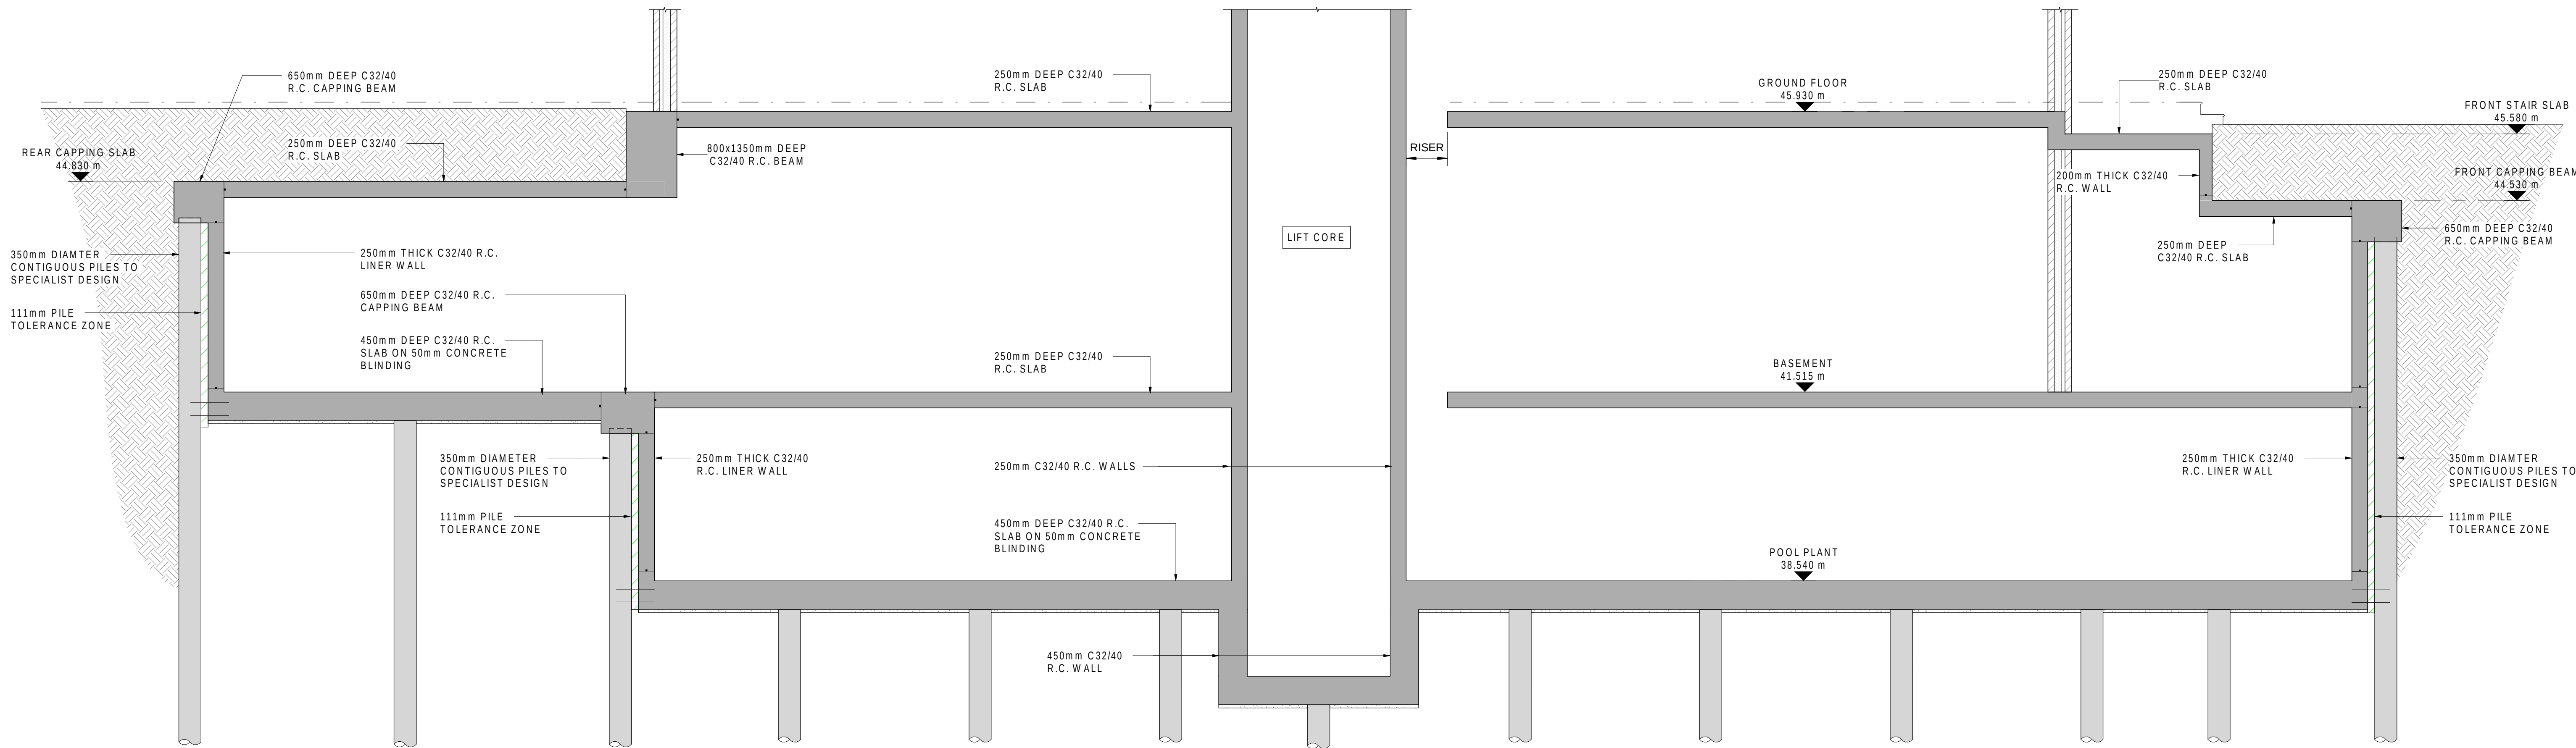

PROPOSED CROSS SECTION A - A  
1: 50 @ A0 / 1:100 @ A3

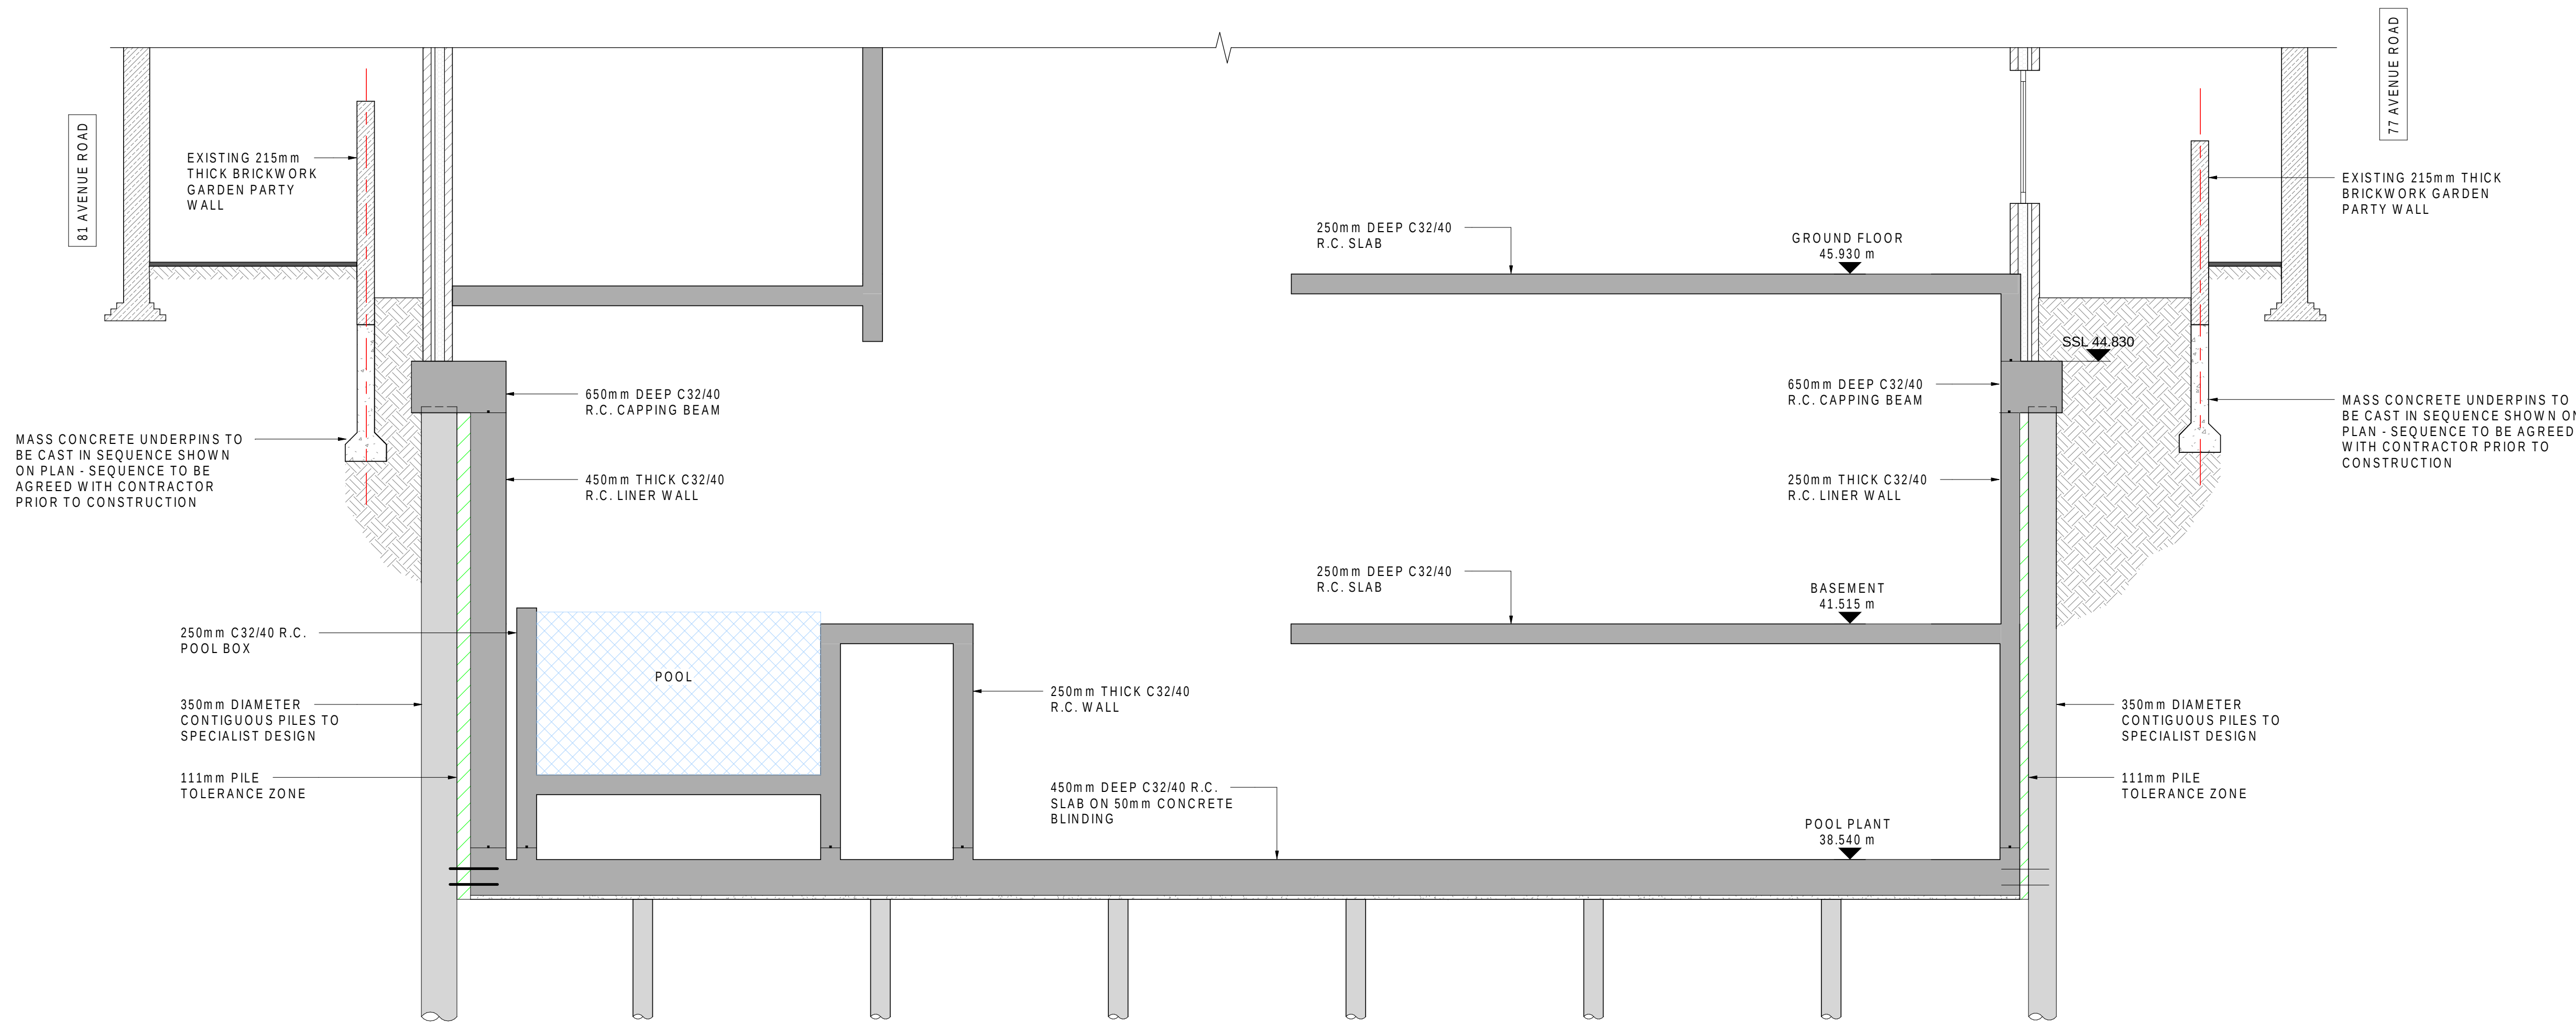

PROPOSED CROSS SECTION B - B  
1: 50 @ A1; 1:100 @ A3

|      |          |                    |             |
|------|----------|--------------------|-------------|
| P2   | 21/05/21 | ISSUED FOR COMMENT | AONDH       |
| P1   | 20/03/20 | ISSUED FOR COMMENT | PE/NG       |
| Rev. | Date     | Amendment          | Drawn / CDR |

Drawing Status PRELIMINARY


Form

Job Title  
79 AVENUE ROAD,  
LONDON,  
NW 8


Drawing Title  
PROPOSED SECTION A-A & B-B

Form Structural Design Ltd 77 St John Street London EC1M 4NN  
T: 020 7253 2853 E: studio@form-sd.com W: www.form-sd.com


|         |             |          |         |
|---------|-------------|----------|---------|
| Date    | Scale       | Drawn    | Checked |
| DEC 19  | 1 : 50      | PE       | WG      |
| Job No. | Drawing No. | Revision |         |
| 193219  | A(28)01     | P2       |         |






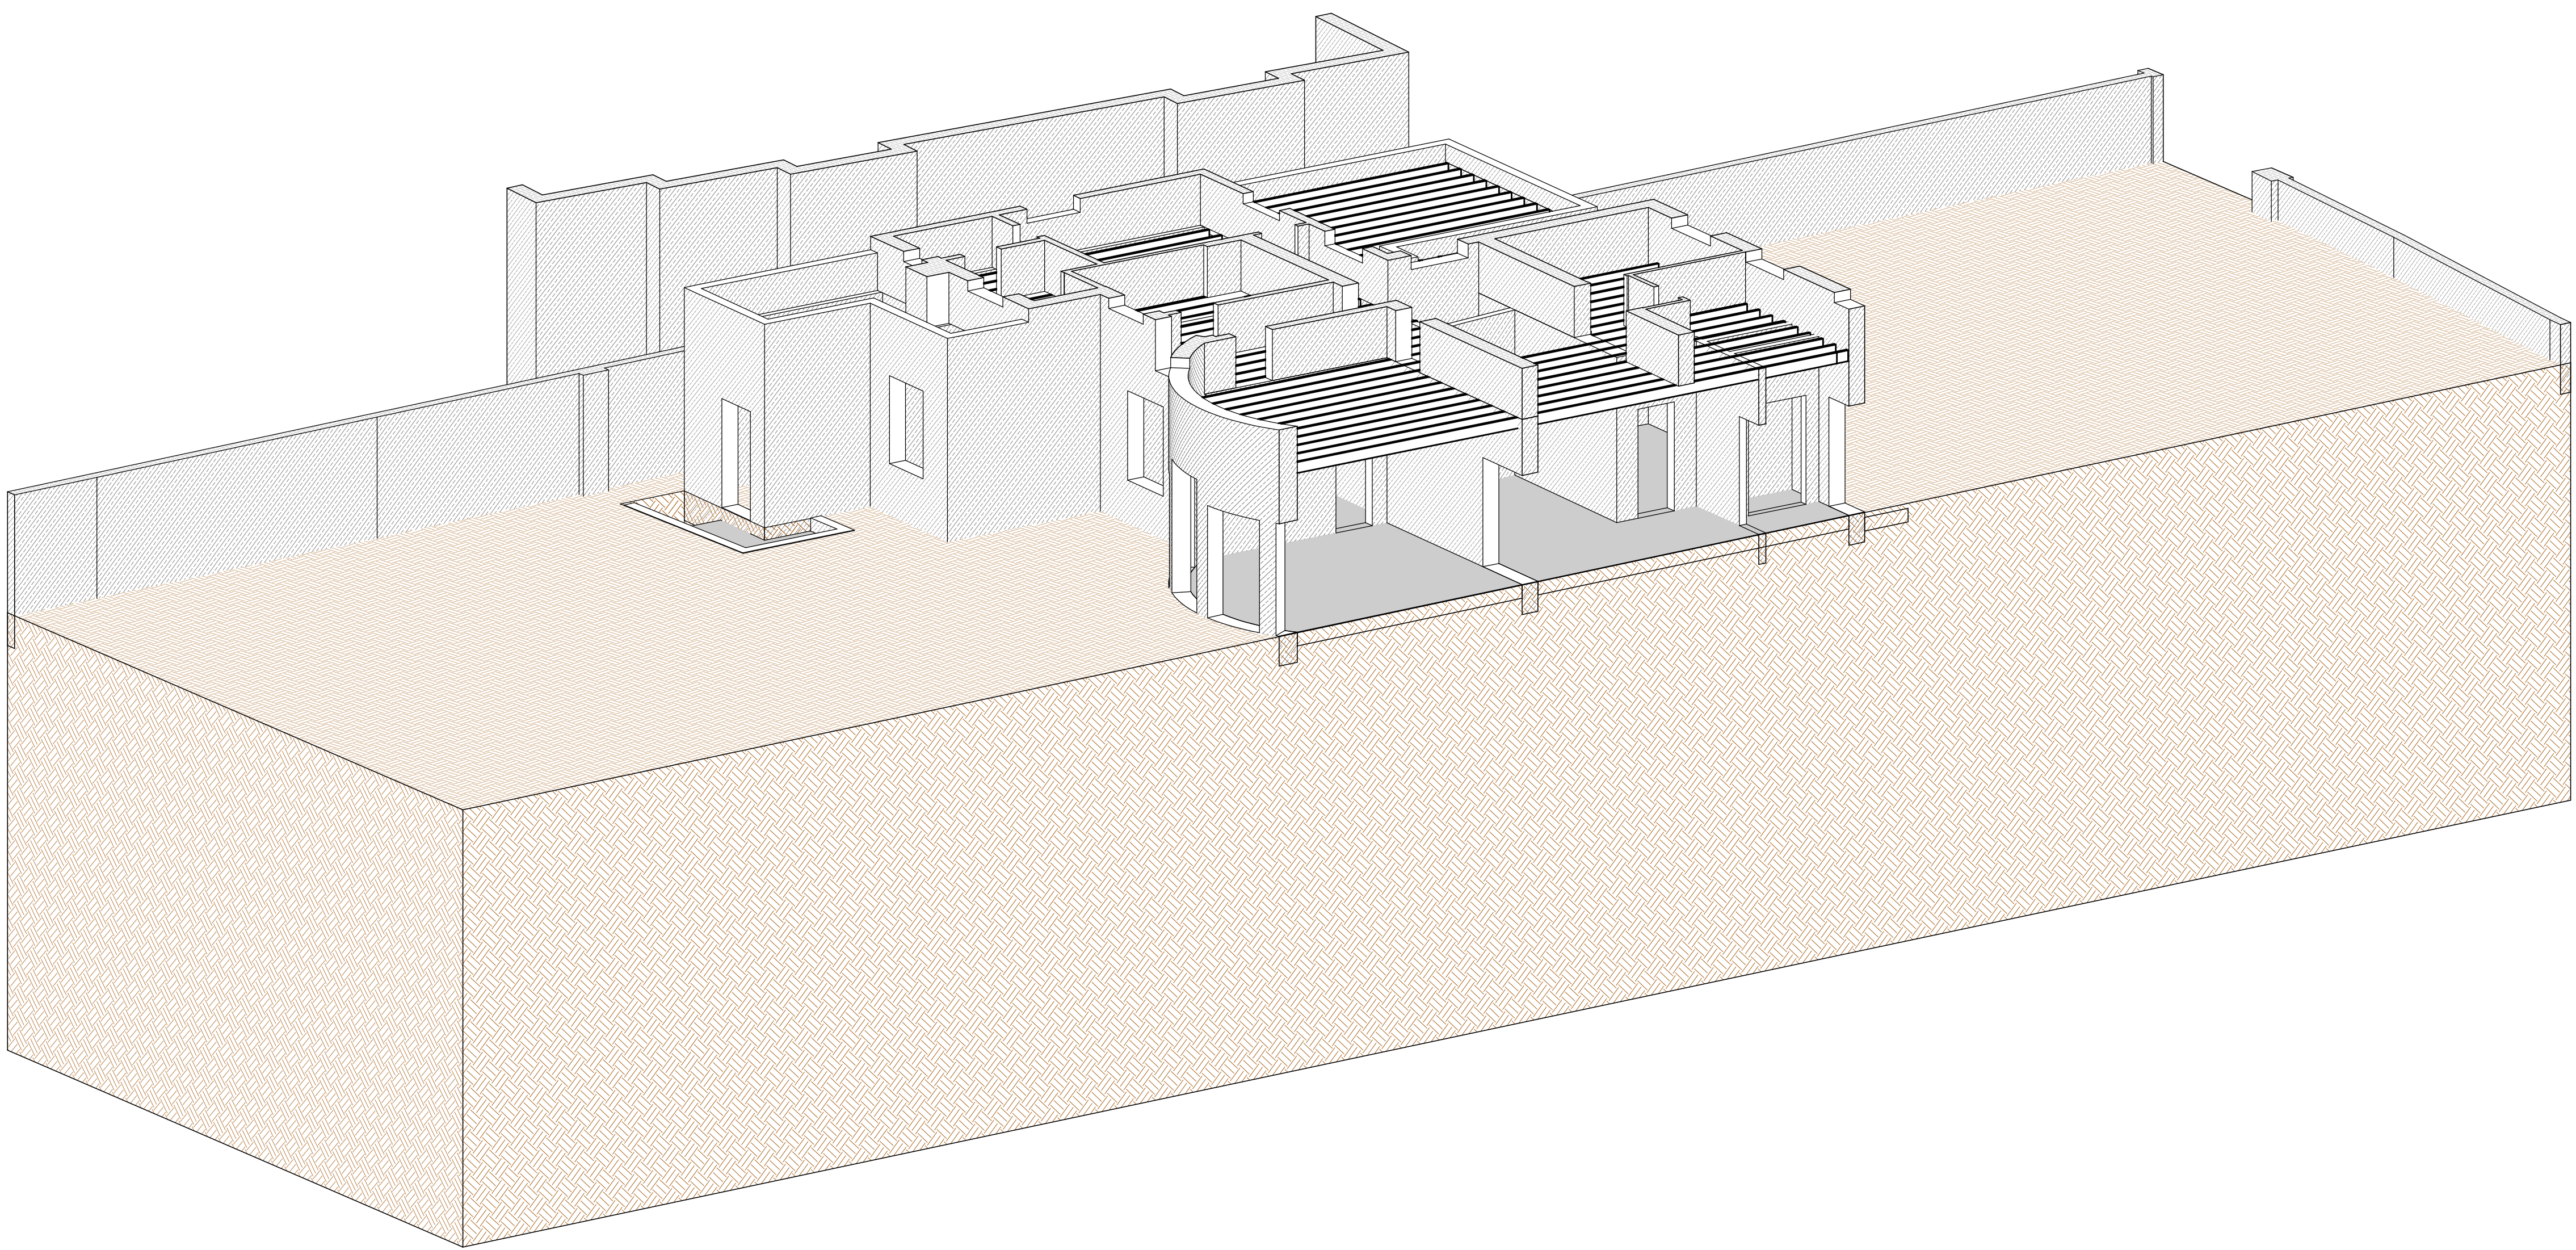

SUGGESTED SEQUENCE OF WORKS - AS EXISTING

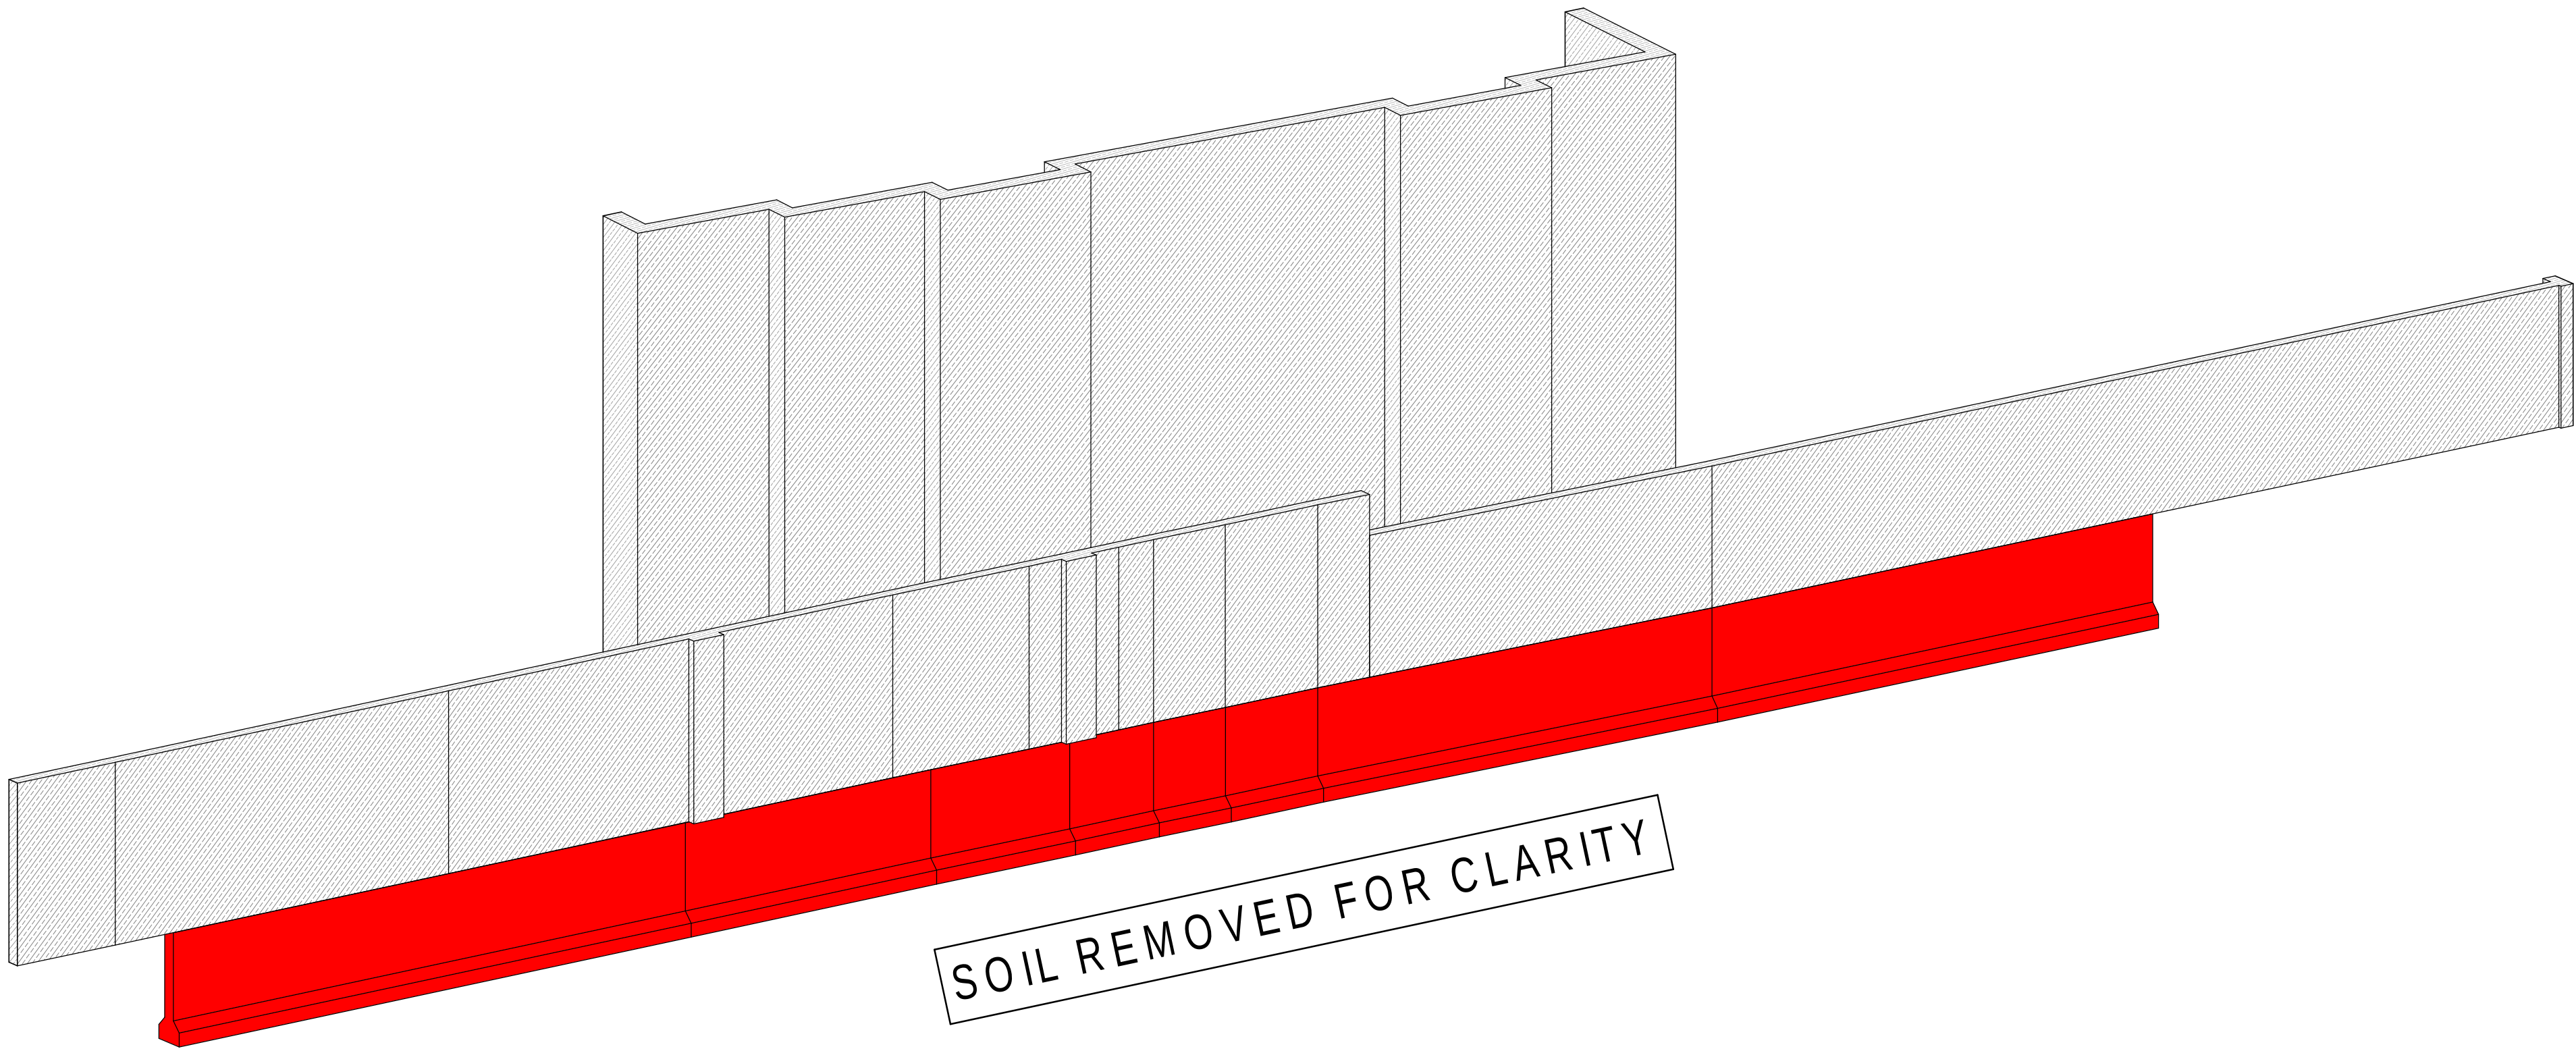

SUGGESTED SEQUENCE OF WORKS - PHASE 1

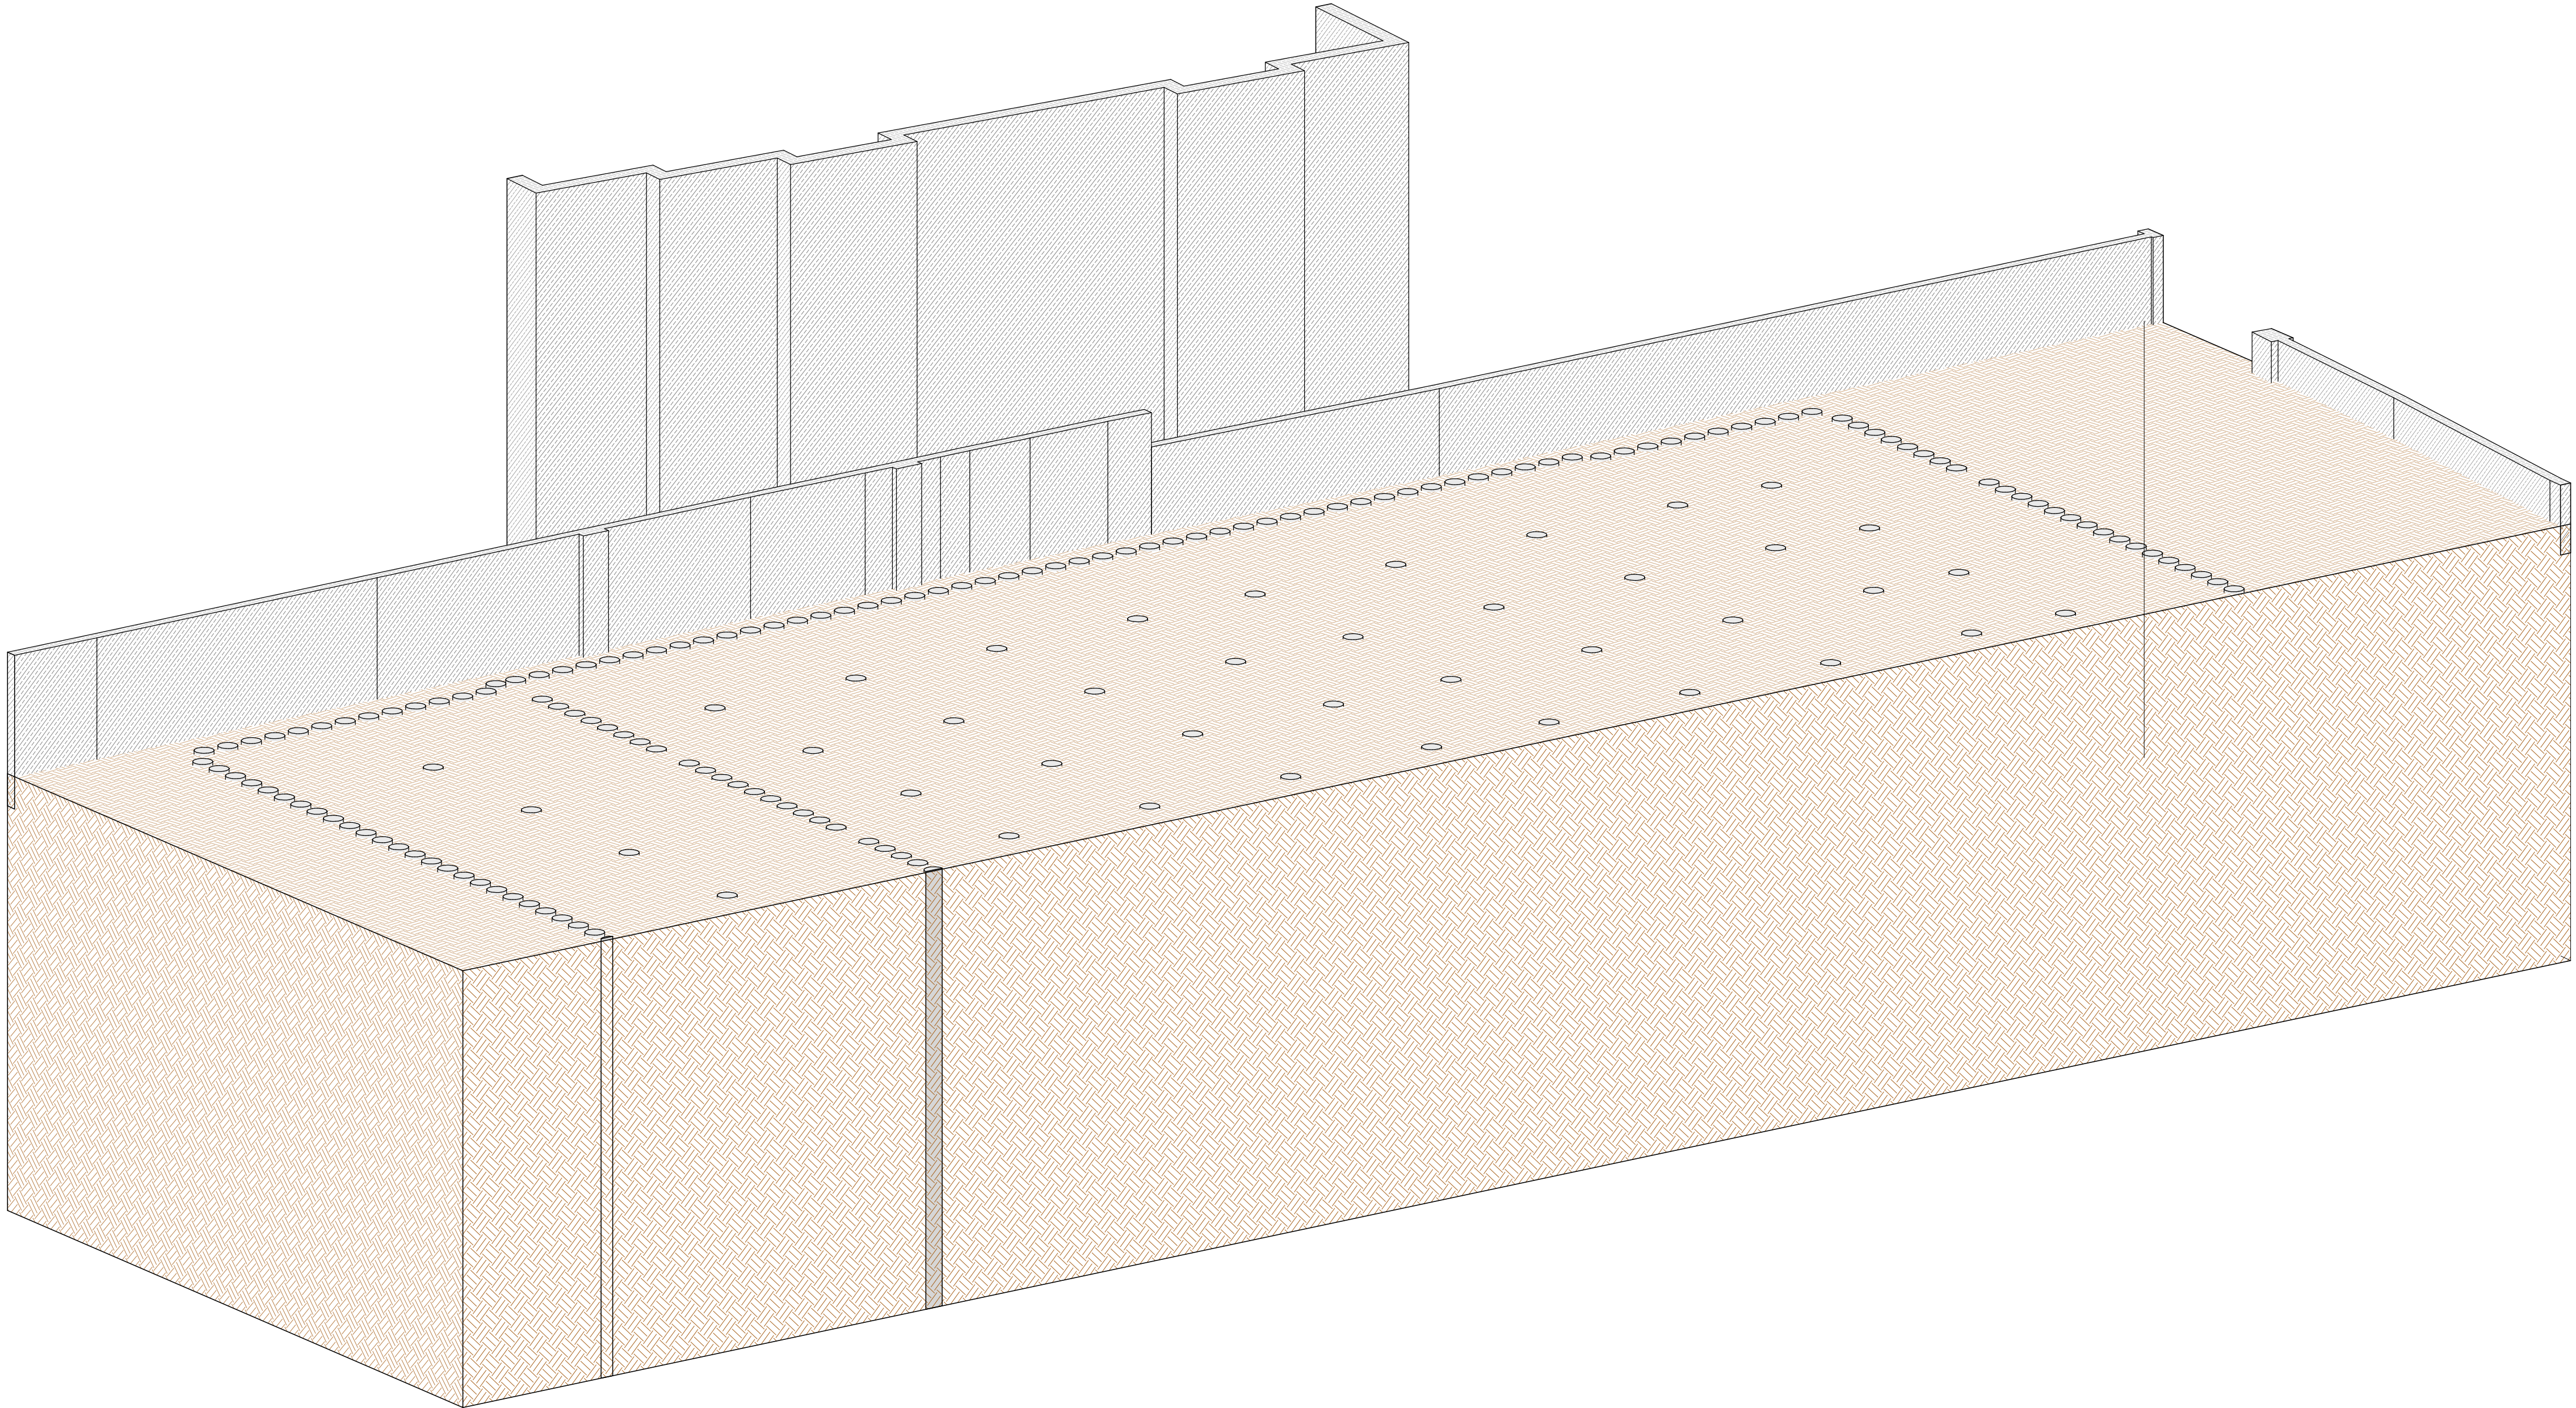

SUGGESTED SEQUENCE OF WORKS - PHASE 2

|                                                                                                                                                                       |  |  |  |
|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------|--|--|--|
| Notes                                                                                                                                                                 |  |  |  |
| THIS DRAWING IS COPYRIGHT OF FORM.                                                                                                                                    |  |  |  |
| DO NOT SCALE FROM THIS DRAWING WORK ONLY TO FIGURED DIMENSIONS.                                                                                                       |  |  |  |
| THE CONTRACTOR IS TO VERIFY ALL DIMENSIONS ON SITE BEFORE COMMENCING WORK. ALL ERRORS AND OMISSIONS ARE TO BE REPORTED TO THE ENGINEER.                               |  |  |  |
| THIS DRAWING IS TO BE READ IN CONJUNCTION WITH ALL RELEVANT ARCHITECTS, SERVICES ENGINEERS AND ENGINEERS DRAWINGS AND SPECIFICATIONS.                                 |  |  |  |
| <b>SUGGESTED SEQUENCE OF WORKS</b>                                                                                                                                    |  |  |  |
| MOBILISATION AND PREPARE SITE WITH ALL NECESSARY HOARDING AND ASSOCIATED HEALTH AND SAFETY AND SECURITY REQUIREMENTS.                                                 |  |  |  |
| LOCATE ALL EXISTING SERVICES AND IDENTIFY THOSE AFFECTED BY THE NEW WORKS AND TAKE NECESSARY ACTIONS AS REQUIRED BY M+E ENGINEER, DRAINAGE ENGINEER AND THAMES WATER. |  |  |  |
| CHECK ALL BOUNDARY CONDITIONS ARE AS TO BE EXPECTED AND REPORT ANY VARIATIONS TO THE ENGINEER.                                                                        |  |  |  |
| <b>PHASE 1</b>                                                                                                                                                        |  |  |  |
| DEMOLISH EXISTING BUILDING                                                                                                                                            |  |  |  |
| CARRY OUT UNDERPINNING IN SEQUENCE SHOWN ON PLAN TO EXISTING GARDEN PARTY WALLS                                                                                       |  |  |  |
| <b>PHASE 2</b>                                                                                                                                                        |  |  |  |
| INSTALL PILING MAT                                                                                                                                                    |  |  |  |
| INSTALL PILES AND TEMPORARY SUPPORT PILES                                                                                                                             |  |  |  |
| <b>PHASE 3</b>                                                                                                                                                        |  |  |  |
| EXCAVATE AND INSTALL CAPPING BEAM TO GROUND FLOOR LEVEL                                                                                                               |  |  |  |
| <b>PHASE 4</b>                                                                                                                                                        |  |  |  |
| CAST PROPOSED GROUND FLOOR AND GROUND FLOOR R.C. BEAMS LEAVING STAIRWELLS AND LIGHTWELLS CLEAR FOR ACCESS                                                             |  |  |  |
| <b>PHASE 5</b>                                                                                                                                                        |  |  |  |
| EXCAVATE TO FORMATION LEVEL OF BASEMENT LEVEL 1                                                                                                                       |  |  |  |
| <b>NOTE:</b> WORKS CAN COMMENCE TO SUPERSTRUCTURE ONCE SLAB INSTALLED                                                                                                 |  |  |  |
| <b>PHASE 6</b>                                                                                                                                                        |  |  |  |
| BREAK DOWN PROPOSED PILES TO PERIMETER OF SUB BASEMENT LEVEL LEAVING TEMPORARY SUPPORT PILES HIGH                                                                     |  |  |  |
| <b>PHASE 7</b>                                                                                                                                                        |  |  |  |
| INSTALL CAPPING BEAM AT BASEMENT LEVEL 1 TO SUB BASEMENT PERIMETER PILES                                                                                              |  |  |  |
| <b>PHASE 8</b>                                                                                                                                                        |  |  |  |
| INSTALL TEMPORARY BRACING TO SUB BASEMENT CAPPING BEAM                                                                                                                |  |  |  |
| <b>PHASE 9</b>                                                                                                                                                        |  |  |  |
| EXCAVATE TO FORMATION LEVEL OF SUB BASEMENT                                                                                                                           |  |  |  |
| <b>PHASE 10</b>                                                                                                                                                       |  |  |  |
| INSTALL SUB BASEMENT SLAB                                                                                                                                             |  |  |  |
| <b>PHASE 11</b>                                                                                                                                                       |  |  |  |
| INSTALL COLUMNS AND WALLS TO SUB BASEMENT                                                                                                                             |  |  |  |
| <b>PHASE 12</b>                                                                                                                                                       |  |  |  |
| INSTALL BASEMENT LEVEL 1 SLAB                                                                                                                                         |  |  |  |
| <b>PHASE 13</b>                                                                                                                                                       |  |  |  |
| REMOVE TEMPORARY PROPPING TO CAPPING BEAM                                                                                                                             |  |  |  |
| <b>PHASE 14</b>                                                                                                                                                       |  |  |  |
| INSTALL BASEMENT LEVEL 1 WALLS AND COLUMNS                                                                                                                            |  |  |  |
| <b>PHASE 15</b>                                                                                                                                                       |  |  |  |
| BREAK DOWN TEMPORARY SUPPORT PILES MAKING SLAB GOOD POST DEMOLITION                                                                                                   |  |  |  |
| <b>PHASE 16</b>                                                                                                                                                       |  |  |  |
| REMAINDER OF PROPOSED WORKS TO COMMENCE                                                                                                                               |  |  |  |

|                                                              |             |           |                |
|--------------------------------------------------------------|-------------|-----------|----------------|
| P2 21/05/21 ISSUED FOR COMMENT                               |             | AC/NDH    |                |
| P1 20/01/20 ISSUED FOR COMMENT                               |             | PE/WG     |                |
| Rev.                                                         | Date        | Amendment | Drawn / Checkd |
| Drawing Status                                               |             |           |                |
| PRELIMINARY                                                  |             |           |                |
| Job Title                                                    |             |           |                |
| 79 AVENUE ROAD,<br>LONDON,<br>NW 8                           |             |           |                |
| Drawing Title                                                |             |           |                |
| SUGGESTED SEQUENCE OF<br>WORKS                               |             |           |                |
| Form Structural Design Ltd 77 St John Street London EC1M 4NN |             |           |                |
| T:020 7253 2893 E:studio@form-sd.com W:www.form-sd.com       |             |           |                |
| Date                                                         | Scale       | Drawn     | Checked        |
| DEC 19                                                       | 1 : 1       | PE        | WG             |
| Job No.                                                      | Drawing No. | Revision  |                |
| 193219-FSD-A                                                 | (30)01      | P2        |                |
