Page 1	of	5
--------	----	---

# SITE LOG

Project No.	B-45739	Shift No. 1	



Name of client		E Brit Services, Charfleets Industrial Estate, Kings Road, Canvey Island. Essex SS8 0QY					
Site address assessed		13-15 John Mews, London. WC1N 2PA.					
TIME	SITE LOG						
12:45	PW and MJ ar	rived on site and discussed todays plan of work with the site supervisor.					
13:06	Stage 1 of 4 S	tage clearance passed on the Garage.					
13:37	Stage 2 of 4 S	tage clearance passed on the Garage					
13:38	2 Clearance te	ests commenced inside the Garage.					
13:48	1 Clearance te	est commenced inside DCU No2.					
14:40	2 Clearance to	ests taken off inside the Garage results satisfactory <0.01f/ml.					
14:50	1 Clearance te	est taken off inside DCU No2 result satisfactory <0.01f/ml.					
15:06	Stage 3 of 4 S	tage clearance passed on the Garage.					
15:07	1 Reassuranc	1 Reassurance tests commenced during the dismanteling of the enclosure.					
15:59	Stage 4 of 4 S	Stage 4 of 4 Stage clearance passed on the Garage.					
16:09	1 Reassuranc	1 Reassurance test taen off result satisfactory <0.01f/ml.					
16:35	PW and MJ le	PW and MJ left site.					

# NB: Information given is supplementary to the 4SC report and does not form part of the 4SC certification Daily Inspection/Checks:

Hygiene unit clean and connected to services Yes		Enclosure as bestos warning signs	Yes	
Transit route sealed off and signed	Yes	Respirator areas warning signs	Yes	
Waste/Skip area locked	Yes	Enclosure seals checked and intact	Yes	
Warning labels attached to skip	Yes	Adequate negative pressure	Yes	
Copy of METHOD STATEMENT read	Yes	NPU vented outside building	Yes	
Operatives transiting in accordance with HSG247				
Regular inspection of all areas (enclosure, transit route, surroundings, skip)				
Were any defects/problems brought to attention of contractor?				
All bagged as bestos locked in waste skip at end of shift if applicable				
Site in clean, safe & tidy condition at end of shift				

Analyst PDH WILLCOCK	Signature	Date 19-Aug-2014
	Life Environmental Services	
	The natural choice for environmental compliance and risk management solutions	
Head Office		
4 Duckett's Wharf	New Meltham House	
South Street	Units 37/38 Beresford Way	
Bishop's Stortford	Chesterfield	
CM23 3AR	S41 9FG	
	Tel: 01246 263 370	
Tel: 01279 503117	Fax: 01246 283 399	
Fax: 01279 503162		
		Issue 8/Site Log/Life/Jan 14

## **CERTIFICATE OF REOCCUPATION**



Project No. <u>B-45739</u>	Shift No. <u>1</u>		Enclos	ure Reference No. <u>(</u>	Garage		
Name and address of clie	ent		E Brit Services, Charfleets Industrial Estate, Kings Road, Canvey Island. Essex SS8 0QY.				
Site Address			13-15 John Me	ws, London.WC1N 2PA.			
Description of works/Are	eas to be assessed		Removal of AIE	Cladding to Steelwork wi	thin the garage.		
Name of asbestos remov	al contractor		E Brit Services.				
Has the LARC site super inspection of the enclosu satisfactory (Representa	re is completed an	id	Yes	Analyst not to procee satisfactory inspection	d without contractor's c	onfirmatio	on of a
CONTRACTOR'S REPR	ESENTATIVE CO	NFIRMA	TION OF END	LOSURE INSPECTIO	N		
I confirm that the enclosu	re has been inspe	cted and	l is satisfactory	for the analyst to proce	eed with stage 1 of the	reoccupat	tion procedure
Name: C Brackett	Si	ignature	:CU	Time:	13:00 Date:	19-Aug-20	014
Stage 1 of 4: Preliminary	check of site con	dition a	nd job comple	teness			
1.1 Plan of work checked	to confirm areas	to be as	sessed and ent	tire defined work area	agreed and completed	:	
(record any problems, di	fferences or know	n asbest	os to remain)				
			150				
Are the following	1.2 Work	1.3 En	closure intact	1.4 NPU/Vac	1.5 Hygiene Unit	1.6 V	ision Panel/
intact and operating?	areas intact			Operational	Operational	CCTV present	
	Yes	Yes		Yes	Yes	Yes	
Inspections with viewing panel / cctv	Adequate Lighting	Yes		Suitable sufficient Access Equipment	Yes		
Areas free from	1.7 Enclosure ar	d Surro	unding area	1.8 Waste route/skip			9 Transit
obvious asbestos						route/	Hygiene Unit
waste & debris	Yes			Yes		Yes	
Stage 1: Pass	(STRIKE THROUG	SH REST	OF FORM IF F	AILED)			
Comments: As the site is	underseins meier se	furbiolom	ant aumaunding	area and weets/transit hav	a gonoral dobira procent		
As the site is	undergoing major re-	-turbishm	ent surrounding a	area and waste/transit nav	e general debirs present.		
Assessed by name: PDH	Willcook Sie	nature:		Time: 1	3:06 <b>D</b> ata:	19-Aug-1	4
Stage 2 of 4: Thorough v		gnature.	<i></i>	Time.	o.oo Date.	13-Aug-1-	*
2.1 Airlock/baglock and e	anclosure are free	from		2.4 Any evidence of la	ock down sprays (E.g. F	Σ\/Λ\	
waste bags, materials an		HOIII	Yes	where the LARC was		VA)	No
equipment	a annecessary		162	Where the Lake was	not instructed to		140
2.2 The enclosure and air	rlocks have been v	/isually		2.5 ACM's removed.	encapsulated or enclo	sed as	
inspected and within lim				specified in the plan			
been deemed to be visibly clean of dust and			Yes				Yes
debris	,						
2.3 Enclosure is dry				2.6 Any remaining as	bestos has been left in	good	
			Yes	condition or encapsu	lated depending on the	e	N1/A
			162	material and has bee	n marked on the attac	hed	N/A
				plan			

Life Environmental Services
The natural choice for environmental compliance and risk management solutions

Issue 5/COR/Life/Jan14

Head Office
4 Duckett's Wharf
South Street
Bishop's Stortford
CM23 3AR
Tel: 01279 503117
Fax: 01279 503162

New Meltham House Units 37/38 Beresford Way Chesterfield 541 9FG Tel: 01246 263 370 Fax: 01246 283 399



## **CERTIFICATE OF REOCCUPATION**



Project No. B-45739	Shift No. 1	Enclo	sure Reference No.	Garage	•	•	services
Stage 2: Pass	(STRIKE THROU	GH REST OF FORM IF	FAILED)				
The length of the visual	was <sup>16</sup>	mins					
Comments:							
Assessed by name: PDH	Willcock	Signature:		Time: 13:37	Date:	19-Aug	g-2014
Stage 3 of 4: Clearance a	00 00 00 00 00		,				
3.1 All areas dry	Yes	3.2 Volume/Area of enclosure	15m2/45m3	3.3 Method of dis	sturbance	Brus	hing
3.4 NPU's off & capped	Yes	3.5 Number of sampl	les 2	3.6 Duration of d	isturbance	3 mi	nutes
Air test certificate No's:	AMC-01						
Stage 3: Pass	(STRIKE THROU	GH REST OF FORM IF	FAILED)				
The enclosure can be dic Comments: Assessed by name: PDH		Signature:		<b>Time:</b> 15:06	Date:	19-Au	ug-2014
Stage 4 of 4: Assessment	200		closure is removed)				
4.1 Former enclosure at been dismantled and the immediate surrounding	nd equipment has e work area and s are visibly free		4.2 Transit / waste rou free from any visible a enclosure materials a	.2 Transit / waste route and area is ree from any visible asbestos debris, nclosure materials and waste?			
from any asbestos debr materials and waste?	is, enclosure		4.3 Was there any evi- and dust being release enclosure dismantlem	ed from the	No		
4.4 Any known ACMS w any uncovered during s safe condition?		N/A	4.4 Reassurance Air te If no reassurance test give reasons why belo	was required	Yes		
Comments: Reassurance test satisfactory <0.01f/ml.							
Stage 4: Pass							
The area Can be re-occu	ıpied						
Assessed by name: PDH	l Willcock	Signature	: ,	Time: 15:59	Date:	19-Au	ıg-2014
Contractor's representative acknowledgement:							
I have been advised by Paul Willcock of Life Environmental that the Certificate of Reoccupation has been issued because the area has Passed All Stages clearance procedures.							

Life Environmental Services

The natural choice for environmental compliance and risk management solutions

Signature: (

Issue 5/COR/Life/Jan14

Date: 19-Aug-2014

Time: 16:01

4 Duckett's Wharf	New Meltham House
South Street	Units 37/38 Beresford Way
Bishop's Stortford	Chesterfield
CM23 3AR	S41 9FG Tel: 01246
Tel: 01279 503117	263 370
Fax: 01279 503162	Fax: 01246 283 399

Contractor representative name: C Brackett



### Page 4 of 5

#### **AIR TEST CERTIFICATE**



Project No. <u>B-45739</u> Report No. <u>AMC-01</u> \_\_ Shift No. 1

Name and address of client E Brit Services Charfleets Industrial Estate, Kings Road, Canvey Island. Essex. SS8 0QY. 13-15 John Mews London WC1N 2PA. Site address
Areas to be assessed and brief description of job
Name of asbestos removal contractor

Removal of AIB Cladding to steelwork in the garage.

E Brit Services.

No	Pump	Head	Key	Location/Area	Temp	Pressure		imes (24hr)		low (I/min)	Corrected	Volume	Fibres	Fields	Calculated	Reported
	ref	ref			°C	mb	Start	Stop	Start	Stop	flow (I/min)	(litres)			Result f/ml	Result f/ml
1	HFP12	PW1	CL	Inside Garage	18	1009	13:38	14:40	8:0	8:0	N/A	496	2	200	0.0009	<0.01
2	HFP27	PW2	CL	Inside Garage	18	1009	13:38	14:40	8:0	8:0	N/A	496	2	200	0.0009	<0.01
3	H163MB	PW4	R	Dismantling Garage Enclosure	18	1009	15:07	16:09	8:0	8:0	N/A	496	4	200	0.0018	<0.01
		PW10	FB										MNC			

RET. CHI - Compilative Monitoring, E - Ecak, D - Background, CE - Clearance Testing, R - Reassurance, TD - Tien Blank Mile - Mounted Not Counted					
Microscope No.	MS11MB	Graticule Diameter (um)	100		
Flow Meter No.	F7 F60	HSE/NPL Test Slide No.	NPL12		
Where counted?	Site	5th Band Observed on Test Slide	Yes		
Watch/Thermometer/Barometer No.	W35		169		
Stage Micrometer No.	MM27	"O" Ring Diameter (mm)	21.7		

Analyst PDI	H Willcock	Signatur
Head Office		•
4 Duckett's Wharf	New Meltham House	west travers.
South Street	Units 37/38 Beresford Way	
Bishop's Stortford	Chesterfield	- ~ -
CM23 3AR	S41 9FG	
	Tel: 01246 263 370	= ( ≥ < ) =
Tel: 01279 503117	Fax: 01246 283 399	
Fam. 01270 F02162		

Date 19-Aug-2014

Life Environmental Services The natural choice for environmental compliance and risk management solutions

Issue 6/Air Test/Life/Jan14


#### Page of

## **PLAN OF WORK AREA**

Project No.	B-45739	Shift No.	1
Report No.	AMC-01		



Name and address of client	E-Brit Services, Charfleets Industrail Estate, Kings Road, Canvey Island, Essex.SS8 0QY.	
Site address	13-15 John Mews, London WC1N 2PA.	
Areas to be assessed and brief description of the works	Removal of AIB Cladding to steelwork within the garage.	

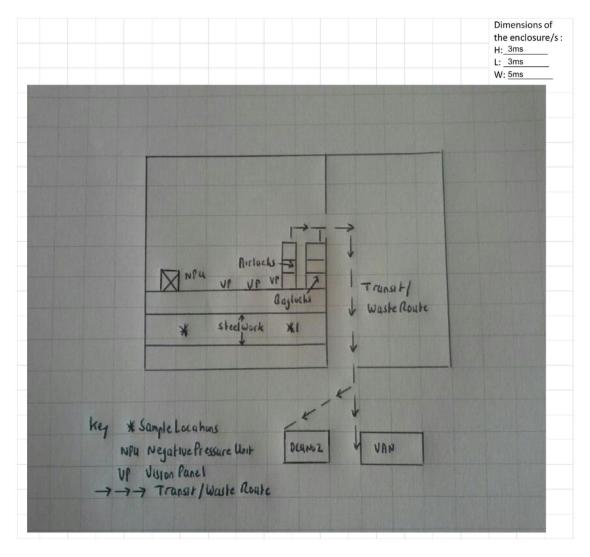

Name PDH Willcock	Signature	Date_19-Aug-2014
Contractor's Name C Brackett	Signature	mpany E -Brit Services Ltd.

