

REPORT ON ENVELOPE AIR

TIGHTNESS TESTING

AT

SOUTH CAMDEN COMMUNITY SCHOOL CHARRINGTON STREET LONDON NW1 1RG

> CLIENT: BAM CONSTRUCT UK LTD



HRS Services Ltd 81 Burton Road Sheffield S3 8BZ Tel 01142723004 altas@hrsservices.co.uk

1. INTRODUCTION

This report details the results of the envelope air tightness test carried out by HRS Services Ltd at:

South Camden Community School Charrington Street London NW1 1RG

The estimated year of construction was 2011.

The test was commissioned by Jim McCormack.

2. TEST CONDITIONS AND RESULTS

The worst acceptable building air permeability performance criteria as defined in Section 2 of the Building Regulations 2000 (as amended), Part L2A Conservation of Fuel and Power in New Buildings Other Than Dwellings is $10m^{3}/(h.m^{2})$ @ 50Pa.

The test was carried out on 09.12.11, between 17:30 and 18:25. The result is representative of the building as tested on this day.

The type of HVAC was mechanical.

The envelope area for air permeability is defined as the area of the external walls plus the area of the roof and the ground floor. The envelope area was calculated by the client.

The entire area of the building was tested.

The area of the building excluded was the ground floor plant room.

The envelope area of the test area was 2353m².

The following air permeability was determined at 50Pa.

 $9.46m^{3}/(h.m^{2})$

The test area therefore passed the specified air permeability performance criteria

Summary of Temporary Sealing

Temporary sealing was applied to the following elements of the building for the air test:

• HVAC supplies and extracts

Please see the next page for full details of temporary sealing.

3. TEMPORARY SEALING

The following tables provide a detailed breakdown of the temporary sealing applied to the building during the air test.

Temporary sealing applied to intentional openings								
Element	Temporarily sealed for air test?	Comment/Extent of Sealing						
HVAC supplies	Yes	All supplies sealed						
HVAC extracts	Yes	All extracts sealed						

Comments on Temporary Sealing

All temporary sealing applied was in compliance with Building Regulations 2000 (as amended), Part L2A Conservation of Fuel and Power in New Buildings Other Than Dwellings.

4. TEST METHOD

The envelope air tightness test was carried out in line with the following standards:

ATTMA TS1 Issue 2 - Measuring Air Permeability of Building Envelopes

BS EN 13829:2001 Thermal performance of buildings - Determination of air permeability of building - Fan pressurisation method.

The purpose of the test was method B (building envelope) as stated in BS 13829:2001. This requires that all adjustable openings shall be closed and remaining intentional openings sealed.

The building was pressurised using the HRS Services Ltd 'MIDIFAN' system. The MIDIFAN system comprises of a hydraulic powered fan designed to supply up to $32m^3$ /second at 70 Pascals static pressure. The MIDIFAN system was tested and calibrated in accordance with BS 848 Part 1 1997. The confidence limits on volumetric flow is $\pm 4\%$.

The MIDIFAN system was set up in the front double door.

Pressure differences across the MIDIFAN and the building were measured using digital micromanometers at the start, during and end of the test. Air temperatures were measured using Therma 1 digital thermometer with K Special penetration probes. Measurements were taken at the start and end of the test. The probes were located central and external to the building. Wind speeds at the start and end of the test were measured using a Kestrel K4000 meter. Barometric pressure was established by an absolute pressure meter.

The test area was prepared for air testing by the client. During the test HRS are external to the test area and are therefore reliant on the client maintaining the test area as agreed. The agreed test state of the test area is with all external windows and doors closed, and all internal doors open, with any temporary seals employed to remain intact for the duration of the test.

5. DETAILS OF TEST RESULTS


Please refer to the test results overleaf. The results have been interpolated from the readings taken between **32.5**Pa and **81.5**Pa with a correlation co-efficient of **0.9906**.

Zero-Flow Pressure Differences

The mean fan off Δp at the start of the test, $\Delta p_{0,1}$, was -0.5 The mean fan off Δp at the end of the test, $\Delta p_{0,2}$, was -4.5 The zero flow pressure difference $\Delta p_{0,1+}$ at the start of the test was 1.5 The zero flow pressure difference $\Delta p_{0,1-}$ at the start of the test was -1.5 The zero flow pressure difference $\Delta p_{0,2+}$ at the end of the test was 2.5 The zero flow pressure difference $\Delta p_{0,2+}$ at the end of the test was -3

FOR THE FULL SET OF CALCULATIONS USED TO CALCULATE THE AIR PERMEABILITY RATE, PLEASE GO TO

http://www.hrsservices.co.uk/downloads/air_permeability_calculations.pdf

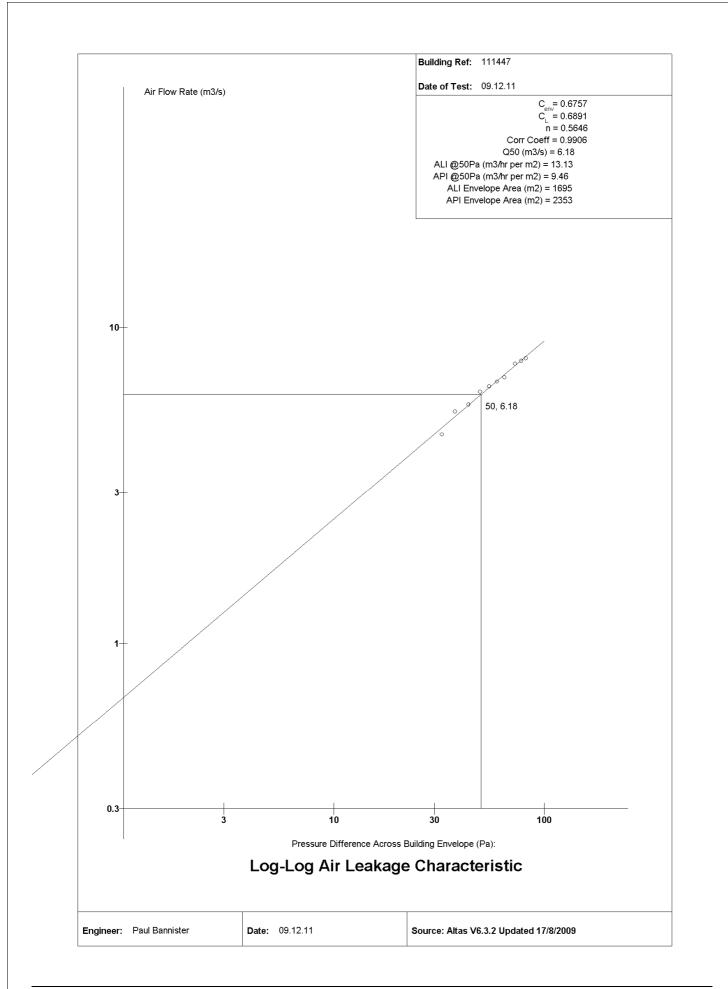

	ent De	<u>tails</u>														
Client	Client Name: BAM Construct UK Ltd							с	lient Cont	act:		Jim N	1cCorma	ck		
Site A So Cl	ing Ref: Address: outh Cam harrington ondon	111447 den Comi a Street		school				н	RS Ref. N	lo:		1114	47			
		ige Te									Tes	t Data F	ase No:	11	1447	
Test Start Time: 17:30																
Test	Finish Ti	me:	18:2	25							Dat	e of Tes	t:	09	.12.11	
														risation:		x
Gene	eral Weat	her Cond	litions:										Depres	surisatio	on: [
	dry	and clou	dy with r	io wind												
<u></u>	asarev	d Para	<u>ппеце</u> Г	<u></u>												
				Parameter	r			S	tart		End					
			-	Parameter Wind Speed					tart 0.4		End 0.6					
			F		d (m/s)	C)		0					_			
			-	Wind Speed External Te Internal Ter	d (m/s) emp (deg np (deg (C)		0 7 1	0.4 7.5		0.6 5.5 15.1		_			
			-	Wind Speer External Te Internal Ter Barometric	d (m/s) emp (deg np (deg (Pressure	C) e (Pa)		0 7 1 1	0.4 7.6 7.5 00700		0.6 5.5 15.1 10090	0				
	Internal te	emp Sens	-	Wind Speed External Te Internal Ter Barometric Fan off Pre	d (m/s) emp (deg np (deg (Pressure	C) e (Pa)		0 7 1 1	0.4 7.5		0.6 5.5 15.1	0				
	Internal to	emp Sens	-	Wind Speed External Te Internal Ter Barometric Fan off Pre	d (m/s) emp (deg np (deg (Pressure ss. Diff. (C) e (Pa)		0 7 1 1	0.4 7.6 7.5 00700		0.6 5.5 15.1 10090	0				
an Speed	Internal to	emp Sens	-	Wind Speed External Te Internal Ter Barometric Fan off Pre	d (m/s) emp (deg np (deg (Pressure ss. Diff. (C) e (Pa)	0	0 7 1 1	0.4 7.6 7.5 00700		0.6 5.5 15.1 10090	0				
			sor Loca	Wind Speed External Te Internal Ter Barometric Fan off Pre ation:	d (m/s) mp (deg np (deg (Pressure ss. Diff. (central	C) e (Pa) Pa)	0 49.5	07711	.4 .6 7.5 00700 .5		0.6 5.5 15.1 10090 -4.5	0				
an Speed	0	0	sor Loca	Wind Speed External Te Internal Ter Barometric Fan off Pre- ation:	d (m/s) mp (deg pressure ss. Diff. (central	C) e (Pa) Pa)	_	0 7 1 1 	.4 .6 7.5 00700 .5	0	0.6 5.5 15.1 10090 -4.5 5	0				
an Speed (Pa)	0 81.5	0 77.5	sor Loca 0 72.5	Wind Speed External Te Internal Ter Barometric Fan off Pre- ation: 0 64.5	d (m/s) mp (deg Pressure ss. Diff. (central 0 59.5	C) e (Pa) Pa) 0 54.5	49.5	0 7 1 1 -0 0 43.5	.4 .6 7.5 00700 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5	0	0.6 5.5 15.1 10090 -4.5 5	0				
an Speed (Pa)	0 81.5	0 77.5	sor Loca 0 72.5	Wind Speed External Te Internal Ter Barometric Fan off Pre- ation: 0 64.5	d (m/s) mp (deg Pressure ss. Diff. (central 0 59.5	C) e (Pa) Pa) 0 54.5	49.5	0 7 1 1 -0 0 43.5	.4 .6 7.5 00700 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5	0	0.6 5.5 15.1 10090 -4.5 5	0				
an Speed (Pa)	0 81.5	0 77.5	sor Loca 0 72.5	Wind Speed External Te Internal Ter Barometric Fan off Pre- ation: 0 64.5	d (m/s) mp (deg Pressure ss. Diff. (central 0 59.5	C) e (Pa) Pa) 0 54.5	49.5	0 7 1 1 -0 0 43.5	.4 .6 7.5 00700 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5 .5	0	0.6 5.5 15.1 10090 -4.5 5	0				

Page 6 of 7 111447 South Camden Community School 09.12.11



AIR PERMEABILITY TEST CERTIFICATE

This is to certify that an air tightness test was carried out at:

SOUTH CAMDEN COMMUNITY SCHOOL CHARRINGTON STREET LONDON NW1 1RG

The test was carried out on 09.12.11 in accordance with ATTMA TS1.

The following air permeability was determined at 50Pa:

9.46m³/(h.m²)

Client: BAM Construct UK Ltd



2587

Name		Position	Signature	Date
Ruth Harrisc	n	Reports Manager	R.Harrison	12.12.2011

To be read in conjunction with relevant test report

Page 7 of 7 111447 South Camden Community School 09.12.11 HRS Services Ltd 81 Burton Road Sheffield S3 8BZ Tel 01142723004 altas@hrsservices.co.uk
