
## 69, Redington Road, London NW3 7RP – Existing Tree Survey works schedule 23/07/15 To be read in conjunction with MWA ref: NW270215.01DW Tree Survey.

#### **LINDEN DESIGNS LTD**



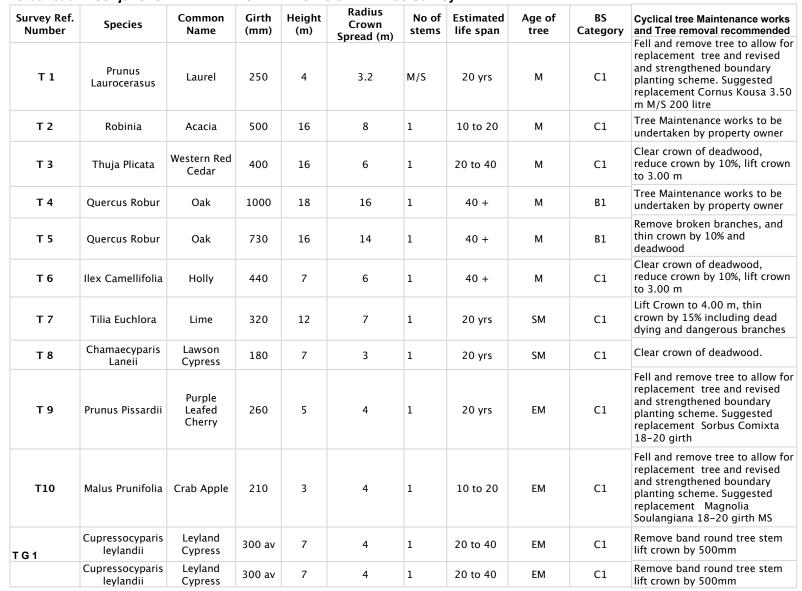

#### LINDEN DESIGNS LTD

### LINDEN DE

	7
	$( \langle \langle \rangle \rangle )$
Jan 1	

# 69, Redington Road, London NW3 7RP – Existing Tree Survey works schedule 23/07/15 To be read in conjunction with MWA ref: NW270215.01DW Tree Survey.

	_									
	Cupressocyparis leylandii	Leyland Cypress	300 av	7	4	1	20 to 40	ЕМ	C1	Remove band round tree stem lift crown by 500mm
KF/ C962(2011)	Betula Pendula	Silver Birch	300 av	8	4	1	20 to 40	EM	C1	Thin crown by 10%. Lift crown by 900 mm. Remove dead dying and dangerous branches
T 11	Prunus Laurocerasus	Laurel	200	5	5	M/S	10 to 15	М	C2	Fell and remove tree to allow for replacement tree and revised and strengthened boundary planting scheme. Suggested replacement Crataegus Monogyna 18–20 girth
	Note 1									All survey details have been taken from MWA survey NW 270215.01DW. Species description and recommended works have been added by LDL and will carried out by Chris Heane Tree Services, and in accordance with BS 3998 and BS 5837
	Note 2									T 11 Prunus Laurocerasus has been added to the schedule, as this plant was not shown on MWA survey referenced above.
	Note 3									The Betula Pendula forming part of TG1 on the survey we understand is subject to a TPO order no KF/C962(2011) and will require permission to carry out works. All remaining trees are subject to conservation area status, and require a 211 agreement prior to works being
	Note 4									undertaken The revised tree survey details are shown on a separate drawing LDL/TWS/15141/01 dated 10.08.15 based on new topographic survey undertaken by Laser surveys Ltd drawing
										no L6934/1 on behalf of the
										Client Shakib and Co

69, Redington Road, London NW3 7RP – Existing Tree Survey works schedule 23/07/15 To be read in conjunction with MWA ref: NW270215.01DW Tree Survey.

	1				
