




D01 (0031 - 2.01) Existing external glazed door Add traditional metal security bars




D02 (0031 - 2.01) New internal glazed partition and door 1800W x 2400H Steel frame Fire rated




D03 (0031 - 2.01) New internal glazed partition and door 1377W x 2400H Steel frame




D04 (0031 - 2.01) New sliding pocket door 1500W x 2040H

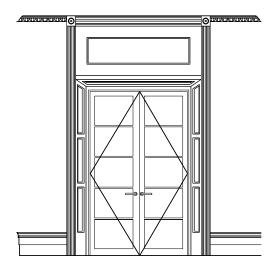

D05 (0031 - 2.02) New internal glazed doors 1327W x 2190H Steel frame Fire rated





D06 (0031 - 2.02) New external sliding door 5220W x 2822H Aluminium frame




D07 (0031 - 2.02) Replacement external sliding door 1804W x 2083H Aluminium frame


REVISION	DATE	DESCRIPTION	PROJECT	No.	DRAWING		REV.	SCALE		
-	-		25 John Street	0031	Proposed Door So		A1 - 1:25	A3 - 1:50	1	
			CLIENT		DRAWING No.	DATE		DRAWN		This and s
			Rhys Jones		5.01	24.01.2024		GRJ		to pro withou














W01 Existing sash window Add traditional metal security bars

W02 New fixed window 996W x 1995H Aluminium frame

W03 Replacement side-hung casement 600W x 995H Aluminium frame

W04 Replacement side-hung casement 1351W x 1505H Aluminium frame

W05 Replacement side-hung casement 1351W x 1505H Aluminium frame

REVISION	DATE	DESCRIPTION	PROJECT No.		DRAWING		REV.	SCALE	
-	-	-	25 John Street	0031	Proposed Window Schedule		Ъ	A1 - 1:25	A3 - 1:50
			CLIENT			DATE	B	DRAWN	CHECKED
			Rhys Jones		5.02	19.01.2024		GRJ	GRJ

