


Construction Management Plan

Camden RoundHouse
Section 26 Environment Addendum

Part of the existing retaining wall to Chalk Farm Road is to be demolished and re-built as part of the access ramp to the development. This work will required limited closure (circa 12 weeks) of the footpath and diversion of the footpath to the other side of the road. The stretch of wall affected is indicated on the plan below. A temporary secure hoarding will be installed along the area shown in green below (Hoarding licence will be applied for separately). Pedestrians will be diverted to the other side of the road for the duration of these works. The hoarding will cover the whole of the pavement to allow for working space.

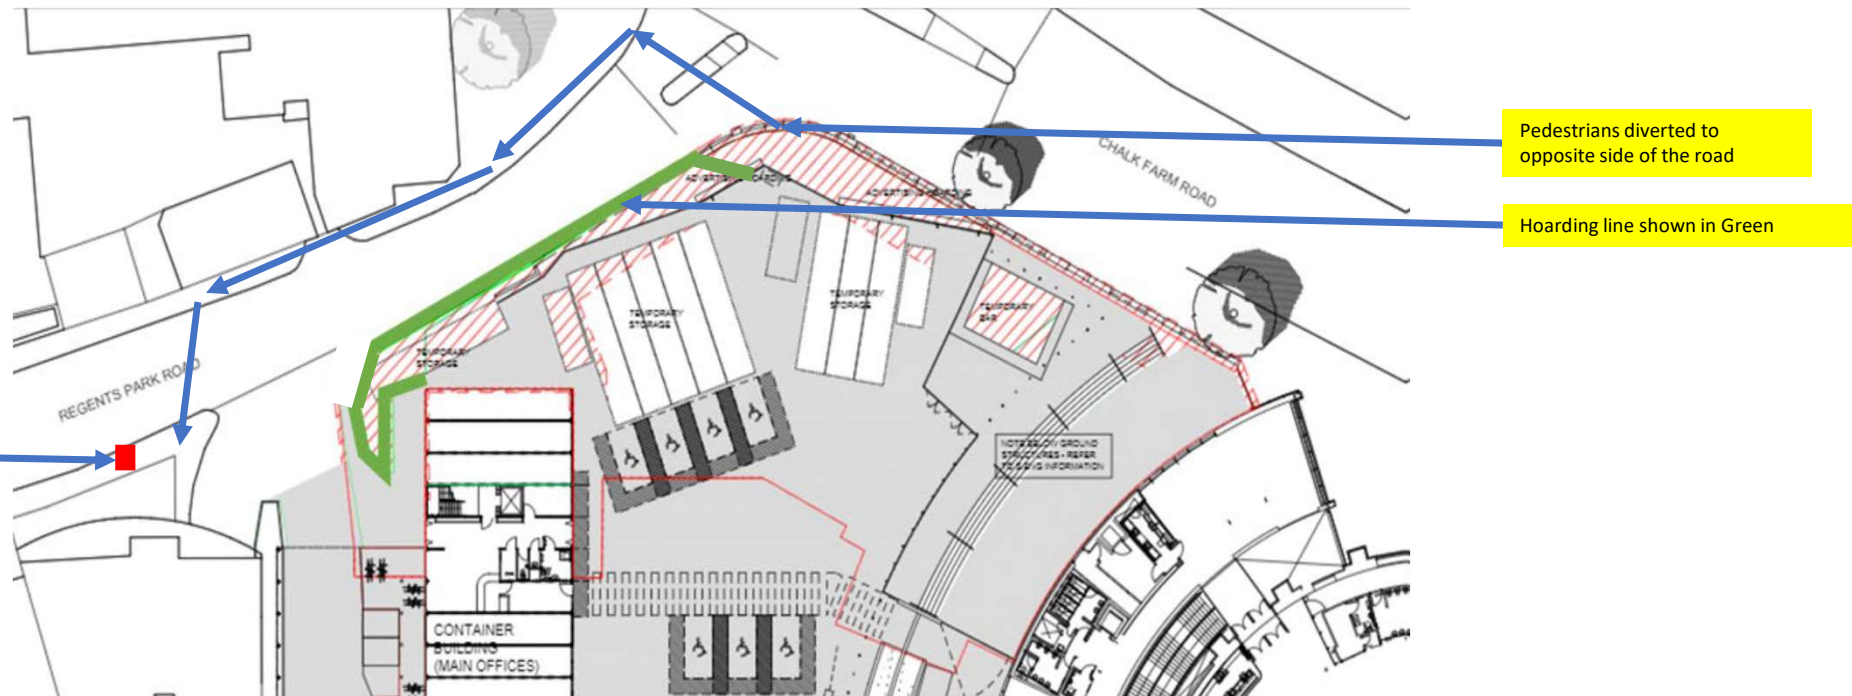

Scaffolding is required along Chalk Farm Road and Regents Park Road,(licences will be applied for separately) the extent of the scaffolding is shown in orange below. All scaffolding will be enclosed with a secure hoarding.



Basic sketch showing scaffolding arrangement on Chalk Farm Road.

