Printed: 09/17/2024

Camden Bridge	start	end
Design	**07/06/24**	**11/10/24**
Procurement	**23/09/24**	**07/01/25**
Purchase TMD	23/09	07/01
Consents	**05/08/24**	**08/11/24**
Fabrication	**15/07/24**	**16/02/25**
Mock up & Lighting	**02/09/24**	**27/09/24**
Civils - Camley Street	**08/11/24**	**16/03/25**
Install Traffic & Pedestrian Manangement Measures	08/11	08/11
Erect Site Hoarding	11/11	12/11
Protection to Footpath	11/11	12/11
Site Clearance	13/11	13/11
Excavate to reduced level behind retaining Wall	14/11	20/11
Install Temporary Earthwork Support	21/11	25/11
Install Piling Platform at Bottom of Excavation	26/11	27/11
Mobilise Piling Rig & Equipment	28/11	28/11
Lift in Piling Rig & Mini Excavator into Excavation	29/11	29/11
Bored Piling	30/11	13/12
Attendance on Piling, Muck Away	14/12	22/12
Xmas Break	23/12	31/12
Lift Out Piling Rig & Mini Excavator from excavation & Demoblise	22/12	22/12
Excavate to RL Piling Plaform & Dispose	02/01	02/01
Install Blinding Concrete	03/01	03/01
Cut Down Piles to Level	04/01	05/01
Integrity Tests for Piles	06/01	06/01
Construct 1200mm Deep Pile Cap	07/01	13/01
Curing	14/01	15/01
Strip Shutters	16/01	16/01
Waterproofing	17/01	17/01
Backfill & Compact Excavation	18/01	18/01
Construct Wall to Half Height	20/01	24/01
Curing	25/01	26/01
Strip Shutters	27/01	27/01
Waterproofing	28/01	28/01
Backfill & Compact Excavation	29/01	29/01
Construct Walls to Full Height	30/01	03/02
Curing	04/02	05/02
Strip Shutters	06/02	06/02
Waterproofing	07/02	07/02
Backfill & Compact Excavation	08/02	08/02
Remove Temorary Works	09/02	10/02
Remove TM & Relocate Hoarding	11/02	11/02
Reinstall TM & Relocate Hoarding	12/02	12/02
Install Portal Steelwork	13/02	14/02
Construct Cover Slab	15/02	19/02
Clear Site	20/02	20/02
Remove TM & Relocate Hoarding	21/02	21/02
Float	22/02	16/03
Civils - Granary Street Phase 1	**11/11/24**	**16/03/25**
Install Piling Platform	11/11	12/11

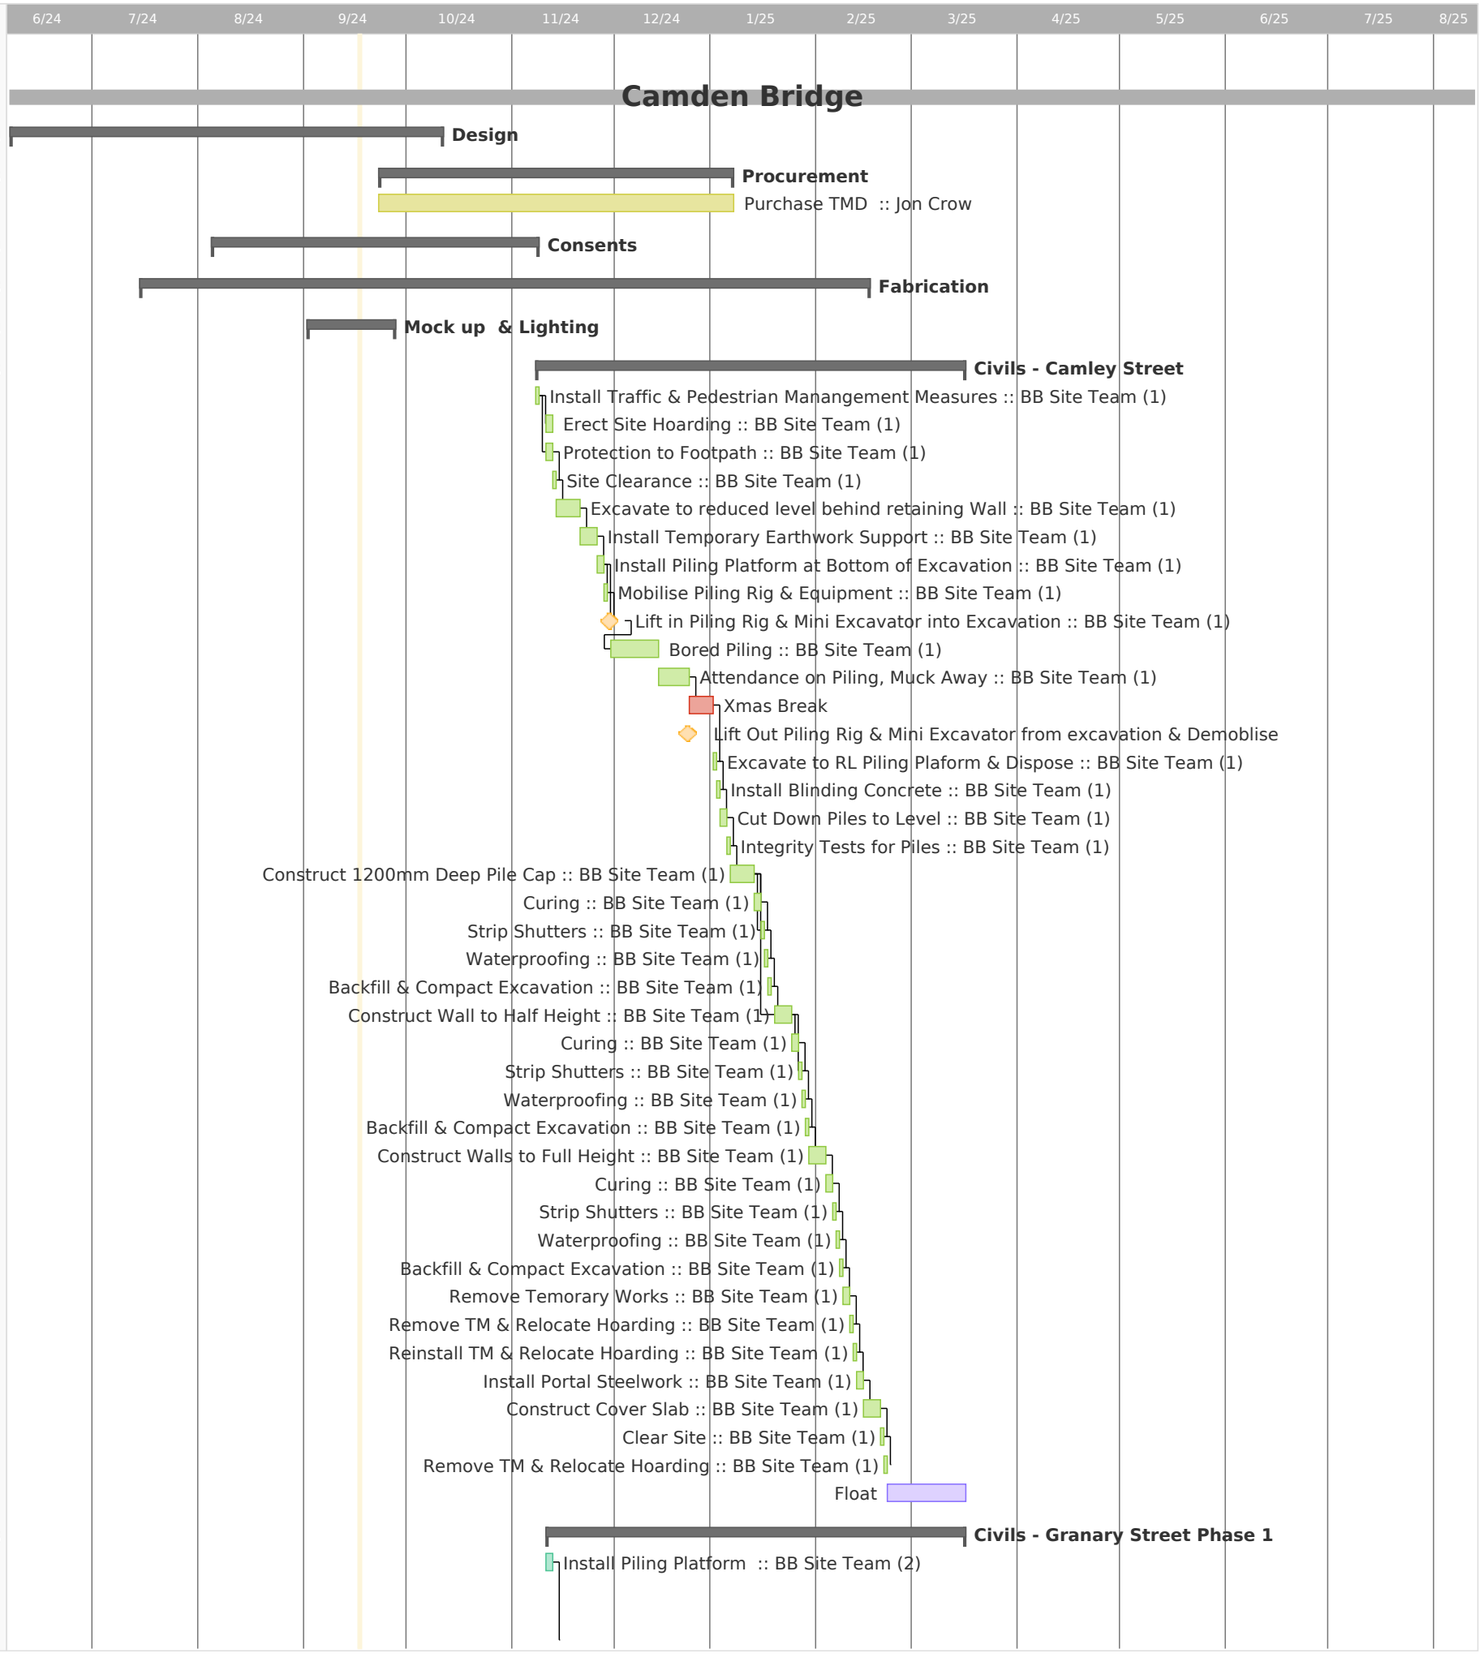

Printed: 09/17/2024

Mobilise Piling Rig & Equipment	13/11	13/11
Bored Piling	14/11	27/11
Attendance on Piling, Muck Away	14/11	27/11
Excavate to RL Piling Plaform & Dispose	28/11	29/11
Install Blinding Concrete	02/12	02/12
Cut Down Piles to Level	03/12	04/12
Integrity Tests for Piles	04/12	04/12
Construct 1200mm Deep Pile Cap	05/12	13/12
Curing	16/12	17/12
Strip Shutters	18/12	18/12
Waterproofing	19/12	19/12
Backfill & Compact Excavation	20/12	20/12
Demobilise Civils Team	21/12	21/12
Install Portal Steelwork	06/01	10/01
Float	29/01	16/03
Bridge Install - Weekend 1	**17/03/25**	**26/04/25**
Set up TW for bridge install	17/03	21/03
Closure of canal	21/03	23/03
Mobilise crane to site and rig	21/03	23/03
Deliver section 1 and install	21/03	21/03
Deliver section 2 and install	22/03	22/03
Deliver centre section and install	23/03	23/03
Site connection	24/03	30/03
Install and tune TMD	24/03	30/03
Touch up and paint	31/03	11/04
Erect Temporary Structure on Granary St	14/04	25/04
Install Lights	31/03	25/04
Open Bridge to public in temporary state	26/04	26/04
Bridge Install - Contingency Weekend 2	**24/03/25**	**26/04/25**
Set up TW for bridge install	24/03	28/03
Closure of canal	28/03	30/03
Mobilise crane to site and rig	28/03	30/03
Deliver section 1 and install	28/03	28/03
Deliver section 2 and install	29/03	29/03
Deliver centre section and install	30/03	30/03
Site connection	31/03	06/04
Install and tune TMD	31/03	06/04
Touch up and paint	07/04	18/04
Erect Temporary Structure on Granary St	21/04	25/04
Install Lights	07/04	25/04
Open Bridge to public in temporary state	26/04	26/04
Civils - Granary Street Phase 2 - Dates to be agreed	**16/03/25**	**12/08/25**
Fabricate approach handrails	16/03	24/05
Fabricate approach structure	16/03	24/05
Paint handrails & Approach structure	25/05	12/06
Install Piling Platform	15/06	16/06
Mobilise Piling Rig & Equipment	17/06	17/06
Bored Piling	18/06	01/07
Attendance on Piling, Muck Away	18/06	01/07
Excavate to RL Piling Plaform & Dispose	02/07	03/07
Install Blinding Concrete	06/07	06/07
Cut Down Piles to Level	07/07	08/07

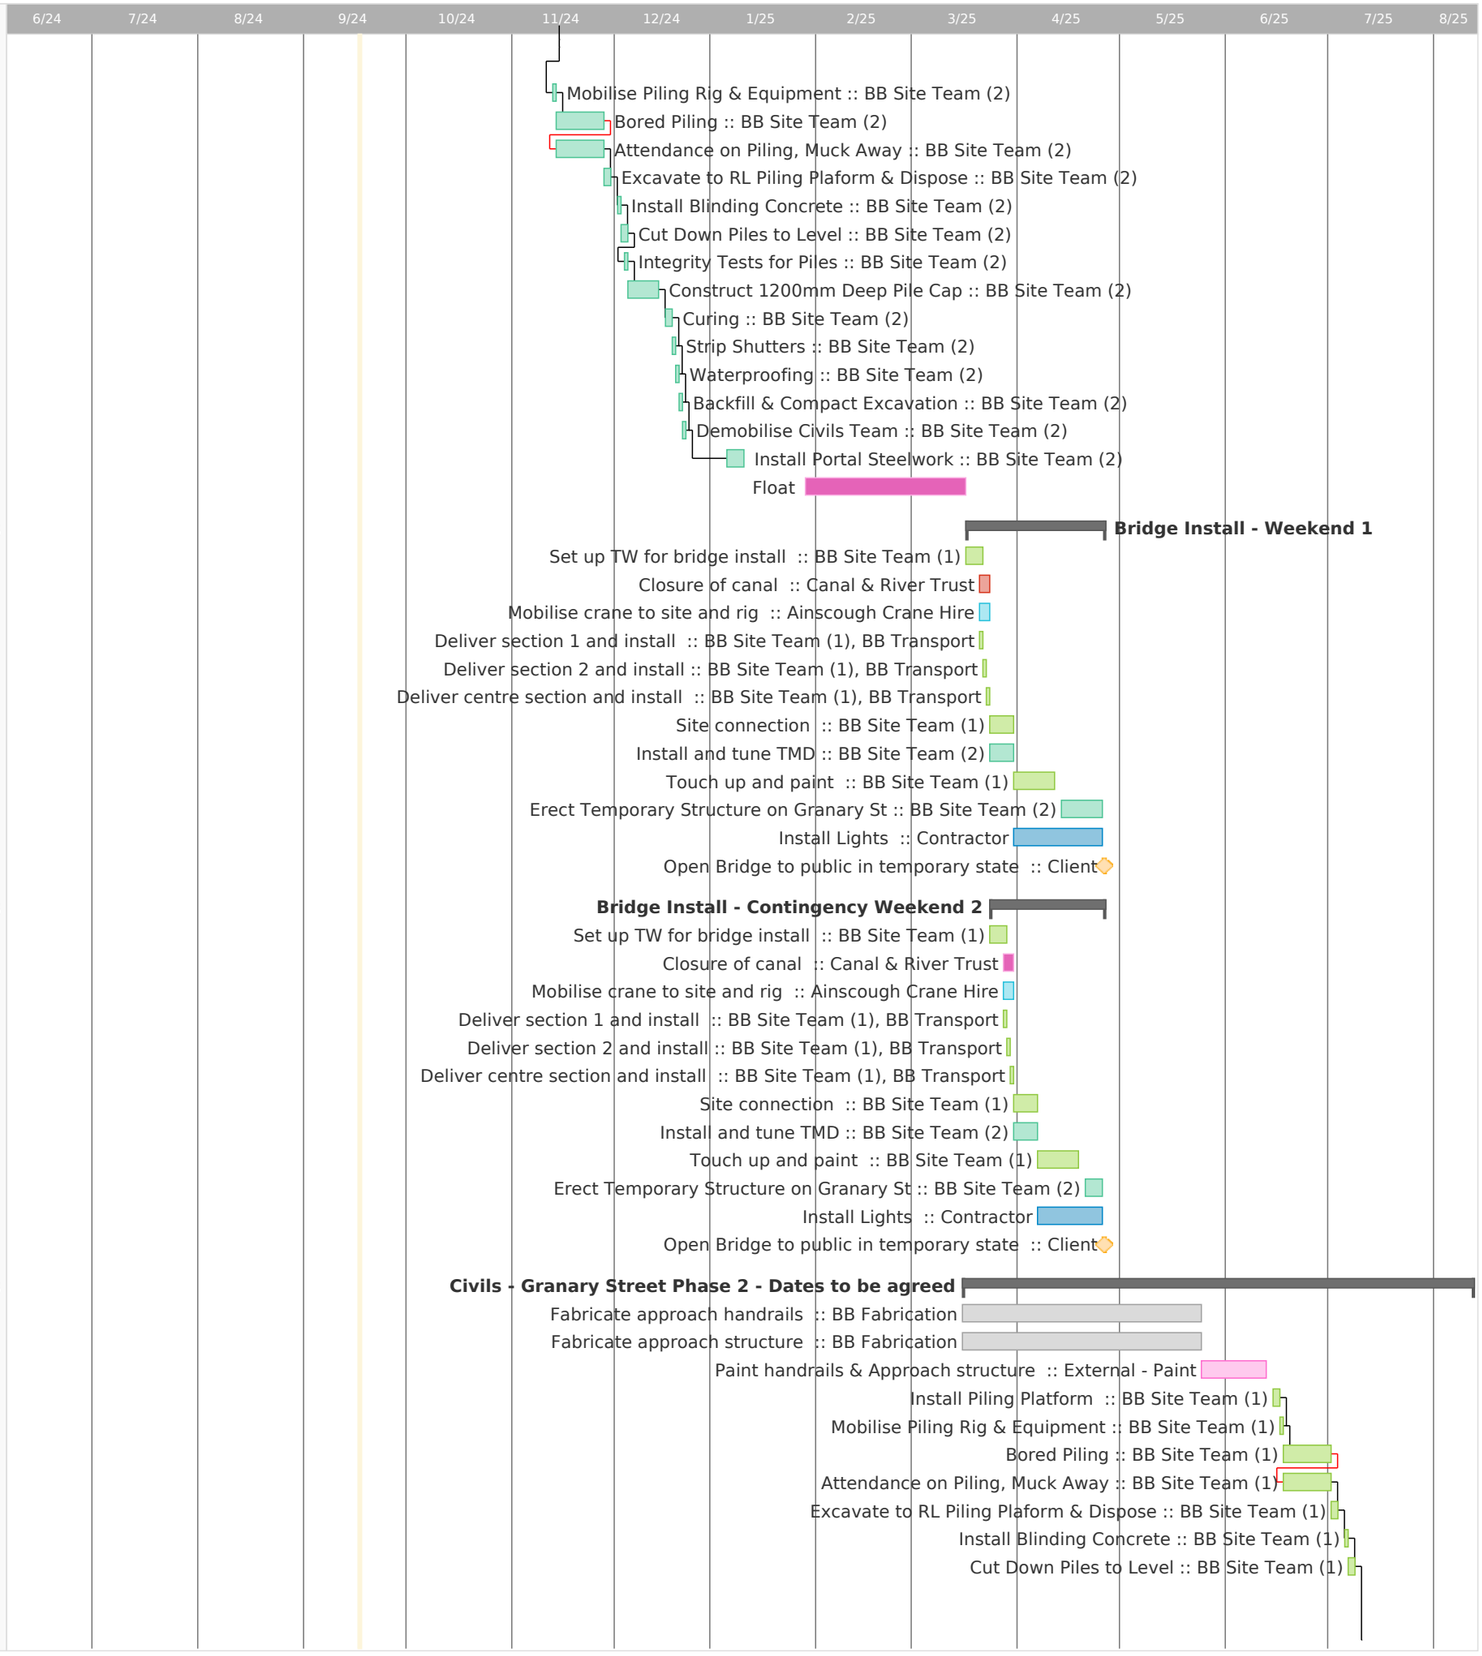

Printed: 09/17/2024

Integrity Tests for Piles	08/07	08/07
Construct Pile Caps 5 No x 700mm deep	09/07	15/07
Curing	16/07	17/07
Strip Shutters	20/07	20/07
Waterproofing	21/07	21/07
Backfill & Compact Excavation	22/07	22/07
Demobilise Civils Team	23/07	23/07
Install Ramp Steelwork	24/07	27/07
Snag	02/08	12/08
Open bridge	08/08	08/08
