Approximate Project Plan for Crown and Anchor London WC2H

Actual | % Complete | Actual (beyond plan) | % Complete (beyond plan)

	ACTIVITY	PLAN START	PLAN DURATION	ACTUAL START	ACTUAL DURATION
1	Scoffold	1	6	0	0
2	Carry out Condition Survey and Report	7	4	0	0
3	Tender Specialist Works Packages	11	4	0	0
4	Place Orders for Specialist Packages	15	2	0	0
5	Paint Strip and clean Terracotta	17	2	0	0
6	Clean Brick Facades 1st to roof	19	3	0	0
7	Restore Masonry,Stone Dressings	22	5	0	0
8	Roof repairs including Lead to Dormers	23	8	0	0
9	Survey Windows for repair and replacement	23	2	0	0
10	Window Manufacture	25	10	0	0
11	Install Windows and complete repairs	35	5	0	0
12	Decorate all windows and Woodwork	40	5	0	0
13	Complete final snagging and checks	45	2	0	0
14	Final inspections and sign off	47	2	0	0
15	Dismantle Scaffold	49	2	0	0
16	Clear Site	51	1	0	0
17	Total Contract period	1	52	0	0
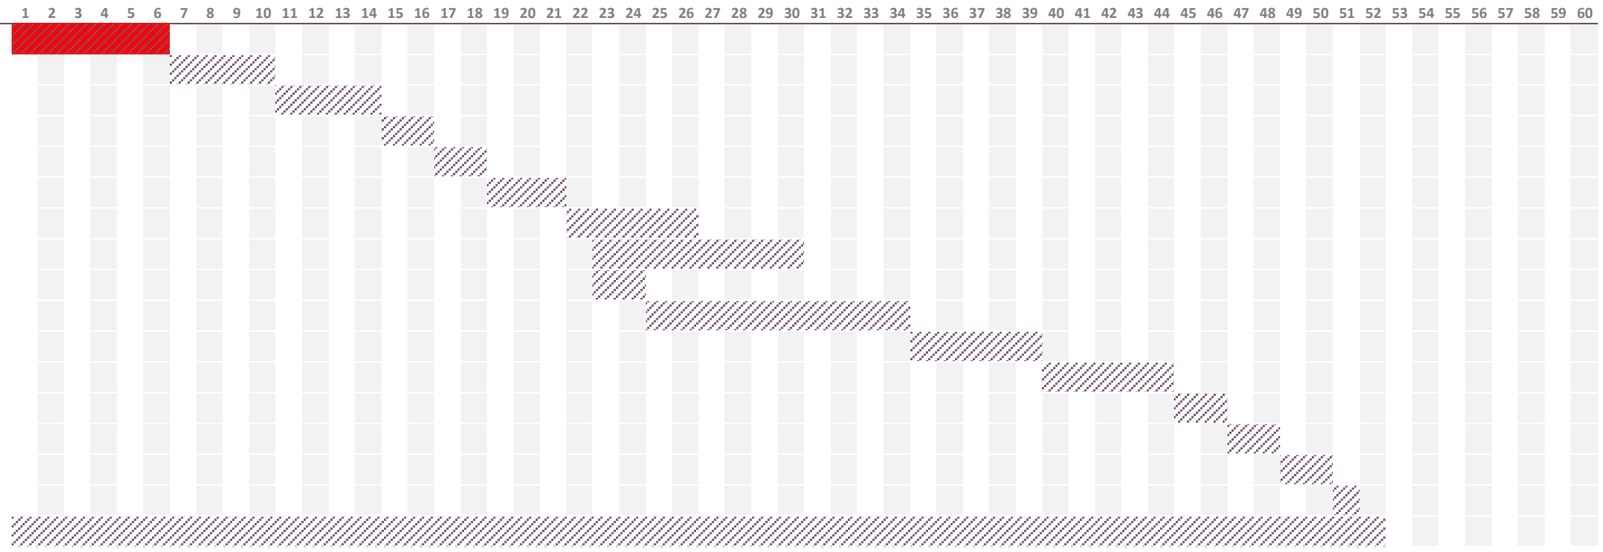
PERIODS
