Camden Mews

None

17/08/2015

Johnny Winter

Line	Name	Start	Duration	Finish
1	Stage K	19/10/2015	48w	16/09/2016
2	Site set up	19/10/2015	2w	30/10/2015
3	Demolish Garage structure, leave slab and entranceway	29/10/2015	1w 1d	05/11/2015
4	Breakout and strip existing structure	06/11/2015	1w 1d	13/11/2015
5	Brace existing structure	16/11/2015	1w	20/11/2015
6	Remove Rear wall	20/11/2015	4d	25/11/2015
7	Remove roof structure	24/11/2015	3d	26/11/2015
8	Reemove 1 meter ground cover under existing building	26/11/2015	4d	01/12/2015
9	Underpin all structure boundary walls and Garden (not existing area Garage)	26/11/2015	6w 3d	11/01/2016
10	Remove main basement spoil	08/01/2016	1w	14/01/2016
11	Drainage connection	08/01/2016	2w	21/01/2016
12	Basement Slab	18/01/2016	3d	20/01/2016
13	Ground floor slab / beam	20/01/2016	4d	25/01/2016
14	Garage slab remove and clear	25/01/2016	3d	27/01/2016
15	Underpin Garage area	26/01/2016	3w	15/02/2016
16	Remove garage basement spoil	11/02/2016	3d	15/02/2016
17	Basement slab	16/02/2016	1w	22/02/2016
18	Ground floor slab	23/02/2016	1w	29/02/2016
19	Repair brickwork openings/ new rear wall reconstruction	22/02/2016	6w	01/04/2016
20	Brickwork repairs / Insulation	21/03/2016	4w	15/04/2016
21	Roof structure covering / finishes	28/03/2016	7w	13/05/2016
22	Envelope windows / doors	02/05/2016	7w	17/06/2016
23	Partitions 1st fix	16/05/2016	5w	17/06/2016
24	Stair	30/05/2016	4w 1d	27/06/2016
25	services 1st fix	20/06/2016	5w	22/07/2016
26	ceilings linings / finishes	04/07/2016	6w 3d	17/08/2016
27	bathroom carcass/	21/06/2016	4w 4d	22/07/2016
28	Bathroom finishes	18/07/2016	3w	05/08/2016
29	joinery installation	18/07/2016	5w 2d	23/08/2016
30	kitchen /manufacture and install	13/06/2016	11w 3d	31/08/2016
31	Services & finishes	25/07/2016	6w 1d	05/09/2016
32	Commisioning	22/08/2016	3w	09/09/2016

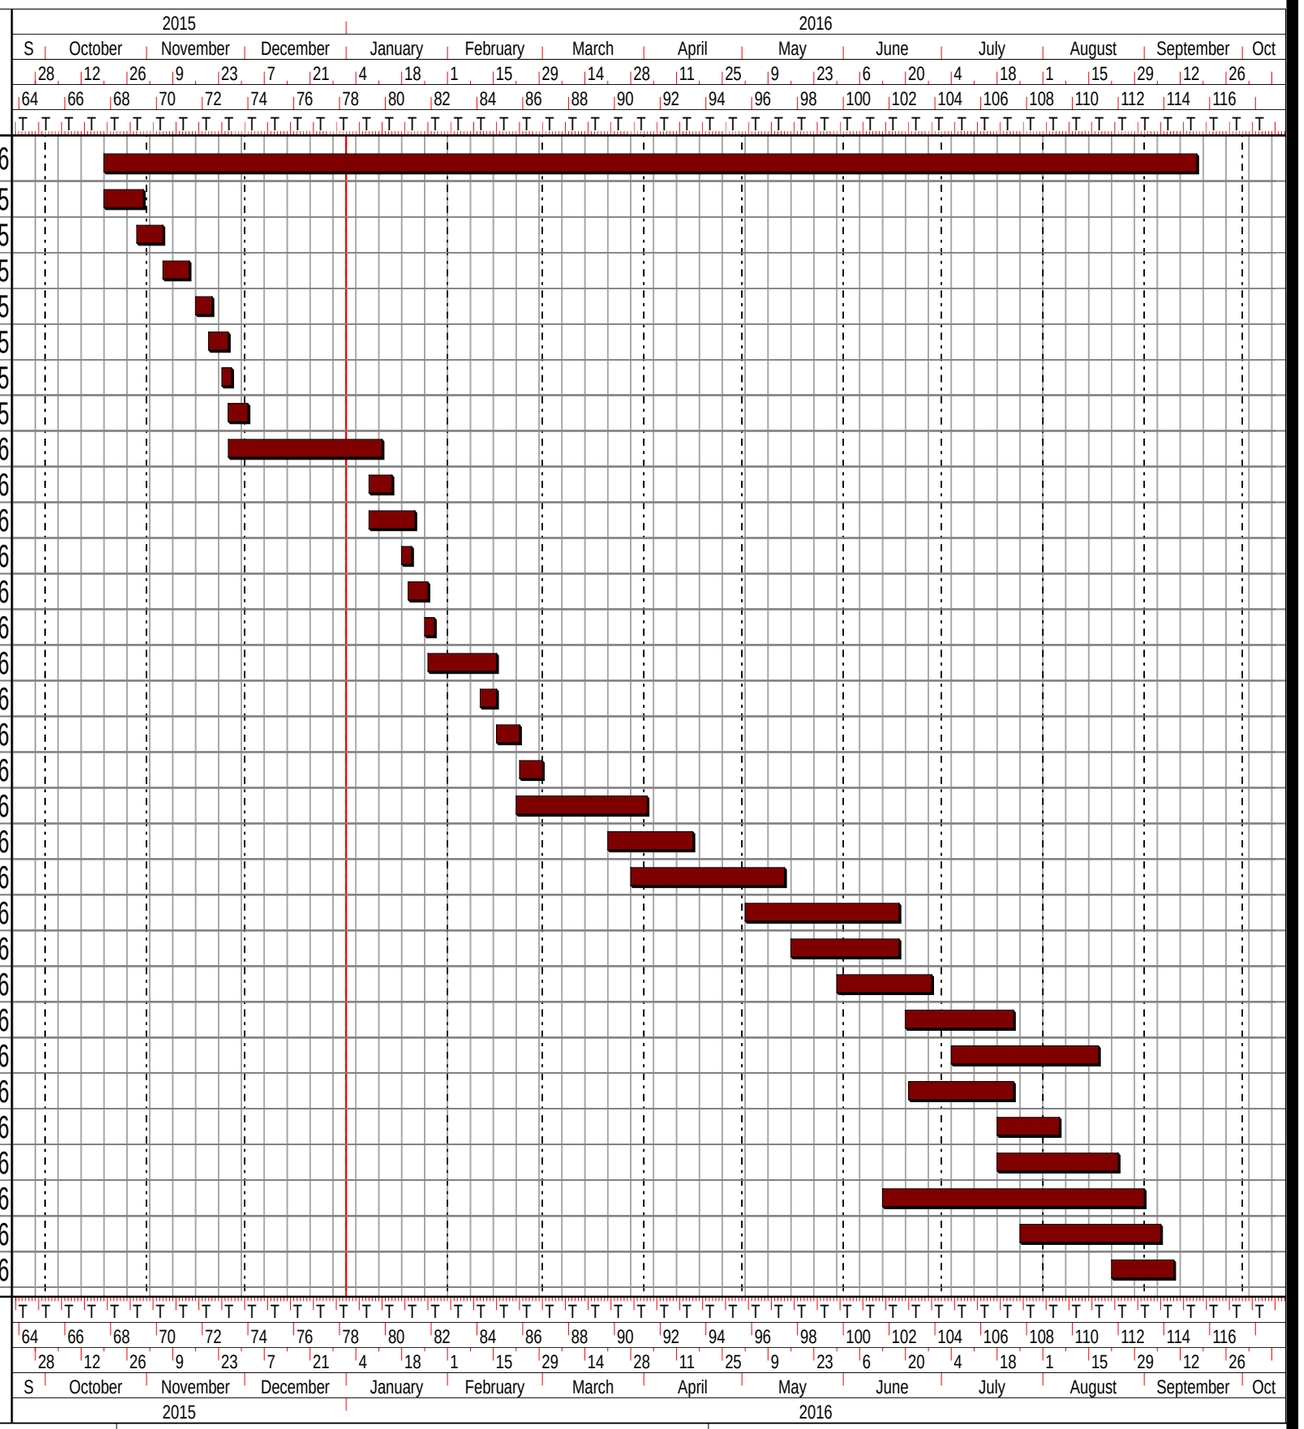

Line | Name | Start | Duration | Finish

Drawn by: | Dwg No. | Revision No. | Notes:

Project Ref. E:\85_CAMDEN_MEWS\00 FILING\0 Admin files\0.03 Programmes\150112_Camden Mews.pp

Planned by Asta Powerproject
