# APPENDIX A

PROGRAMME

# GOSH

24/02/2016 GARDINER & THEOBALD Richard Turner

| Line | Name | Duration | Start | Finish |
|---|---|---|---|---|
| 1 | CONTRACT PROCUREMENT | 8w 2d | 09 Dec 15 | 18 Feb 16 |
| 2 | Confirm Scope and Approach to Contract | 7w | 18 Dec 15 | 18 Feb 16 |
| 3 | Compile Contract Documents | 3w | 18 Jan 16 | 05 Feb 16 |
| 4 | Confirm Contract Framework | 7w | 18 Dec 15 | 18 Feb 16 |
| 5 | Issue Design Documentation | 7w | 18 Dec 15 | 18 Feb 16 |
| 6 | Erith Review Documentation | 7w | 18 Dec 15 | 18 Feb 16 |
| 7 | Erith provide initial design, methodology and programme | 7w | 18 Dec 15 | 18 Feb 16 |
| 8 | Erith Prepare AIP | 3w | 01 Feb 16 | 19 Feb 16 |
| 9 | Erith Issue AIP to Camden | 1w | 22 Feb 16 | 26 Feb 16 |
| 10 | Camden AIP Approval Period | 5w | 29 Feb 16 | 05 Apr 16 * |
| 11 | Design Team refine scope, including tower crane, BWIC, fair faced concrete | 7w | 18 Dec 15 | 18 Feb 16 |
| 12 | Engineer check reinforcement quantities | 7w | 18 Dec 15 | 18 Feb 16 |
| 13 | CMP Development | 4w 4d | 18 Jan 16 | 18 Feb 16 |
| 14 | Issue CMP to Camden | 1d | 19 Feb 16 | 19 Feb 16 |
| 15 | CMP Approval Period | 5w | 22 Feb 16 | 29 Mar 16 * |
| 16 | BCP | 4d | 16 Feb 16 | 19 Feb 16 |
| 17 | BCB Approval Period | 5w 1d | 22 Feb 16 | 30 Mar 16 * |
| 18 | Finalise Contract Sum | 1w 4d | 08 Feb 16 | 18 Feb 16 |
| 19 | Design team review proposals | 1w 4d | 08 Feb 16 | 18 Feb 16 |
| 20 | Client Approval | 1d | 19 Feb 16 | 19 Feb 16 * |
| 21 | Party Wall Award (G& T) | 7w 3d | 22 Feb 16 | 15 Apr 16 * |
| 22 | Issue LOI | 1d | 19 Feb 16 | 19 Feb 16 * |
| 23 | Execute Contract | 1w | 15 Feb 16 | 19 Feb 16 * |
| 24 | Procure Tower Crane (CTL260) | 31w 1d | 22 Feb 16 | 03 Oct 16 |
| 25 | Apply for Thames Water Discharge License | 1d | 22 Feb 16 | 22 Feb 16 |
| 26 | Thames Water Approval Period | 8w | 23 Feb 16 | 20 Apr 16 |
| 27 | Carry out Delapidation Survey | 2d | 22 Feb 16 | 23 Feb 16 |
| 28 | Check Survey Settling Out Stations and Set up Grid-Line Site Control | 1w | 22 Feb 16 | 26 Feb 16 * |
| 29 | Agree Building Monitoring Regime | 1w | 22 Feb 16 | 26 Feb 16 |
| 30 | Set up Building Monitoring Retro-Targets | 1w | 29 Feb 16 | 04 Mar 16 * |
| 31 | Agree Environmental Monitoring (Real Time for Noise / Dust and Vibration) and Order Equipment | 1w | 22 Feb 16 | 26 Feb 16 |
| 32 | Set up Real Time Monitoring Equipment | 1w | 29 Feb 16 | 04 Mar 16 * |
| 33 | Develop Detailed Design and Methodology | 5w 1d | 20 Jan 16 | 04 Mar 16 * |
| 34 | Agree Movement Monitoring for Temporary Works with Swanton | 1w | 07 Mar 16 | 11 Mar 16 * |
| 35 | Procure Steel for Gantry | 8w | 07 Mar 16 | 04 May 16 |
| 36 | Procure Steel for Horizontal Propping | 12w | 07 Mar 16 | 02 Jun 16 |
| 37 | Hoarding and Gantry License Application | 1d | 22 Feb 16 | 22 Feb 16 |
| 38 | Hoarding and Gantry License Application Period | 4w | 23 Feb 16 | 21 Mar 16 |
| 39 | Pedestrian Crossing Application - Guilford Street | 1d | 22 Feb 16 | 22 Feb 16 |
| 40 | Pedrestrian Cross-Over Application Period | 4w | 23 Feb 16 | 21 Mar 16 |
| 41 | Street Light Removal Application | 1d | 22 Feb 16 | 22 Feb 16 |
| 42 | Street Lighting Removal Application Period | 4w | 23 Feb 16 | 21 Mar 16 |
| 43 | Street Lighting Removal | 2d | 22 Mar 16 | 23 Mar 16 |
| 44 | Install Temporary Lighting | 1w | 17 Mar 16 | 23 Mar 16 |
| 45 | TTRO / Parking Suspensions Application | 1d | 22 Feb 16 | 22 Feb 16 |
| 46 | TTRO / Parking Suspensions Application Period | 4w | 23 Feb 16 | 21 Mar 16 |
| 47 | Procure CFA Piling Rig for Machine Platform Piles | 12w | 07 Mar 16 | 02 Jun 16 |
| 48 | Procure Plunge Piles | 12w | 07 Mar 16 | 02 Jun 16 |
| 49 | Procure Raking Prop Steel | 3w | 07 Mar 16 | 29 Mar 16 * |
| 50 | Procure Attenuation Tank | 9w 3d | 22 Feb 16 | 29 Apr 16 |
| 51 | Procure Gantry Steel | 6w 2d | 07 Mar 16 | 21 Apr 16 |
| 52 | Commence Monitoring Regime For 1 Month | 4w | 01 Mar 16 | 30 Mar 16 |
| 53 | Sheet Pile Procurement Period | 8w | 07 Mar 16 | 04 May 16 |
| | Obtain TBS | | | |
| 54 | WORKS ON SITE START | 1d | 29 Mar 16 * | 29 Mar 16 |
| 55 | Install Temporary Site Welfare | 1w | 18 Mar 16 * | 24 Mar 16 |
| 56 | Move Hoarding Millman Street | 2w | 31 Mar 16 | 13 Apr 16 |
| 57 | Adjust Hoarding Millman Mews | 2w | 31 Mar 16 | 13 Apr 16 |
| 58 | Install Hoarding Guilford Place | 2w | 31 Mar 16 | 13 Apr 16 |
| 59 | Install Hoarding Guilford Street | 2w | 31 Mar 16 | 13 Apr 16 |
| 60 | Close Guilford Street South Side | 3d | 14 Apr 16 | 18 Apr 16 |
| 61 | Remove Paving Slabs / Service Protection / Place Concrete Road | 1w | 19 Apr 16 | 25 Apr 16 |
| 62 | Install Hoarding around Road Closure | 1w | 26 Apr 16 | 03 May 16 |
| 63 | Install Plinths for Gantry | 1w | 04 May 16 | 10 May 16 |
| 64 | Install Gantry Steel | 3w | 11 May 16 | 01 Jun 16 |
| 65 | Install Road Lighting on Gantry | 1w | 02 Jun 16 | 08 Jun 16 |
| 66 | Install Welfare on Gantry and Access (Stairs and Walkways) | 1w | 09 Jun 16 | 15 Jun 16 |
| 67 | Construct Concrete Drive Through under Gantry | 2w | 16 Jun 16 | 29 Jun 16 |
| 68 | Construct Site Entrance / Exit Gates | 1w | 30 Jun 16 | 06 Jul 16 * |
| 69 | Remove Welfare from Site | 1w | 16 Jun 16 | 22 Jun 16 * |
| 70 | Install Raking Props to Site Perimeter | 8w | 30 Mar 16 | 25 May 16 |
| 71 | Saw Cutting to Site Perimeter | 8w | 13 Apr 16 | 09 Jun 16 |
| 72 | Excavate and Place Piling Mat to the Attenuation Tank | 3d | 04 May 16 | 06 May 16 |
| 73 | Install Sheet Piles to the Attenuation Tank Area | 1w | 09 May 16 | 13 May 16 |
| 74 | Excavate and Install Attenuation Tank | 1w | 16 May 16 | 20 May 16 |
| 75 | Install Piling Platform for perimeter Piling | 1w | 27 Apr 16 | 04 May 16 |
| 76 | Break out and Fill Basement | 1w | 21 Apr 16 | 27 Apr 16 |
| 77 | Install Sheet Piles around Site Perimeter | 8w | 09 May 16 | 04 Jul 16 |
| 78 | Weld Sheet Piles | 8w | 17 May 16 | 12 Jul 16 |
| 79 | Install Plunge Piles for Machine Gantry | 2w | 03 Jun 16 | 16 Jun 16 |
| 80 | Install Plant Platform | 2w | 17 Jun 16 | 30 Jun 16 |
| 81 | Cut Down Sheet Piles | 7w 2d | 24 May 16 | 14 Jul 16 |
| 82 | Construct Capping Beam | 5w | 17 Jun 16 | 21 Jul 16 |
| 83 | Install High Level Propping to Capping Beam | 4w | 05 Jul 16 | 01 Aug 16 |
| 84 | Break out Ground Floor Slab | 4w | 08 Jul 16 | 04 Aug 16 |
| 85 | Excavation to the Intermediate Propping Level - Sheet Piles to be welded | 5w | 25 Jul 16 | 26 Aug 16 |
| 86 | Install the Intermediate Propping Level | 4w | 17 Aug 16 | 14 Sep 16 |
| 87 | Excavation to Formation Level - Sheet Piles to be welded | 5w | 07 Sep 16 | 11 Oct 16 |
| 88 | Construct Crane Base | 1w | 30 Sep 16 | 06 Oct 16 |
| 89 | Install Tower Crane | 2d | 07 Oct 16 | 10 Oct 16 |
| 90 | Construct Drainage Layer at Formation Level | 4w | 30 Sep 16 | 27 Oct 16 |
| 91 | Construct Lower Basement Slab Including Drianage | 6w | 11 Oct 16 | 21 Nov 16 |
| 92 | Construct Cores and Verts between Lower Basement level and Intermediate Slab Level | 4w | 04 Nov 16 | 01 Dec 16 |
| 93 | Install Intermediate Slab | 4w | 25 Nov 16 | 22 Dec 16 |
| 94 | Remove Intermediate and Ground Floor Slab Temporary Works | 3w | 13 Dec 16 | 16 Jan 17 |
| 95 | Construct Cores and Verts between Intermediate Slab and Ground Floor Slab | 4w | 10 Jan 17 | 06 Feb 17 |
| 96 | Construct Ground Floor Slab | 4w | 27 Jan 17 | 23 Feb 17 |
| 97 | Snagging | 4w | 03 Feb 17 | 02 Mar 17 |
| 98 | Complete Basement Box | 1d | 02 Mar 17 | 02 Mar 17 |

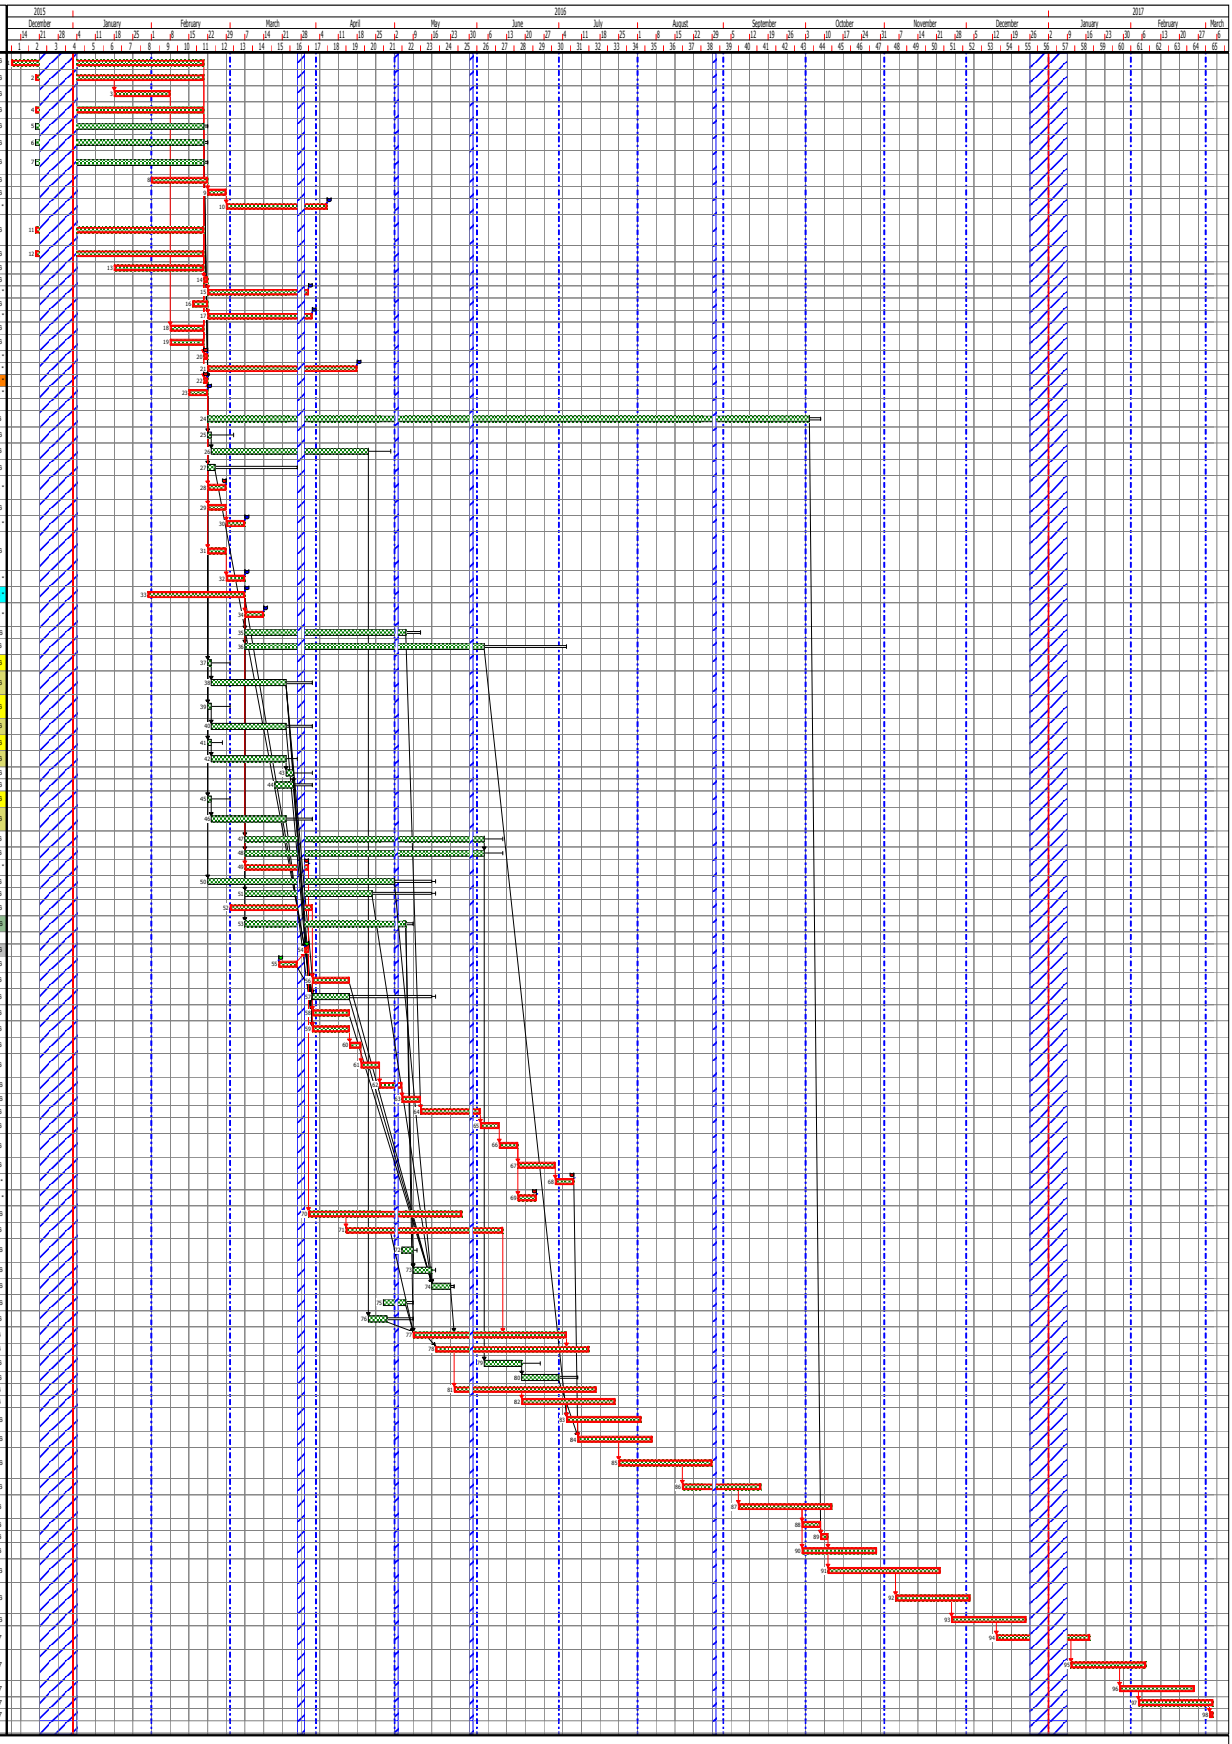


Trades Contractor
Default

| Drawn by: Planner - Chart Properties | Dwg No. 00001 | Revision No. A | Notes: Comment - Chart Properties |
|---|---|---|---|

Project Ref. C:\Users\callumjenkins\Desktop\Mark Ups and File Dump\Great Ormond Street Basement TRY 2 18 02 16.pp

Planned by Asta Powerproject
