SCHNEIDER DESIGNERS
architecture. design. interiors

OUTLINE PROGRAMME

For information only

Plan | Actual | % Complete | Actual (beyond plan) | % Complete (beyond plan)
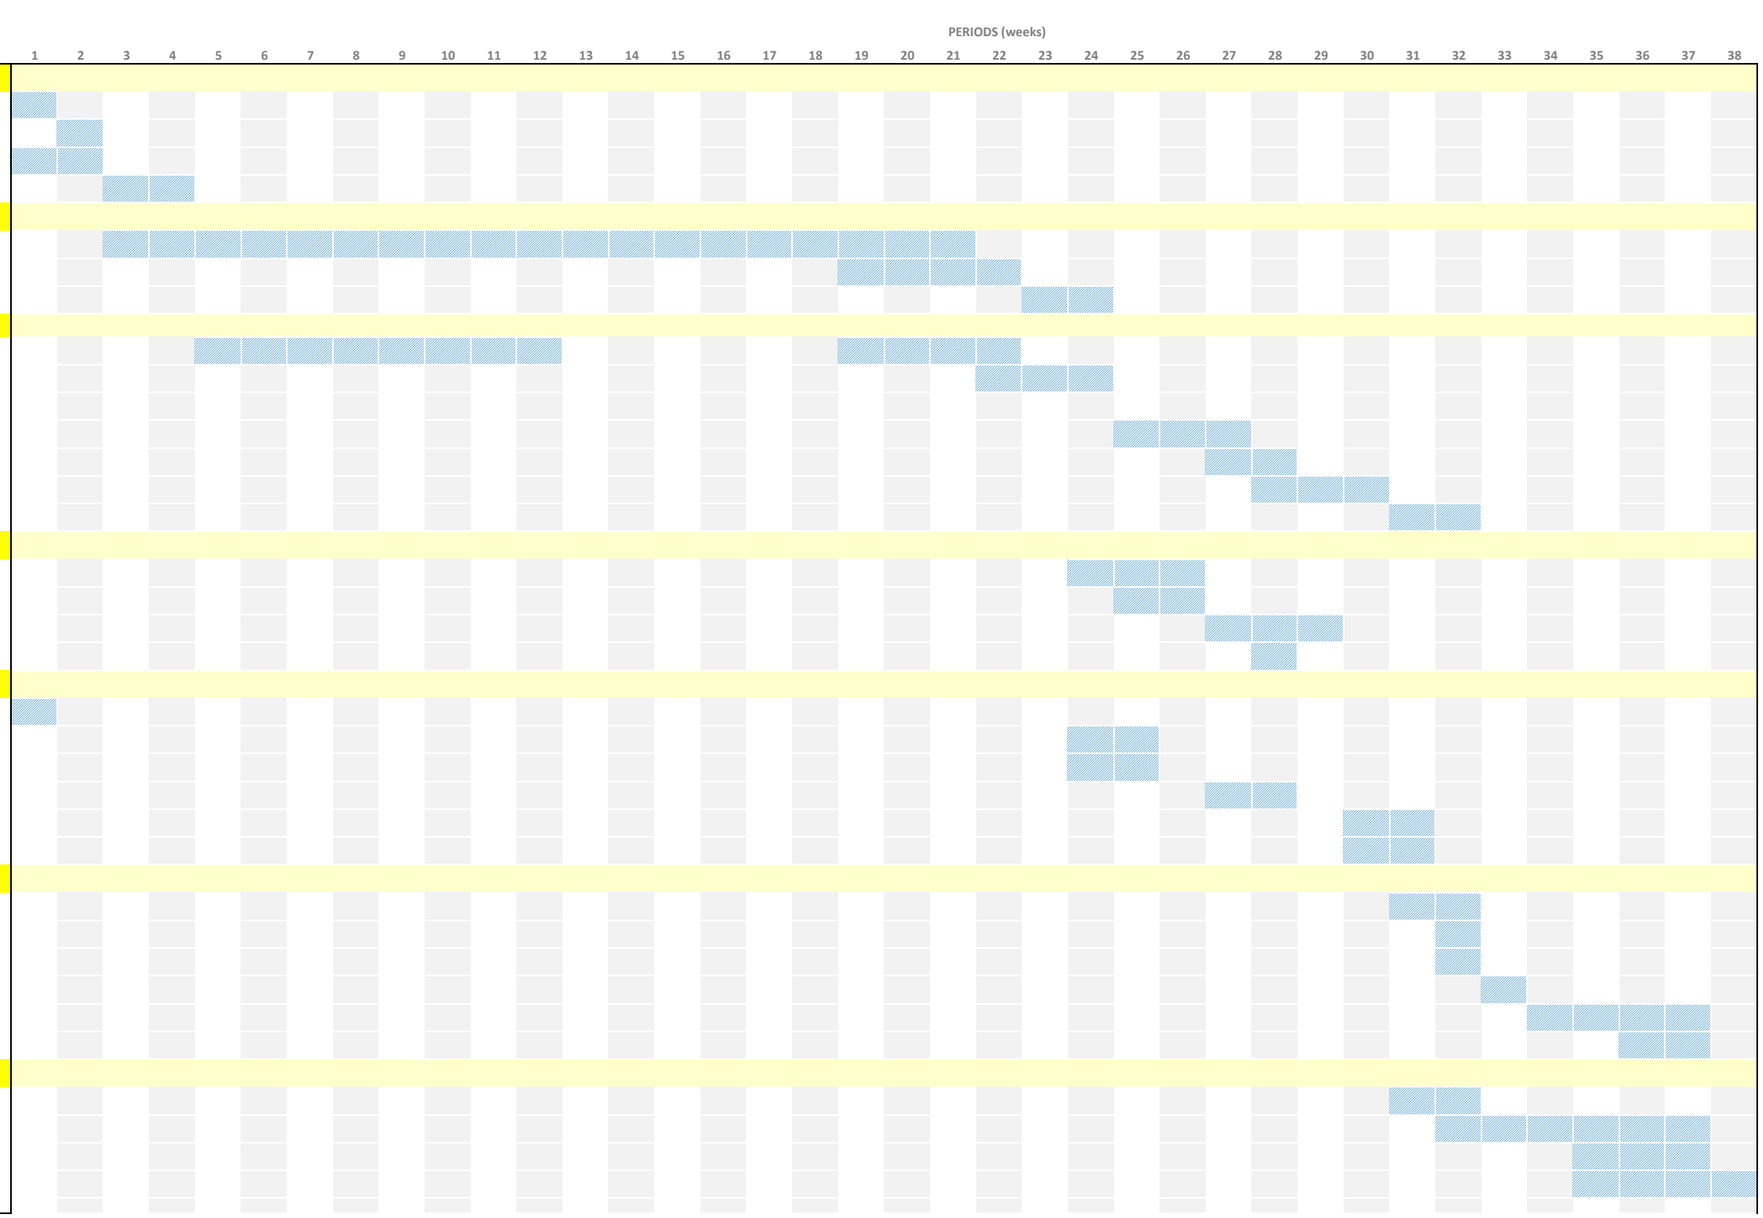
		DURATION (days)	START	END
1	**MOBILISATION & DEMOLITION**	**37.5**		
1.1	Site set up	6		
1.2	Hoarding erecting	8		
1.3	Preparation / demolition works before excavation	9.5		
1.4	Excavation works, prepartion for underpinning	14		
2	**SUPERSTRUTURE WORKS**	**156**		
2.1	Underspinning, reinforcement works	114		
2.2	New slab	30		
2.3	Drainage works, sump pump fittings	12		
3	**NEW WORKS**	**153**		
3.1	Structural alterations including new beams	78		
3.2	Tanking of walls and floor	18		
3.3	Construction of new partition walls, insulation			
3.4	Construction of new ceiling, insulation	18		
3.5	Skimmimg plaster throughout	12		
3.6	Tiling	15		
3.7	Flooring installation	12		
4	**PLUMBING**	**52.5**		
4.1	Hot/cold water connection 1st fix	18		
4.2	Installation of UFH	12		
4.3	Hot/cold water connection 2nd fix	18		
4.4	Connection to boiler and test	4.5		
5	**ELECTRICS**	**65**		
5.1	Temporary installation	5		
5.2	1st Fix power	12		
5.3	1st Fix lighting	12		
5.4	Connection to electric board and test	12		
5.5	2nd Fix power	12		
5.6	2nd Fix lighting	12		
6	**JOINERY**	**64**		
6.1	Intallation of new doors	12		
6.2	Installation of architraves	6		
6.3	Installation of skirtings	6		
6.4	Installation of windows	7		
6.5	Installation of joinery units	24		
6.6	Fitting of kitchen units	9		
7	**FINISHES**	**89**		
7.1	Preparation of walls and ceilings, etc	12		
7.2	Internal decoration	33		
7.3	External decoration	20		
7.4	Finishes	24		
	TOTAL	**38**	**Weeks**	
		9.5	**Months**
