ID	Task Name	Duratio	Start	Finish	Resource Nan
0	**10 PARKWAY, CAMDEN**	**157 da**	**Mon 31/10/1**	**Mon 19/06/1**	
1					
2	**ENABLING WORKS**	**45 day**	**Mon 31/10/16**	**Fri 13/01/17**	
3	Service Isolations	5 days	Mon 31/10/16	Fri 04/11/16	Capri
4	Site Surveys	10 day	Mon 31/10/16	Fri 11/11/16	
5	Scaff / Crane Licences	10 day	Mon 31/10/16	Fri 11/11/16	
6	Site set up / temps	10 day	Mon 31/10/16	Fri 11/11/16	Capri
7	Cleaning to side alley	15 day	Mon 07/11/16	Fri 25/11/16	Rentokil
8	Strip out (all except balustrade) to 3rd floor	10 days	Mon 07/11/16	Fri 18/11/16	Lantern
9	Ditto 2nd Floor	10 day	Mon 21/11/16	Fri 02/12/16	Lantern
10	Ditto 1st Floor	10 day	Mon 05/12/16	Fri 16/12/16	Lantern
11	Isolate & remove main plant	20 day	Mon 07/11/16	Fri 02/12/16	Capri
12	Temp waterproofing	10 day	Mon 21/11/16	Fri 02/12/16	
13	Sand blast steel decking	20 day	Mon 28/11/16	Fri 23/12/16	
14	Intumescent paint (white) to steels	15 days	Mon 12/12/16	Fri 13/01/17	
15					
16	**FIT OUT WORKS**	**117 da**	**Mon 09/01/17**	**Mon 19/06/17**	
17	**Roof & External Works**	**117 da**	**Mon 09/01/17**	**Mon 19/06/17**	
18	Scaffolding to Front Façade	10 day	Mon 09/01/17	Fri 20/01/17	
19	Scaffold Hire Period	106 da	Mon 23/01/17	Mon 19/06/17	
20	New waterproofing to roof	10 day	Mon 16/01/17	Thu 26/01/17	
21	Roof plant support structure	10 day	Sun 22/01/17	Thu 02/02/17	
22	New roof plant (crane lifts)	15 day	Mon 30/01/17	Fri 17/02/17	
23	Complete roofing works	10 day	Mon 20/02/17	Fri 03/03/17	
24	Window install	44 day	Mon 30/01/17	Thu 30/03/17	
25	Repair / Replace pigeon protection	9 days	Mon 06/03/17	Wed 05/04/17	
26	Renew gas cupboard doors	5 days	Fri 10/03/17	Thu 16/03/17	
27	Entrance canopy steelwork	7 days	Thu 16/03/17	Fri 24/03/17	
28	Video entry panel	10 day	Wed 22/03/17	Tue 04/04/17	
29	External wiring for sign / lights	2 days	Mon 27/03/17	Tue 28/03/17	
30	Entrance canopy cladding	3 days	Thu 30/03/17	Mon 03/04/17	
31	Repairs to lead flashing at parapet	20 days?	Mon 03/04/17	Fri 28/04/17	
32	Front Elevation repairs	39 day	Mon 03/04/17	Thu 25/05/17	
33	External Decorations	11 day	Fri 26/05/17	Fri 09/06/17	
34	New gates	30 day	Mon 27/03/17	Fri 05/05/17	
35	Tactile paving	5 days	Wed 12/04/17	Tue 18/04/17	
36	Cycle Area	10 day	Mon 08/05/17	Fri 19/05/17	
37	Strike scaffold	5 days	Tue 13/06/17	Mon 19/06/17	
38					
39	**Office Areas**	**80 day**	**Wed 11/01/17**	**Mon 01/05/17**	

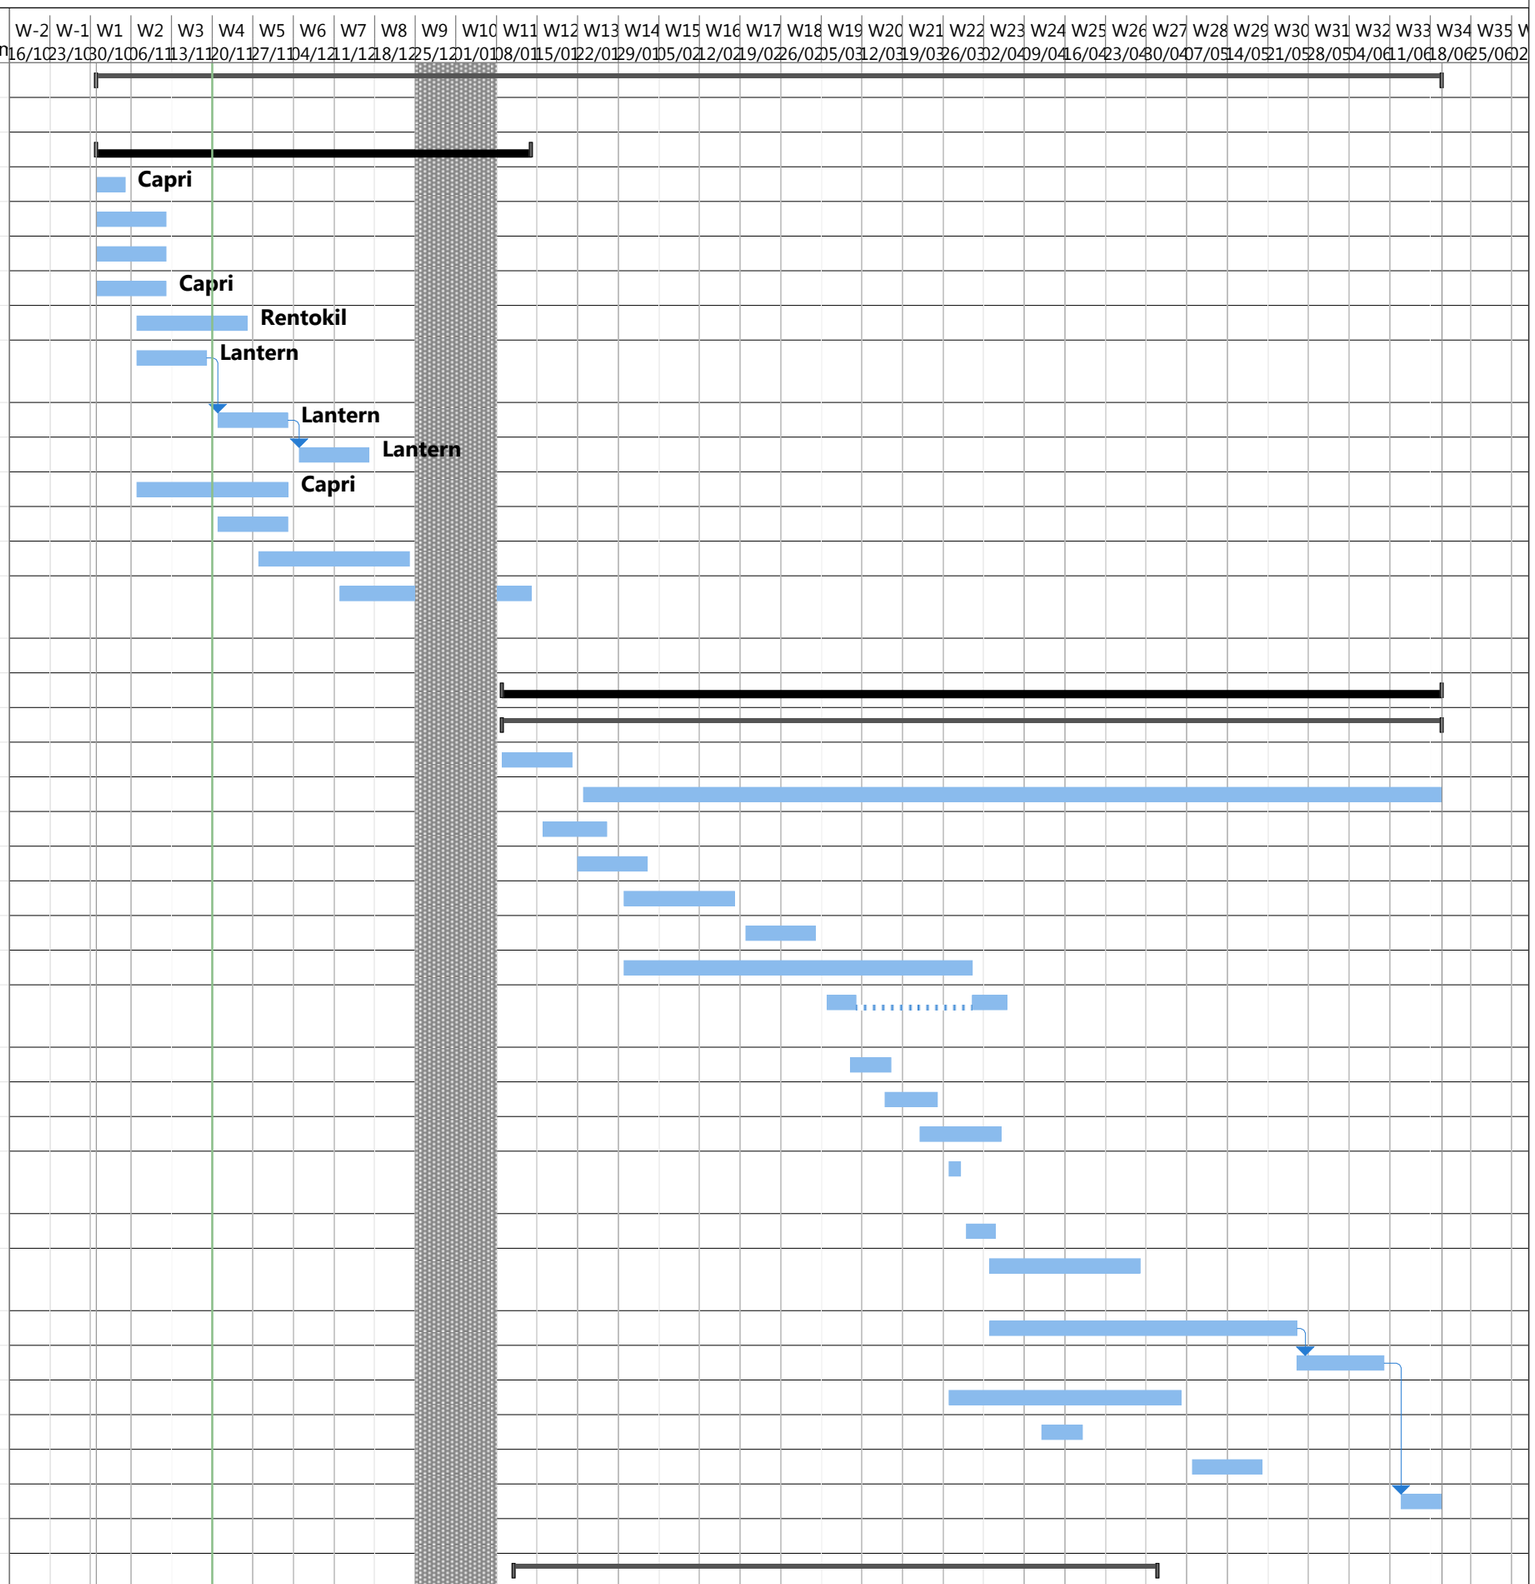
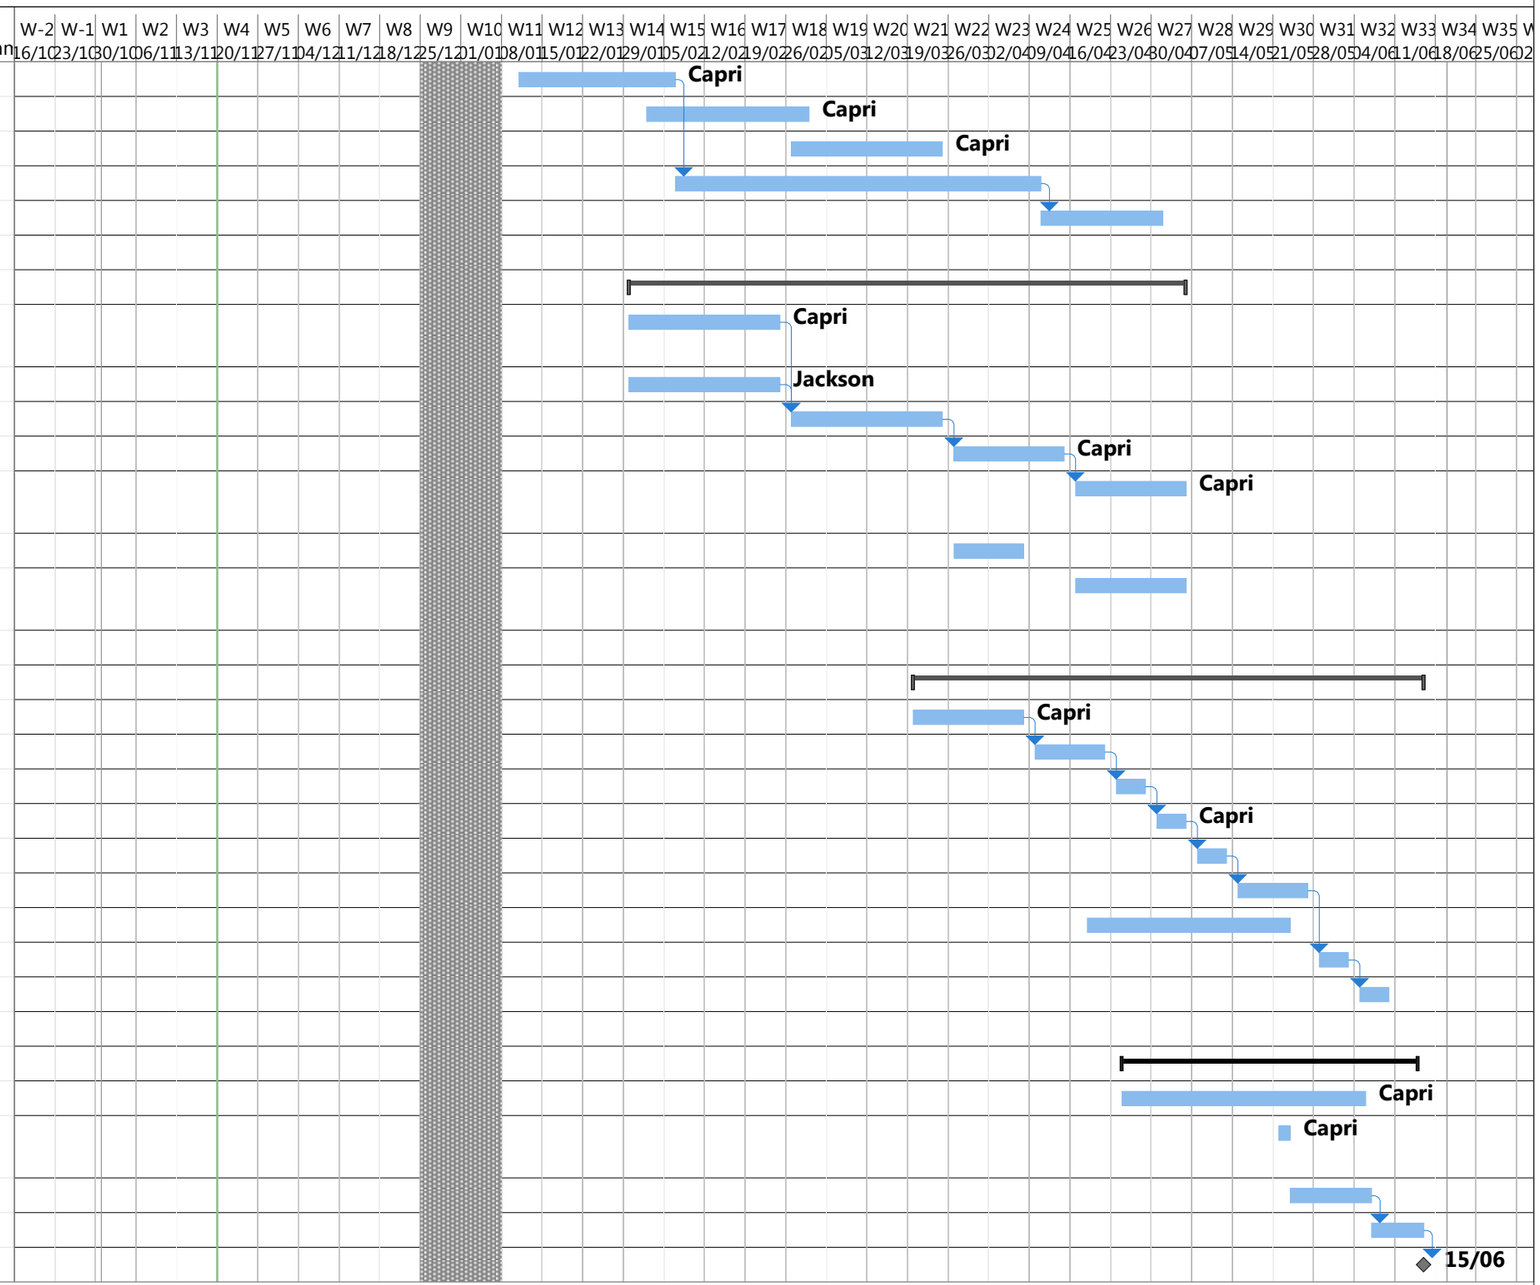
ID	Task Name	Duratio	Start	Finish	Resource Nan
40	M & E to office ceilings FF	20 day	Wed 11/01/17	Mon 06/02/17	Capri
41	M & E to office ceilings 2F	20 day	Thu 02/02/17	Wed 01/03/17	Capri
42	M & E to office ceilings 3F	20 day	Mon 27/02/17	Fri 24/03/17	Capri
43	Wall finishes FF-3F	45 day	Tue 07/02/17	Mon 10/04/17	
44	New carpets to offices	15 day	Tue 11/04/17	Mon 01/05/17	
45					
46	**Toilets, Lifts & Stairs**	**70 day**	**Mon 30/01/17**	**Fri 05/05/17**	
47	M & E First fix to toilets / stairs	20 days	Mon 30/01/17	Fri 24/02/17	Capri
48	Refurbish existing lifts	20 day	Mon 30/01/17	Fri 24/02/17	Jackson
49	Ceiling Wall & Floor finishes	20 day	Mon 27/02/17	Fri 24/03/17	
50	Sanitary Ware	15 day	Mon 27/03/17	Fri 14/04/17	Capri
51	M & E Second fix to toilets / stairs	15 days	Mon 17/04/17	Fri 05/05/17	Capri
52	Metal balustrading to stairs	10 day	Mon 27/03/17	Fri 07/04/17	
53	Stair floor finish / nosings / protect	15 days	Mon 17/04/17	Fri 05/05/17	
54					
55	**Reception Area**	**64 day**	**Mon 20/03/17**	**Thu 15/06/17**	
56	M & E First fix to recept area	15 day	Mon 20/03/17	Fri 07/04/17	Capri
57	Wall & Ceiling finishes	10 day	Mon 10/04/17	Fri 21/04/17	
58	Decorations	5 days	Mon 24/04/17	Fri 28/04/17	
59	Lighting	5 days	Mon 01/05/17	Fri 05/05/17	Capri
60	Ceiling mesh to recept area	5 days	Mon 08/05/17	Fri 12/05/17	
61	Floor finishes reception	10 day	Mon 15/05/17	Fri 26/05/17	
62	Reception Desk	25 day	Wed 19/04/17	Tue 23/05/17	
63	Mirror panelling	5 days	Mon 29/05/17	Fri 02/06/17	
64	Signage	5 days	Mon 05/06/17	Fri 09/06/17	
65					
66	**General**	37 day	Tue 25/04/17	Wed 14/06/17	
67	Testing & Commissioning	30 day	Tue 25/04/17	Mon 05/06/17	Capri
68	Remove welfare facilities	2 days	Mon 22/05/17	Tue 23/05/17	Capri
69	Builders Clean	10 day	Wed 24/05/17	Tue 06/06/17	
70	Final Snagging	7 days	Wed 07/06/17	Thu 15/06/17	
71	Handover	0 days	Thu 15/06/17	Thu 15/06/17
