Keats Grove
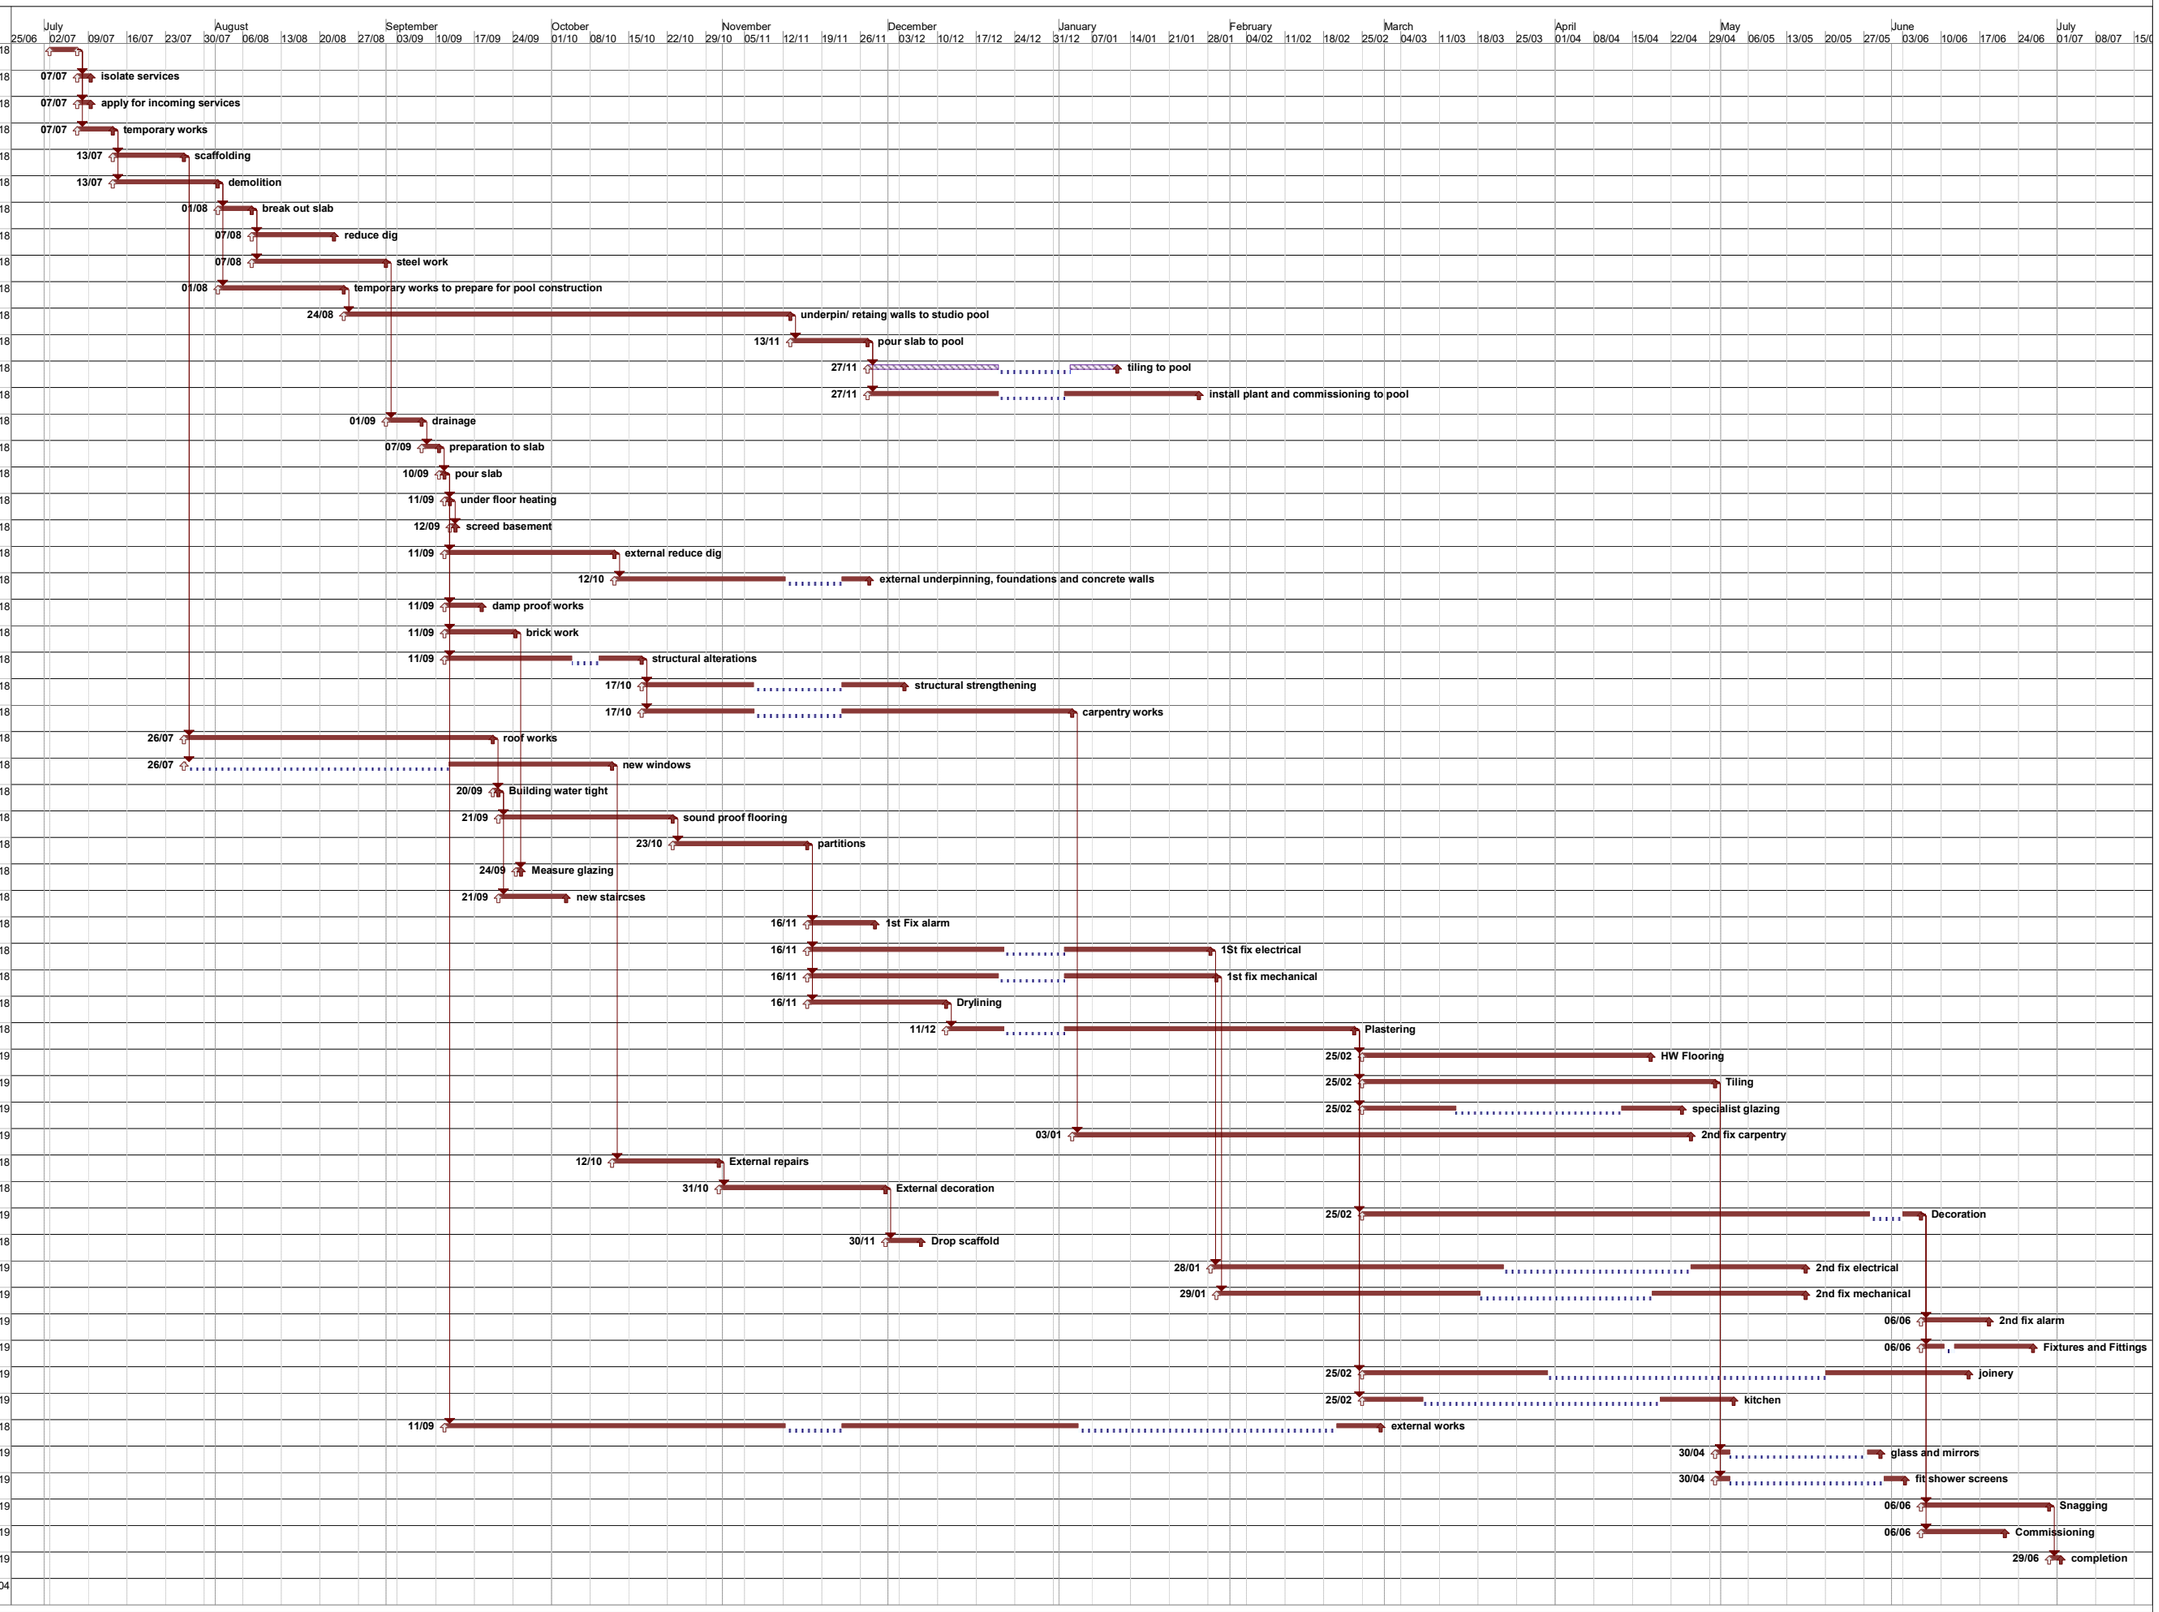
ID	Task Name	Start
1	site set up	Mon 02/07/18
2	isolate services	Sat 07/07/18
3	apply for incoming services	Sat 07/07/18
4	temporary works	Sat 07/07/18
5	scaffolding	Fri 13/07/18
6	demolition	Fri 13/07/18
7	break out slab	Wed 01/08/18
8	reduce dig	Tue 07/08/18
9	steel work	Tue 07/08/18
10	temporary works to prepare for pool construction	Wed 01/08/18
11	underpin/ retaing walls to studio pool	Fri 24/08/18
12	pour slab to pool	Tue 13/11/18
13	tiling to pool	Tue 27/11/18
14	install plant and commissioning to pool	Tue 27/11/18
15	drainage	Sat 01/09/18
16	preparation to slab	Fri 07/09/18
17	pour slab	Mon 10/09/18
18	under floor heating	Tue 11/09/18
19	screed basement	Wed 12/09/18
20	external reduce dig	Tue 11/09/18
21	external underpinning, foundations and concrete walls	Fri 12/10/18
22	damp proof works	Tue 11/09/18
23	brick work	Tue 11/09/18
24	structural alterations	Tue 11/09/18
25	structural strengthening	Wed 17/10/18
26	carpentry works	Wed 17/10/18
27	roof works	Thu 26/07/18
28	new windows	Thu 26/07/18
29	Building water tight	Thu 20/09/18
30	sound proof flooring	Fri 21/09/18
31	partitions	Tue 23/10/18
32	Measure glazing	Mon 24/09/18
33	new staircses	Fri 21/09/18
34	1st Fix alarm	Fri 16/11/18
35	1St fix electrical	Fri 16/11/18
36	1st fix mechanical	Fri 16/11/18
37	Drylining	Fri 16/11/18
38	Plastering	Tue 11/12/18
39	HW Flooring	Mon 25/02/19
40	Tiling	Mon 25/02/19
41	specialist glazing	Mon 25/02/19
42	2nd fix carpentry	Thu 03/01/19
43	External repairs	Fri 12/10/18
44	External decoration	Wed 31/10/18
45	Decoration	Mon 25/02/19
46	Drop scaffold	Fri 30/11/18
47	2nd fix electrical	Mon 28/01/19
48	2nd fix mechanical	Tue 29/01/19
49	2nd fix alarm	Thu 06/06/19
50	Fixtures and Fittings	Thu 06/06/19
51	joinery	Mon 25/02/19
52	kitchen	Mon 25/02/19
53	external works	Tue 11/09/18
54	glass and mirrors	Tue 30/04/19
55	fit shower screens	Tue 30/04/19
56	Snagging	Thu 06/06/19
57	Commissioning	Thu 06/06/19
58	completion	Sat 29/06/19
59		Mon 06/09/04
