ID	Task Name	Duration	Start	Finish
0	**Haverstock Hill Programme Version : CF 001**	**420 days**	**Wed 13/12/17**	**Mon 19/08/19**
1	**Haverstock Hill Programme**	**420 days**	**Wed 13/12/17**	**Mon 19/08/19**
2	**Demolition, site clearance.**	**28 days**	**Wed 13/12/17**	**Thu 01/02/18**
3	Façade Retention	3 wks	Wed 13/12/17	Mon 15/01/18
4	Demolition of superstructure	2 wks	Tue 16/01/18	Mon 29/01/18
5	Ground probing for piling	1 day	Tue 30/01/18	Tue 30/01/18
6	Pilling rig matt	2 days	Wed 31/01/18	Thu 01/02/18
7	**Construction Phase**	**401 days**	**Mon 22/01/18**	**Mon 19/08/19**
8	**Contig wall Pilling and capping beam & Substructure**	**349 days**	**Mon 22/01/18**	**Wed 05/06/19**
9	Piling to contig wall & Bearing Piles	12 wks	Mon 22/01/18	Fri 13/04/18
10	Piling demobilisation	1 day	Mon 16/04/18	Mon 16/04/18
11	Excavate and trim contig wall piles	15 days	Tue 17/04/18	Mon 07/05/18
12	Integrity tests	15 days	Tue 17/04/18	Mon 07/05/18
13	Capping beams to retaining wall	5 wks	Tue 24/04/18	Mon 28/05/18
14	Temporary works	5 days	Tue 29/05/18	Mon 04/06/18
15	Excavate basement	3 wks	Thu 14/06/18	Wed 04/07/18
16	Underfloor Drainage and Incoming Services Provisi	10 days	Thu 05/07/18	Wed 18/07/18
17	Trim bearing piles and construct piling caps	3 wks	Thu 21/06/18	Wed 11/07/18
18	Basement slab	4 wks	Thu 05/07/18	Wed 01/08/18
19	Liner Walls	4 wks	Thu 19/07/18	Wed 15/08/18
20	Basement walls and Columns	4 wks	Thu 09/08/18	Wed 05/09/18
21	Ground floor slab	20 days	Thu 30/08/18	Wed 26/09/18
22	Basement Waterproofing	2 wks	Mon 29/10/18	Fri 09/11/18
23	Blockwork to basement	5 wks	Mon 12/11/18	Fri 14/12/18
24	Staircase Basement to ground floor	1 wk	Thu 27/09/18	Wed 03/10/18
25	**Super structure and external shell**	**216 days**	**Thu 26/07/18**	**Wed 05/06/19**
26	Tower crane installation	0 days	Thu 26/07/18	Thu 26/07/18
27	RC Columns and Core Grnd to 1st	2 wks	Mon 24/09/18	Fri 05/10/18
28	1st Floor slab	1 wk	Mon 08/10/18	Fri 12/10/18
29	Staircase Ground to 1st	1 wk	Mon 15/10/18	Fri 19/10/18
30	RC Frame subcontractor de-mobilise and clear site	1 wk	Mon 22/10/18	Fri 26/10/18
31	Scaffold erect	1 wk	Mon 29/10/18	Fri 02/11/18
32	Load bearing masonry first floor, incl scaffold adaptation	3 wks	Mon 29/10/18	Fri 16/11/18
33	PCC planks	2 days	Mon 19/11/18	Tue 20/11/18
34	Loadbearing masonry second floor, incl. scaffold adaptation	3 wks	Wed 21/11/18	Tue 11/12/18
35	PCC planks	2 days	Wed 12/12/18	Thu 13/12/18
36	Loadbearing masonry third floor, incl. scaffold adaptation	4 wks	Fri 14/12/18	Wed 23/01/19
37	Pcc planks	2 days	Thu 24/01/19	Fri 25/01/19
38	Metsec to Penthouse	2 wks	Mon 28/01/19	Fri 08/02/19
39	Screed to basement	3 days	Mon 17/12/18	Wed 19/12/18
40	screed to ground floor	3 days	Fri 14/12/18	Tue 18/12/18
41	Screed to first floor	3 days	Mon 28/01/19	Wed 30/01/19
42	Screed to second floor	3 days	Mon 11/02/19	Wed 13/02/19
43	Screed to third floor	3 days	Thu 14/02/19	Mon 18/02/19
44	screed to fourth floor	2 days	Mon 18/03/19	Tue 19/03/19
45	Lightweight cladding and render	25 days	Mon 11/02/19	Fri 15/03/19
46	Roof cover and lift shaft roof overrun	15 days	Mon 28/01/19	Fri 15/02/19
47	building basic watertight	0 days	Fri 15/02/19	Fri 15/02/19
48	remove façade retention.	7 days	Mon 28/01/19	Tue 05/02/19
49	Remaining lift overrun walls and roof	5 days	Mon 11/02/19	Fri 15/02/19
50	Roof cover to complete, roof finishes and parapi	20 days	Mon 18/02/19	Fri 15/03/19
51	Windows and EPDM	25 days	Mon 11/02/19	Fri 15/03/19
52	Brickwork finals, snagging	5 days	Mon 18/03/19	Fri 22/03/19
53	PV Panels and Mansafe system	2 wks	Mon 18/03/19	Fri 29/03/19
54	balconies railing and decking	10 days	Mon 25/03/19	Fri 05/04/19
55	RWPs, external mastic and elevations finals	5 days	Mon 01/04/19	Fri 05/04/19
56	scaffold strike	15 days	Mon 08/04/19	Fri 26/04/19
57	Incoming services and S106 works	6 days	Mon 29/04/19	Mon 06/05/19
58	Power On	0 days	Mon 06/05/19	Mon 06/05/19
59	Water On	0 days	Mon 06/05/19	Mon 06/05/19
60	Gas On	0 days	Mon 06/05/19	Mon 06/05/19
61	External Works	15 days	Tue 07/05/19	Mon 27/05/19
62	External finals	5 days	Tue 28/05/19	Mon 03/06/19
63	Dismantle tower crane	2 days	Tue 04/06/19	Wed 05/06/19
64	handover	0 days	Wed 05/06/19	Wed 05/06/19
65	**Internal Fitout**	**130 days**	**Mon 18/02/19**	**Mon 19/08/19**
139	**Communal areas works**	**101 days**	**Mon 18/03/19**	**Mon 05/08/19**
140	Lift installation (both shafts)	40 days	Mon 18/03/19	Fri 10/05/19
141	Lift test and commissioning	5 days	Mon 13/05/19	Fri 17/05/19
142	communal services risers	25 days	Mon 25/03/19	Fri 26/04/19
143	M&E 1st fix	20 days	Mon 15/04/19	Fri 10/05/19
144	Communal landings and Stairs plasterboard	20 days	Mon 29/04/19	Fri 24/05/19
145	T&J communals	20 days	Mon 13/05/19	Fri 07/06/19
146	mist coat and making good	15 days	Mon 27/05/19	Fri 14/06/19
147	M&E 2nd fix	15 days	Mon 03/06/19	Fri 21/06/19
148	Carpentry 2nd fix	20 days	Mon 10/06/19	Fri 05/07/19
149	Decoration	20 days	Mon 24/06/19	Fri 19/07/19
150	Flooring to stairs	10 days	Mon 15/07/19	Fri 26/07/19
151	Ground floor lobby flooring and finals	5 days	Mon 22/07/19	Fri 26/07/19
152	Snagging and sparkle clean	6 days	Mon 29/07/19	Mon 05/08/19
153	Handover	0 days	Mon 05/08/19	Mon 05/08/19

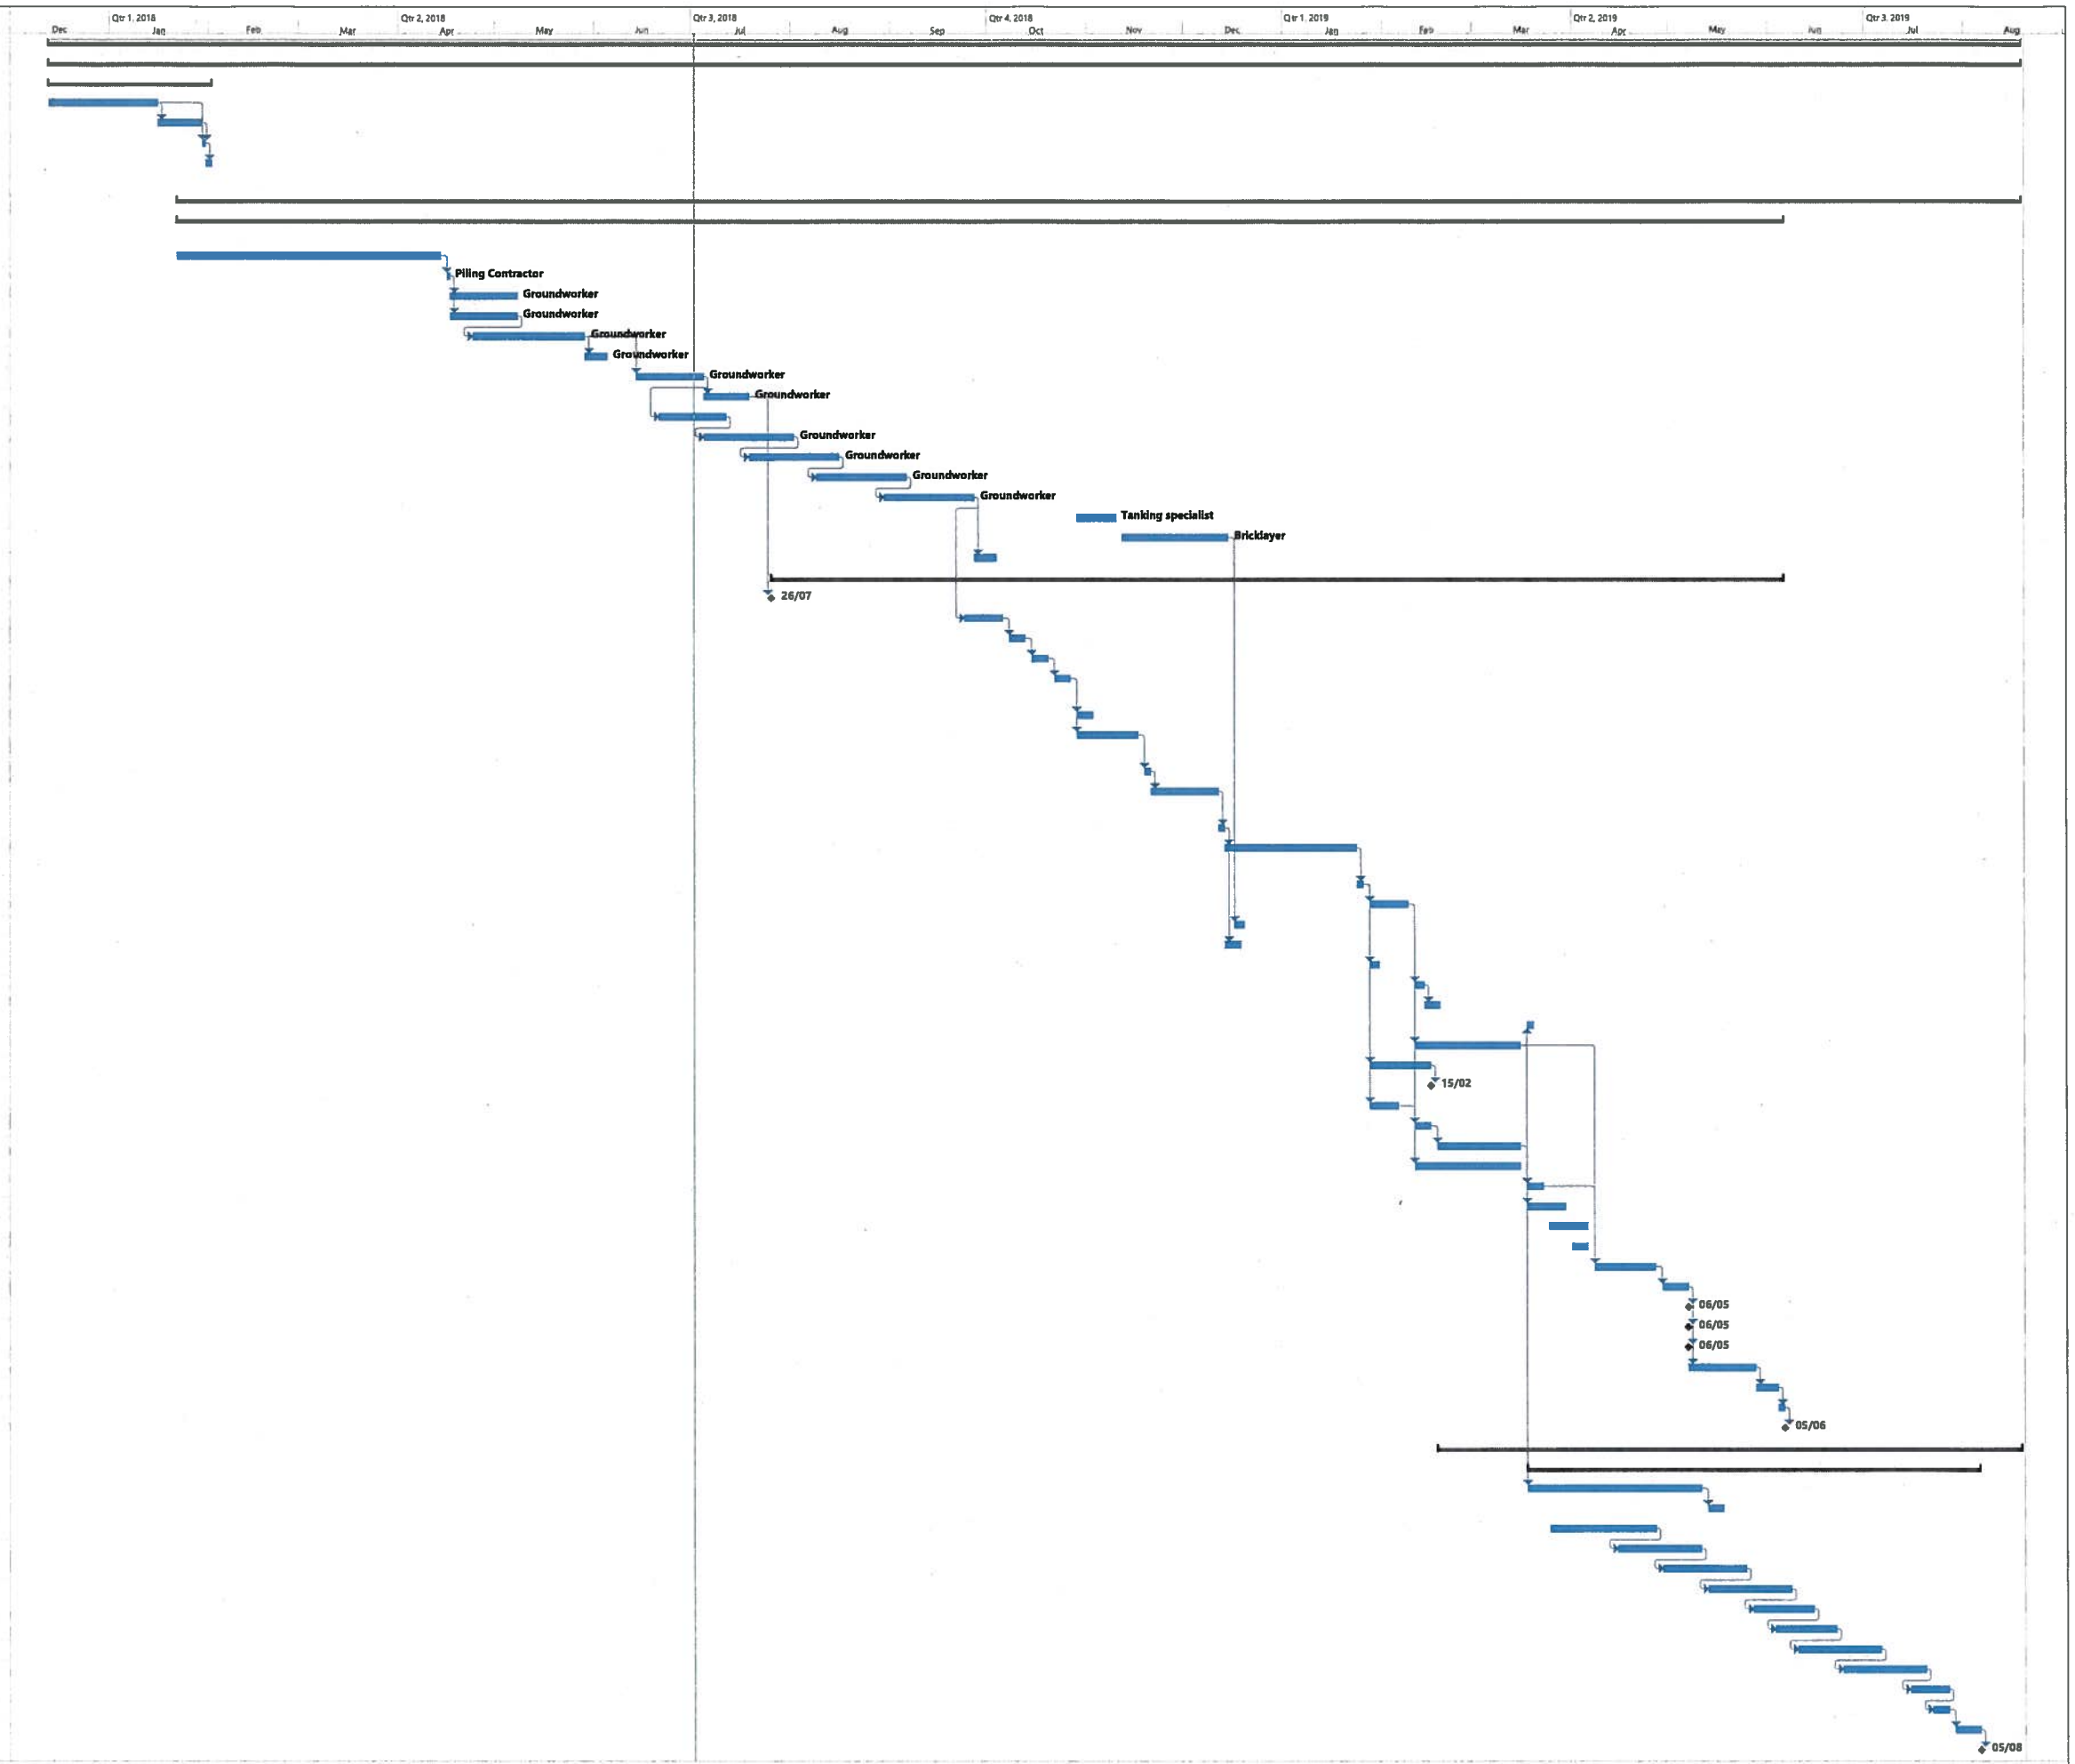

Project: Haverstock Hill Program
Date: Mon 02/07/18

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
