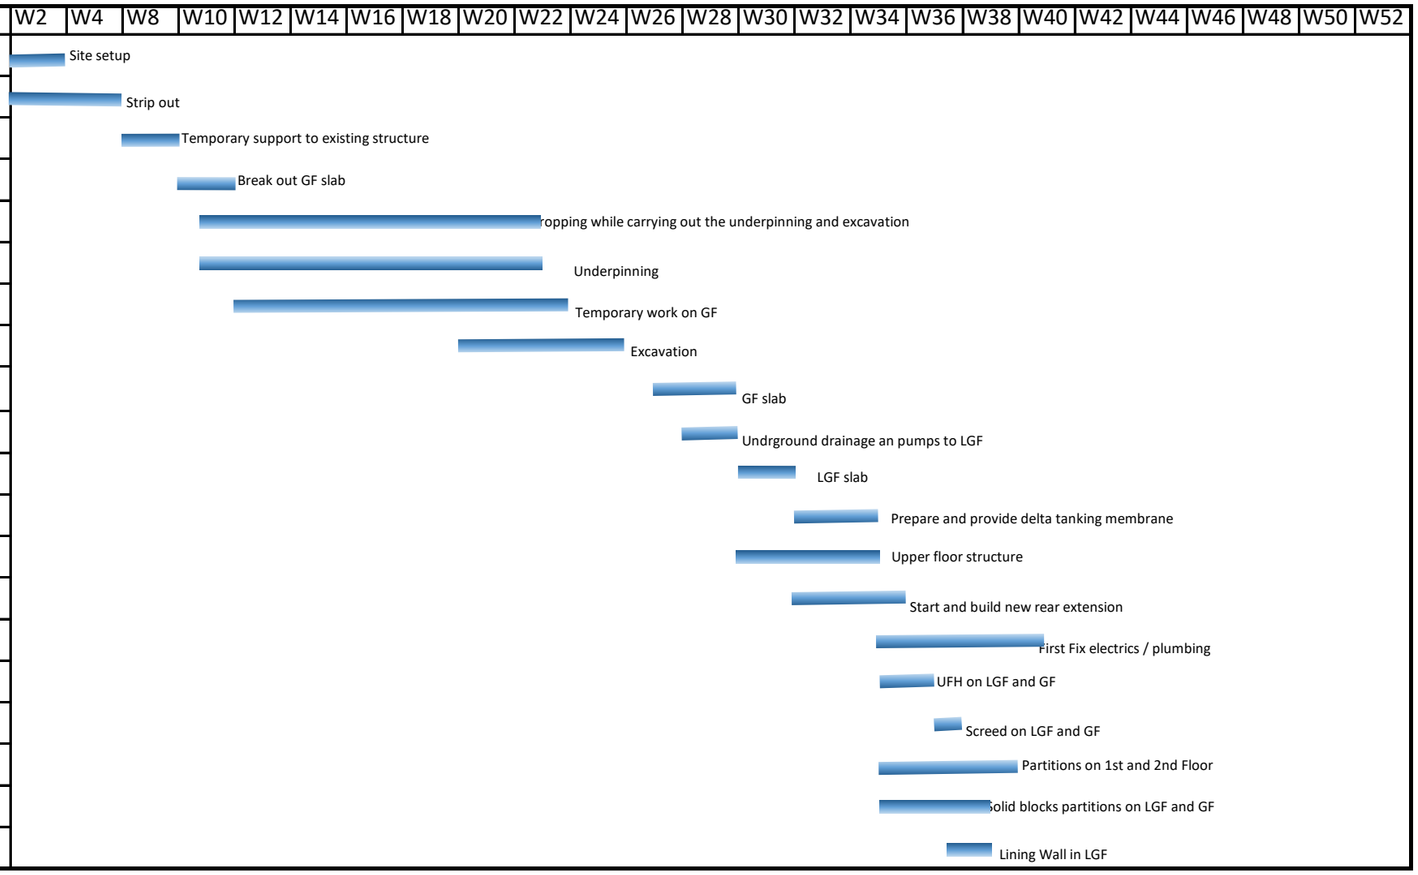Task Name	Duration
Site setup	1 week
Strip out	4 weeks
Temporary support to existing structure	2 weeks
Break out GF slab	2 weeks
Propping while carrying out the underpinning and excavation	12 week
Underpinning	12 weeks
Temporary work on GF	12 weeks
Excavation	6 weeks
GF slab	3 weeks
Undrground drainage an pumps to LGF	2 weeks
LGF slab	2 weeks
Prepare and provide delta tanking membrane	3 weeks
Upper floor structure	5 weeks
Start and build new rear extension	4 weeks
First Fix electrics / plumbing	6 weeks
UFH on LGF and GF	2 weeks
Screed on LGF and GF	1 week
Partitions on 1st and 2nd Floor	5 weeks
Solid blocks partitions on LGF and GF	4 weeks
Lining Wall in LGF	2 weeks
