5 Oval Road Plant Room Construction

ID	Task Name	Duration	Start	Finish
1	Plant room Costruction	40 days	Mon 21/01/19	Fri 15/03/19
2	Underpinning works	35 days	Mon 19/11/18	Fri 04/01/19
3	Break out Extg wall and footing	8 days	Mon 14/01/19	Wed 23/01/19
4	Reduced dig ajd sheet piles	8 days	Mon 21/01/19	Wed 30/01/19
5	Works to Existing drainage	4 days	Tue 29/01/19	Fri 01/02/19
6	Blinding	1 day	Mon 04/02/19	Mon 04/02/19
7	Base slab and reinforcement	5 days	Mon 04/02/19	Fri 08/02/19
8	Formers to walls	5 days	Mon 11/02/19	Fri 15/02/19
9	reinforcement	4 days	Wed 13/02/19	Mon 18/02/19
10	cast walls	7 days	Mon 18/02/19	Tue 26/02/19
11	Roof decking	4 days	Wed 27/02/19	Mon 04/03/19
12	Roof Slab reinforcement	2 days	Mon 04/03/19	Tue 05/03/19
13	Cast roof slab	2 days	Tue 05/03/19	Wed 06/03/19
14	Strike and prop	7 days	Fri 08/03/19	Mon 18/03/19
15	New drainage	5 days	Mon 11/03/19	Fri 15/03/19
16	Stairs	5 days	Mon 11/03/19	Fri 15/03/19
17	External concrete works and ducting	5 days	Mon 18/03/19	Fri 22/03/19

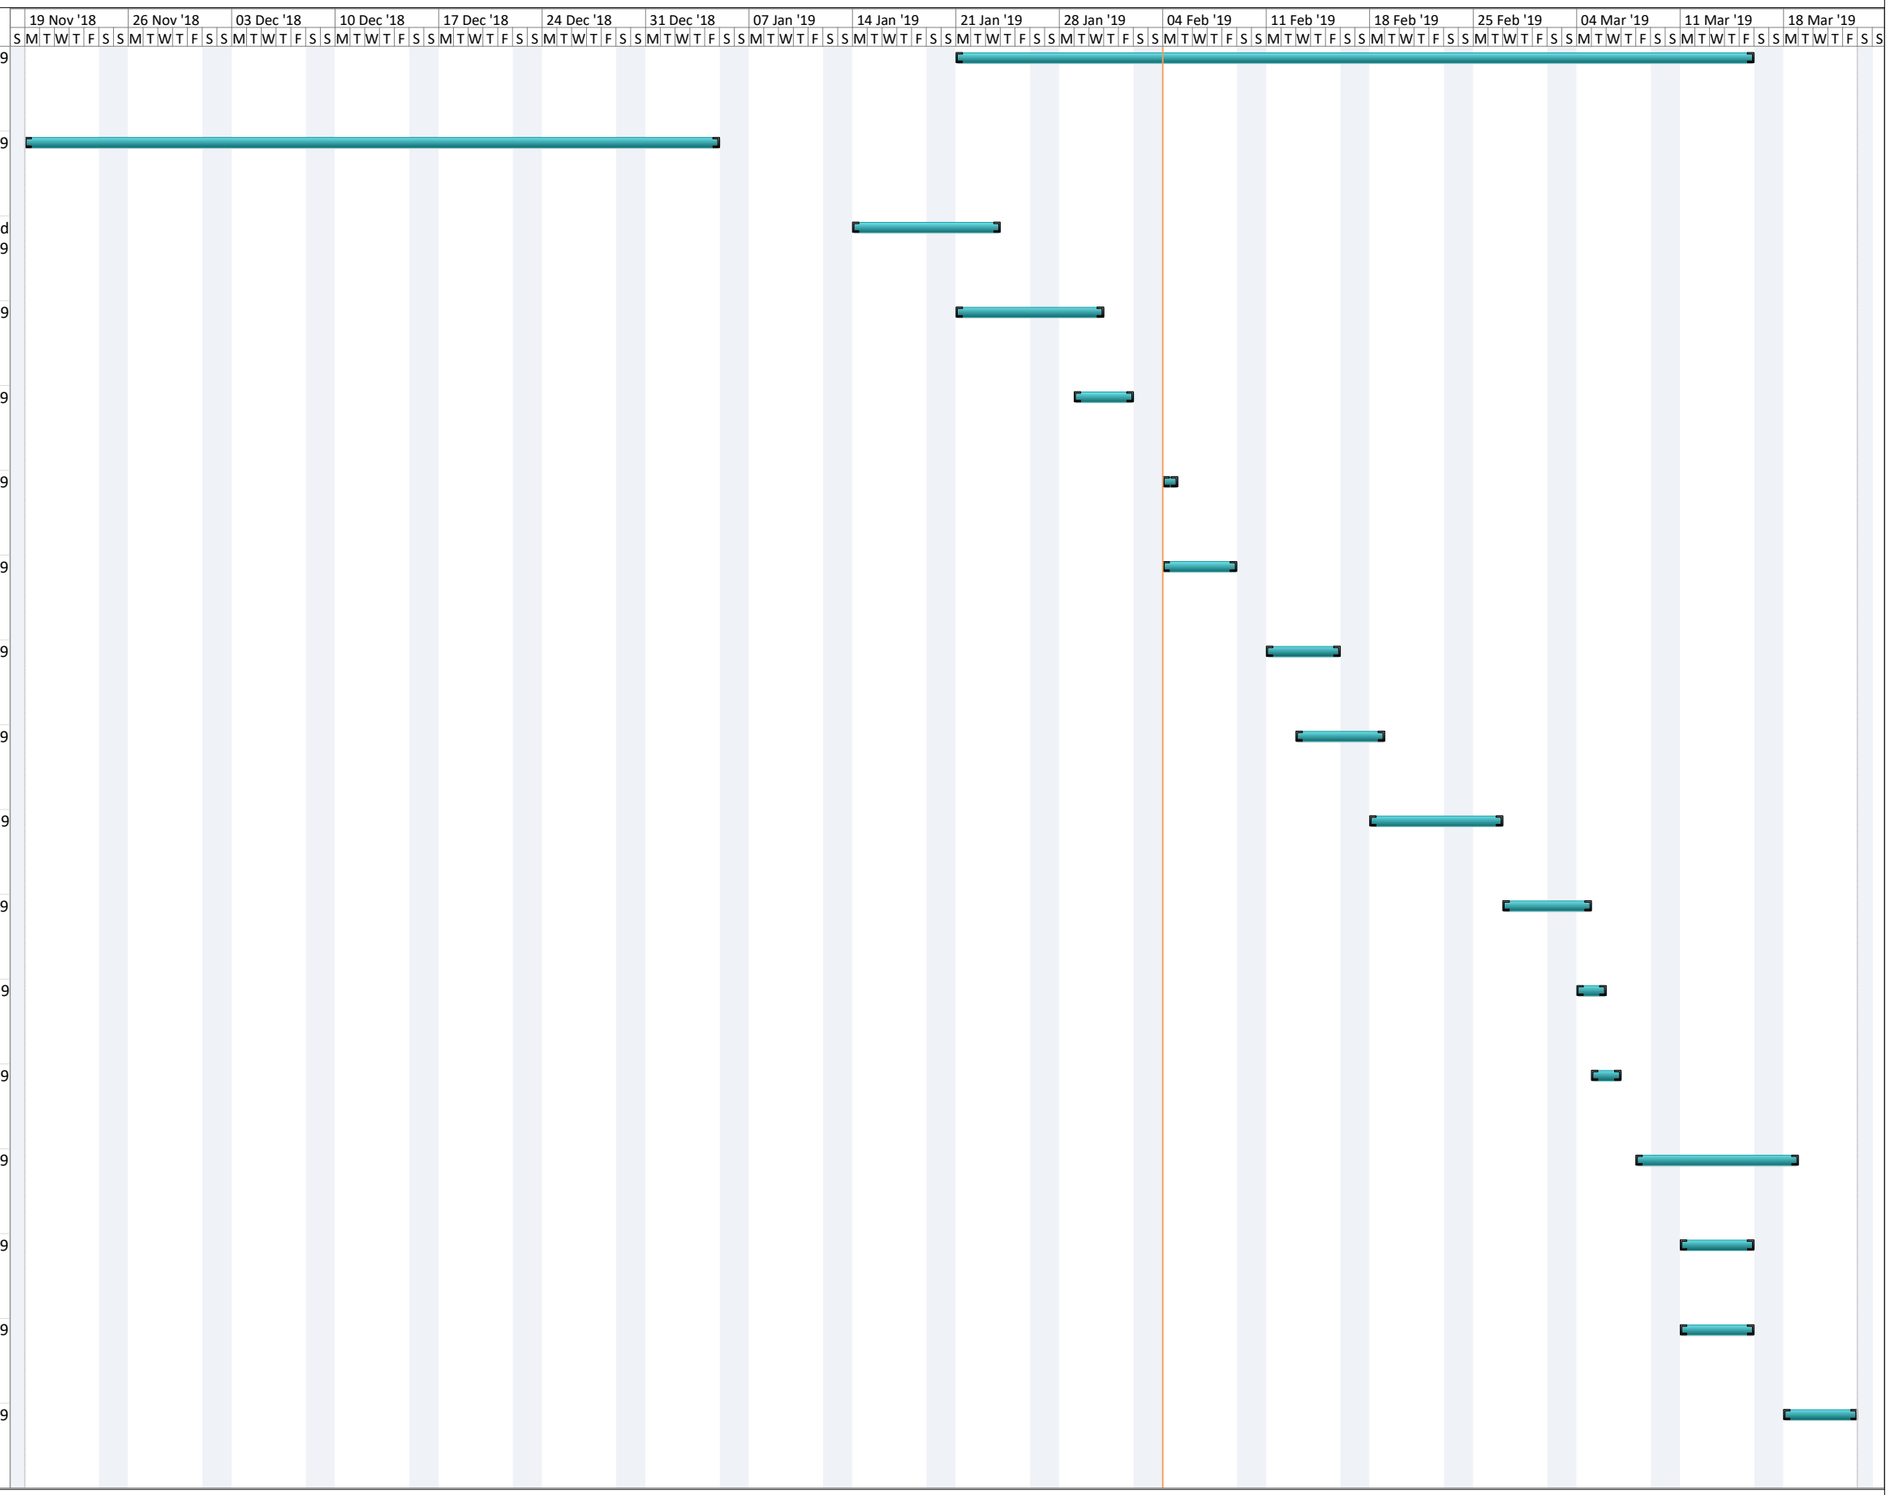

Project: Plant room construction
Date: Mon 04/02/19

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | Deadline | Progress
