St Pancras Gardens Camley Street Ramp
GMOPL106 Camley Street Ramp - Construction Programme 20.10.26
Mon 26/10/20
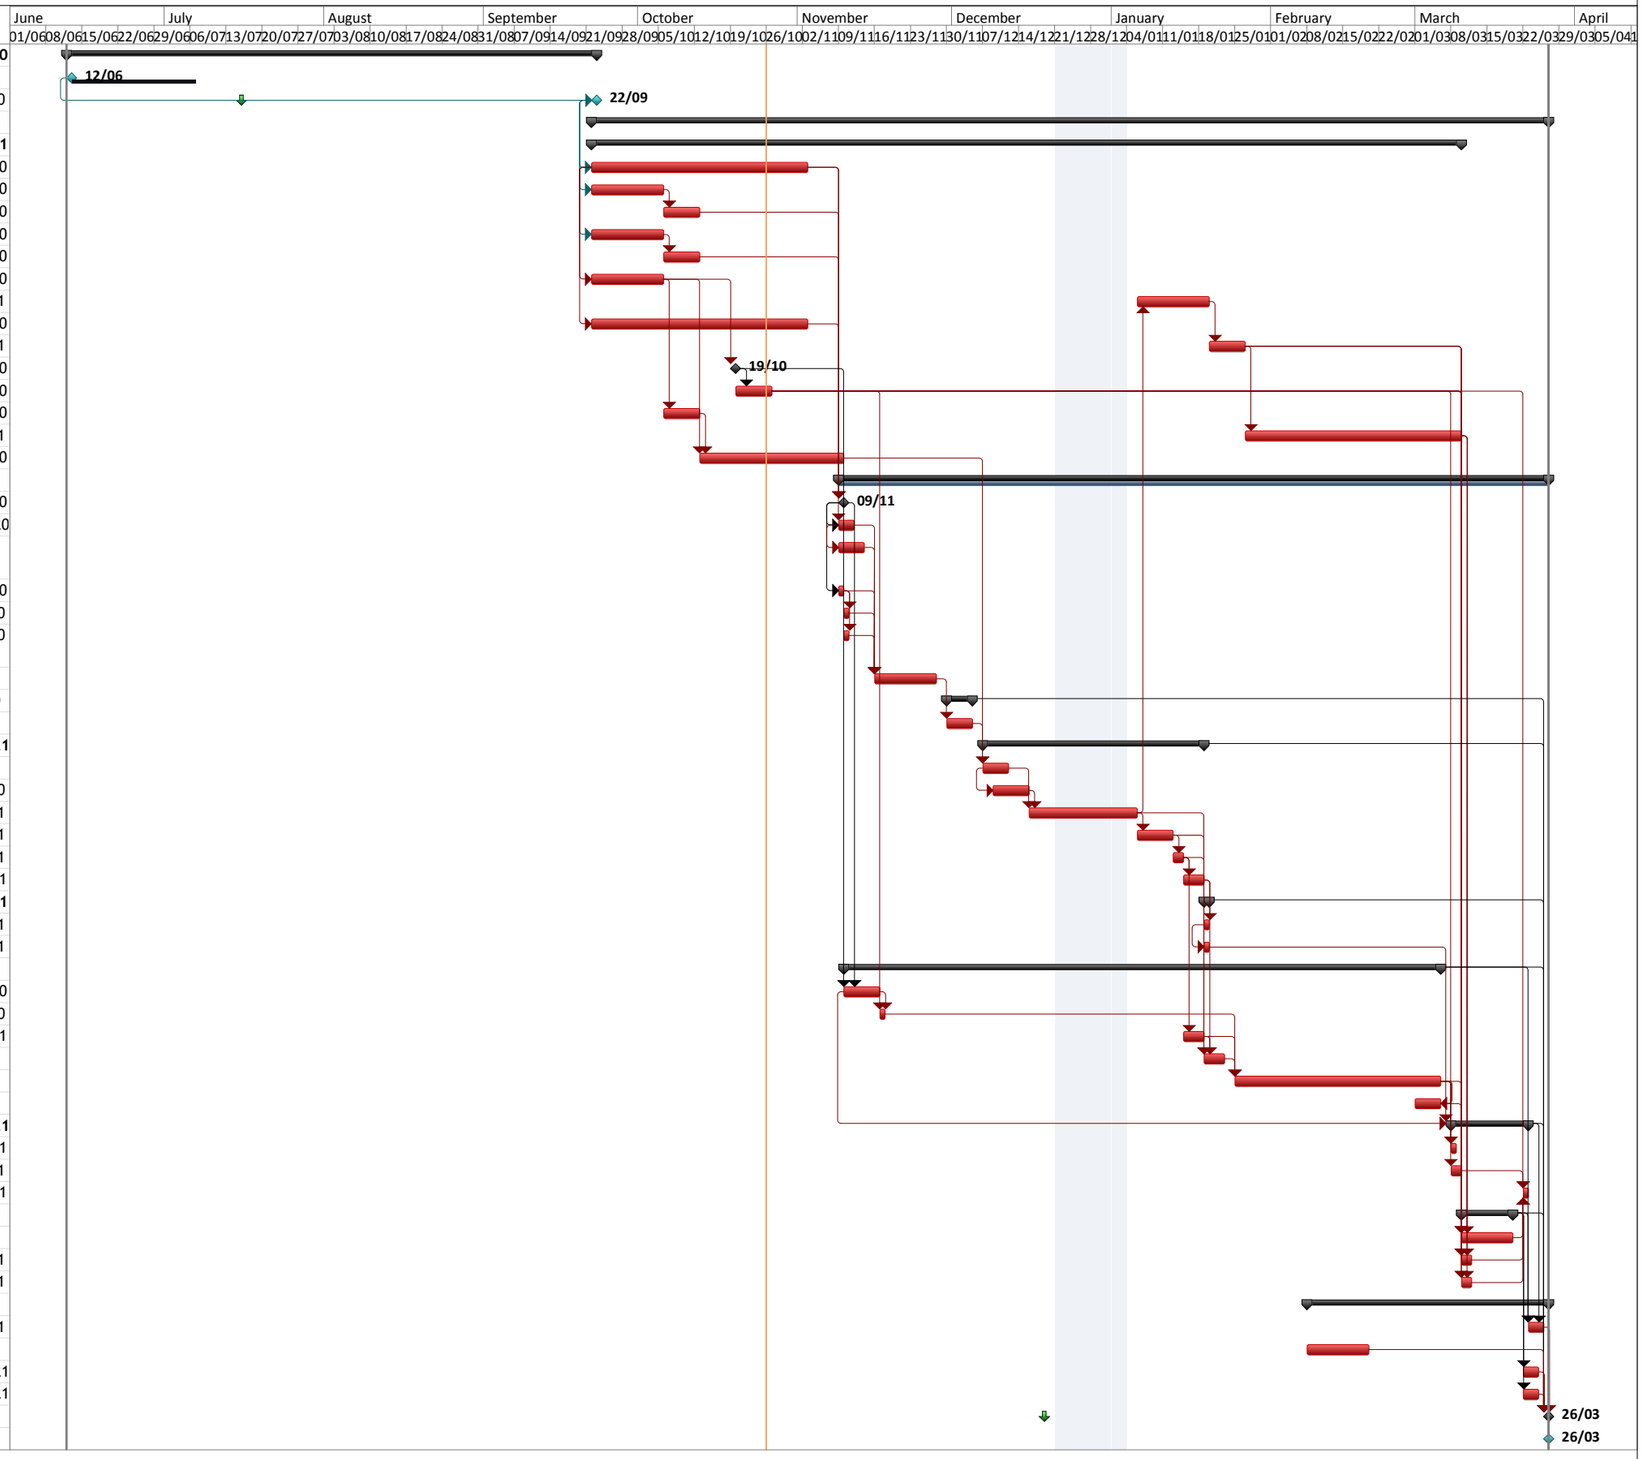
ID	Task Mode	Task Name	Duration	Start	Finish
1		**Tender Period**	**73 days**	**Fri 12/06/20**	**Tue 22/09/20**
2		Tender Return	1 day	Fri 12/06/20	Fri 12/06/20
3		Contract Award	1 day	Tue 22/09/20	Tue 22/09/20
4		**Contract Period**	**124 days**	**Tue 22/09/20**	**Fri 26/03/21**
5		**Mobilisation**	**111 days**	**Tue 22/09/20**	**Tue 09/03/21**
6		CDM Planning Period	30 days	Tue 22/09/20	Mon 02/11/20
7		Construction Phase Programme	10 days	Tue 22/09/20	Mon 05/10/20
8		Client review and acceptance of programm	5 days	Tue 06/10/20	Mon 12/10/20
9		ITP Prepared	10 days	Tue 22/09/20	Mon 05/10/20
10		Client review and approval of ITP	5 days	Tue 06/10/20	Mon 12/10/20
11		Procurement	10 days	Tue 22/09/20	Mon 05/10/20
12		Metal Work Fabrication Drawings	10 days	Wed 06/01/21	Tue 19/01/21
13		Consents and Licences	30 days	Tue 22/09/20	Mon 02/11/20
14		Client Approval of Fabrication Drawings	5 days	Wed 20/01/21	Tue 26/01/21
15		Procurement of Samples	10 days	Tue 06/10/20	Mon 19/10/20
16		Client Approval of Samples	5 days	Tue 20/10/20	Mon 26/10/20
17		Procurement of materials	5 days	Tue 06/10/20	Mon 12/10/20
18		Lead Times for Metal work	30 days	Wed 27/01/21	Tue 09/03/21
19		General Lead times	20 days	Tue 13/10/20	Mon 09/11/20
20		**Contract Works**	**90 days**	**Mon 09/11/20**	**Fri 26/03/21**
21		Commencement	1 day	Mon 09/11/20	Mon 09/11/20
22		Site set up and welfare	3 days	Mon 09/11/20	Wed 11/11/20
23		Footpath closure, hoarding and fencing installation	5 days	Mon 09/11/20	Fri 13/11/20
24		Tree protection	1 day	Mon 09/11/20	Mon 09/11/20
25		Install props to walls to be retained	1 day	Tue 10/11/20	Tue 10/11/20
26		Edge protection for clearance, demolition and excavation.	1 day	Tue 10/11/20	Tue 10/11/20
27		Clearance, Removals and Demolition	10 days	Mon 16/11/20	Fri 27/11/20
28		**Excavation**	**5 days**	**Mon 30/11/20**	**Fri 04/12/20**
29		Bulk excavation to formation levels	5 days	Mon 30/11/20	Fri 04/12/20
30		**Structural Concrete**	**21 days**	**Mon 07/12/20**	**Mon 18/01/21**
31		Formwork	5 days	Mon 07/12/20	Fri 11/12/20
32		Reinforcement	5 days	Wed 09/12/20	Tue 15/12/20
33		Concrete pour	5 days	Wed 16/12/20	Tue 05/01/21
34		Curing	5 days	Wed 06/01/21	Tue 12/01/21
35		Strike Formwork	2 days	Wed 13/01/21	Thu 14/01/21
36		Waterproofing	2 days	Fri 15/01/21	Mon 18/01/21
37		**Drainage and Filling**	**1 day**	**Tue 19/01/21**	**Tue 19/01/21**
38		Pipe install	1 day	Tue 19/01/21	Tue 19/01/21
39		Free draining material	1 day	Tue 19/01/21	Tue 19/01/21
40		**Brickwork**	**74 days**	**Tue 10/11/20**	**Fri 05/03/21**
41		Sample Panel from approved sample	5 days	Tue 10/11/20	Mon 16/11/20
42		Client Approval of sample panel	1 day	Tue 17/11/20	Tue 17/11/20
43		Erect scaffold	2 days	Fri 15/01/21	Mon 18/01/21
44		Install SP21 wall ties	4 days	Tue 19/01/21	Fri 22/01/21
45		Brickwork	30 days	Mon 25/01/21	Fri 05/03/21
46		Copings	5 days	Mon 01/03/21	Fri 05/03/21
47		**Edges and Surfacing**	**11 days**	**Mon 08/03/21**	**Mon 22/03/21**
48		Granite kerb edge	1 day	Mon 08/03/21	Mon 08/03/21
49		Type 1	2 days	Mon 08/03/21	Tue 09/03/21
50		Resin Bonded Gravel	1 day	Mon 22/03/21	Mon 22/03/21
51		**Railings and Gates**	**8 days**	**Wed 10/03/21**	**Fri 19/03/21**
52		Balustrade	8 days	Wed 10/03/21	Fri 19/03/21
53		Handrail	2 days	Wed 10/03/21	Thu 11/03/21
54		Gate	2 days	Wed 10/03/21	Thu 11/03/21
55		**Proposed Completion**	**35 days**	**Mon 08/02/21**	**Fri 26/03/21**
56		Reinstate areas	3 days	Tue 23/03/21	Thu 25/03/21
57		Snagging	10 days	Mon 08/02/21	Fri 19/02/21
58		Removal of Hoarding	3 days	Mon 22/03/21	Wed 24/03/21
59		Demobilisation	3 days	Mon 22/03/21	Wed 24/03/21
60		Completion	1 day	Fri 26/03/21	Fri 26/03/21
61		Contract Completion	1 day	Fri 26/03/21	Fri 26/03/21
