UCL Wates House Refurbishment Project

Line	Name	Duration	Start	Finish
1	**LIAISON WITH STATUTORY AUTHORITIES**	**3w**	**05 Jan 15**	**23 Jan 15**
2	**CDM PLANNING / MOBILISATION**	**3w**	**05 Jan 15**	**23 Jan 15**
3	**SCAFFOLD LICENCE**	**12w**	**05 Jan 15**	**27 Mar 15**
4	**HOARDING LICENCE**	**4w**	**05 Jan 15**	**30 Jan 15**
5	**PROCUREMENT / LEAD-IN**	**13w**	**19 Jan 15**	**24 Apr 15**
6	**DESIGN / PRODUCTION INFO / SAMPLES & MOCK-UPS**	**52w 4d**	**19 Jan 15**	**12 Feb 16**
7	**MILESTONE PAYMENTS**	**77w 3d**	**26 Jan 15**	**22 Aug 16**
8	Milestone payments		26 Jan 15	22 Aug 16
9	**CONSTRUCTION PERIOD (PRINCIPLE CONTRACT)**	**78w 3d**	**26 Jan 15**	**26 Aug 16**
10	Closure of Christopher Ingould Building Lecture Theatre	12w 4d	26 Jan 15	30 Apr 15
11	**SITE ESTABLISHMENT**	**2w**	**26 Jan 15**	**06 Feb 15**
12	Potential Start of CIB (Christopher Ingould Building) Welfare Project		27 Apr 15	27 Apr 15
13	**SERVICE VOIDS SLAB PENETRATIONS**	**4w 4d**	**09 Feb 15**	**12 Mar 15**
14	**PERIMETER EXTENSION**	**29w**	**02 Feb 15**	**31 Aug 15**
15	**NEW EXTENSION (G.L W-M+/2-5)**	**25w 1d**	**05 Feb 15**	**07 Aug 15**
16	**ROOF TOP EXTENSION (G.L W-C / 5-11)**	**19w**	**02 Apr 15**	**20 Aug 15**
17	**ROOF FINISHES**	**19w 1d**	**21 Aug 15**	**18 Jan 16**
18	**EXTERNAL ENVELOPE**	**31w**	**17 Aug 15**	**08 Apr 16**
19	Dismantle Crane		11 Apr 16	11 Apr 16
20	**INTERNAL FITOUT**	**38w 4d**	**02 Nov 15**	**19 Aug 16**
21	**LIFT INSTALLATION**	**17w 4d**	**18 Apr 16**	**19 Aug 16**
22	**STAIRCORE FINISHES**	**12w**	**09 May 16**	**29 Jul 16**
23	**BUILDING FINALS**	**9w**	**27 Jun 16**	**26 Aug 16**
24	Pre-commissioning	4w	27 Jun 16	22 Jul 16
25	Final snagging	4w	18 Jul 16	12 Aug 16
26	Final Testing & Commissioning	4w	25 Jul 16	19 Aug 16
27	Demonstrations	1w	22 Aug 16	26 Aug 16
28	Practical Completion	1d	26 Aug 16	26 Aug 16
29	**WORKS OUTSIDE SITE BOUNDARY**	**54w 4d**	**12 Jan 15**	**19 Feb 16**
30	**UCL FIT-OUT**	**8w 1d**	**01 Aug 16**	**26 Sep 16**

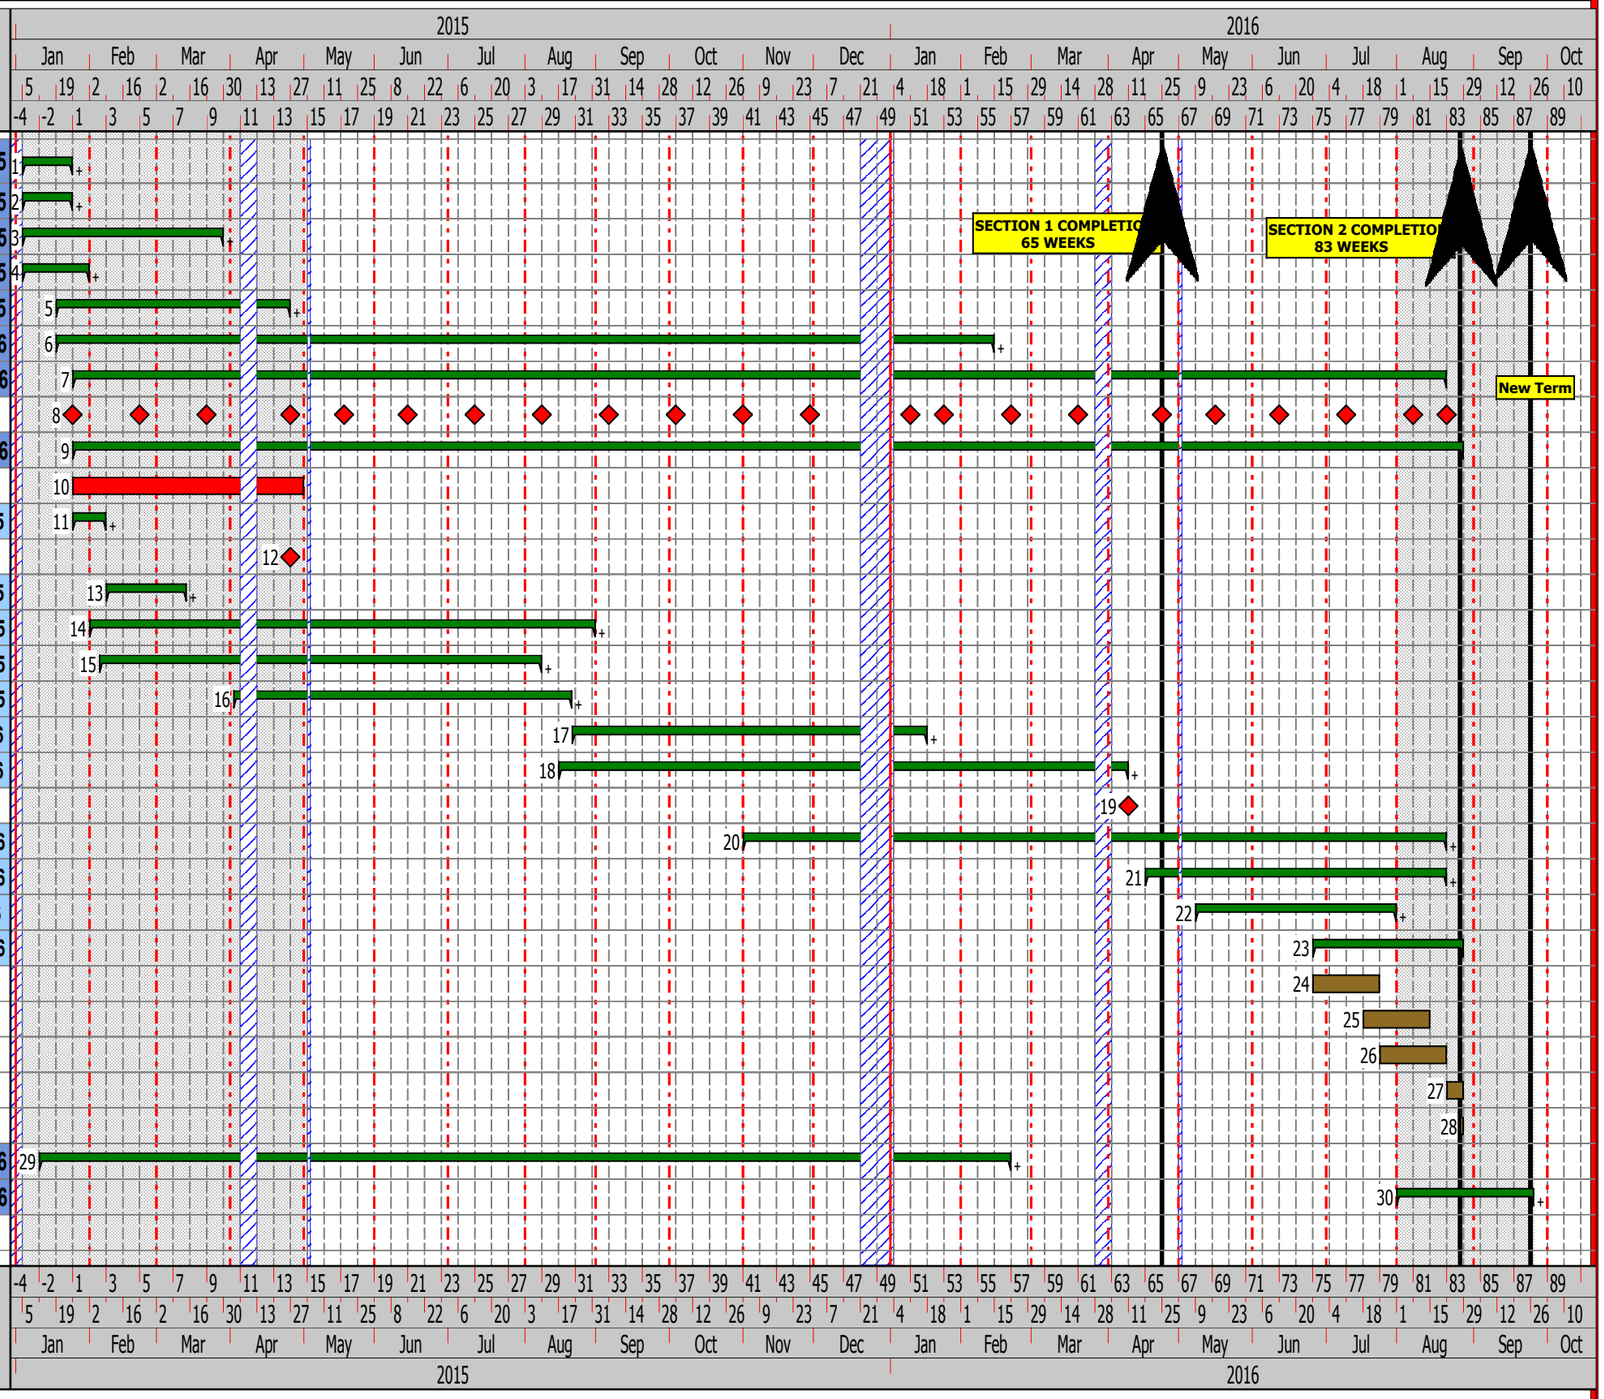

Wates House UCL

Main Summary | Milestone | Building Finals

Symbols

Milestone

Issue Date: 26/01/2015	Revision Date:	Revision No.	Notes:

Project Ref. C:\Users\coffeya\Desktop\Wates House\403 UCL (DP).pp

Planned by Asta Powerproject
