Appendix B: Construction Programme

ID		Task Name	Duration
1		**Enabling Works**	**3 days**
2		Road closure + signage	3 days
3		**Site Setup**	**631 days**
4		Hoardings	5 days
5		Power Supply	2 days
6		Cabins	5 days
7		Cranes	5 days
8		Site demobilisation	5 days
9		**Demolition**	**15 days**
10		Façade panels	5 days
11		Headhouse loading points	5 days
12		Excavation to exposed pile	5 days
13		GSHP connections	5 days
14		**Main structure**	**401 days**
15		Ground floor raft slab	30 days
16		Ground floor walls and Cols	20 days
17		1st floor slab	10 days
18		1st walls and columns	39 days
19		2nd floor slab	12 days
20		2nd floor walls and columns	39 days
21		3rd floor slab	12 days
22		3rd floor walls and columns	39 days
23		4th floor slab	12 days
24		4th walls and columns	39 days
25		5th floor slab	12 days
26		5th floor walls and columns	39 days
27		6th floor slab	12 days
28		6th floor walls and columns	39 days
29		7th floor slab	12 days
30		7th floor walls and columns	20 days
31		7th floor cantilever box	39 days
32		8th floor slab	10 days
33		8th floor walls and columns and roof	30 days
34		Steel stair way	40 days
35		Steel frame roof	20 days
36		Roof cladding	25 days
37		Façade Cladding	30 days
38		Galzing	40 days
39		**Fit-out**	**190 days**
40		Ground floor fix	50 days
41		1st Floor fix	60 days
42		2nd Floor fix	60 days
43		3rd Floor fix	60 days
44		4rd Floor fix	60 days
45		5th floor fix	45 days
46		6th floor fix	45 days
47		7th floor fix	45 days
48		8th floor fix	30 days
49		**Bike store**	**75 days**
50		Steel fame	30 days
51		Concrete roof	15 days
52		Spiral stairway	15 days
53		Carpentry + electric fix	30 days
54		**Electrical and Mechanical**	**265 days**
55		Substation Installation	40 days
56		LV switch room installation	20 days
57		Lift installation	90 days
58		Generator installation	30 days
59		Drainage connections	20 days
60		**Public realm and external decoration**	**15 days**
61		Public realm	15 days
62		External decoration	15 days

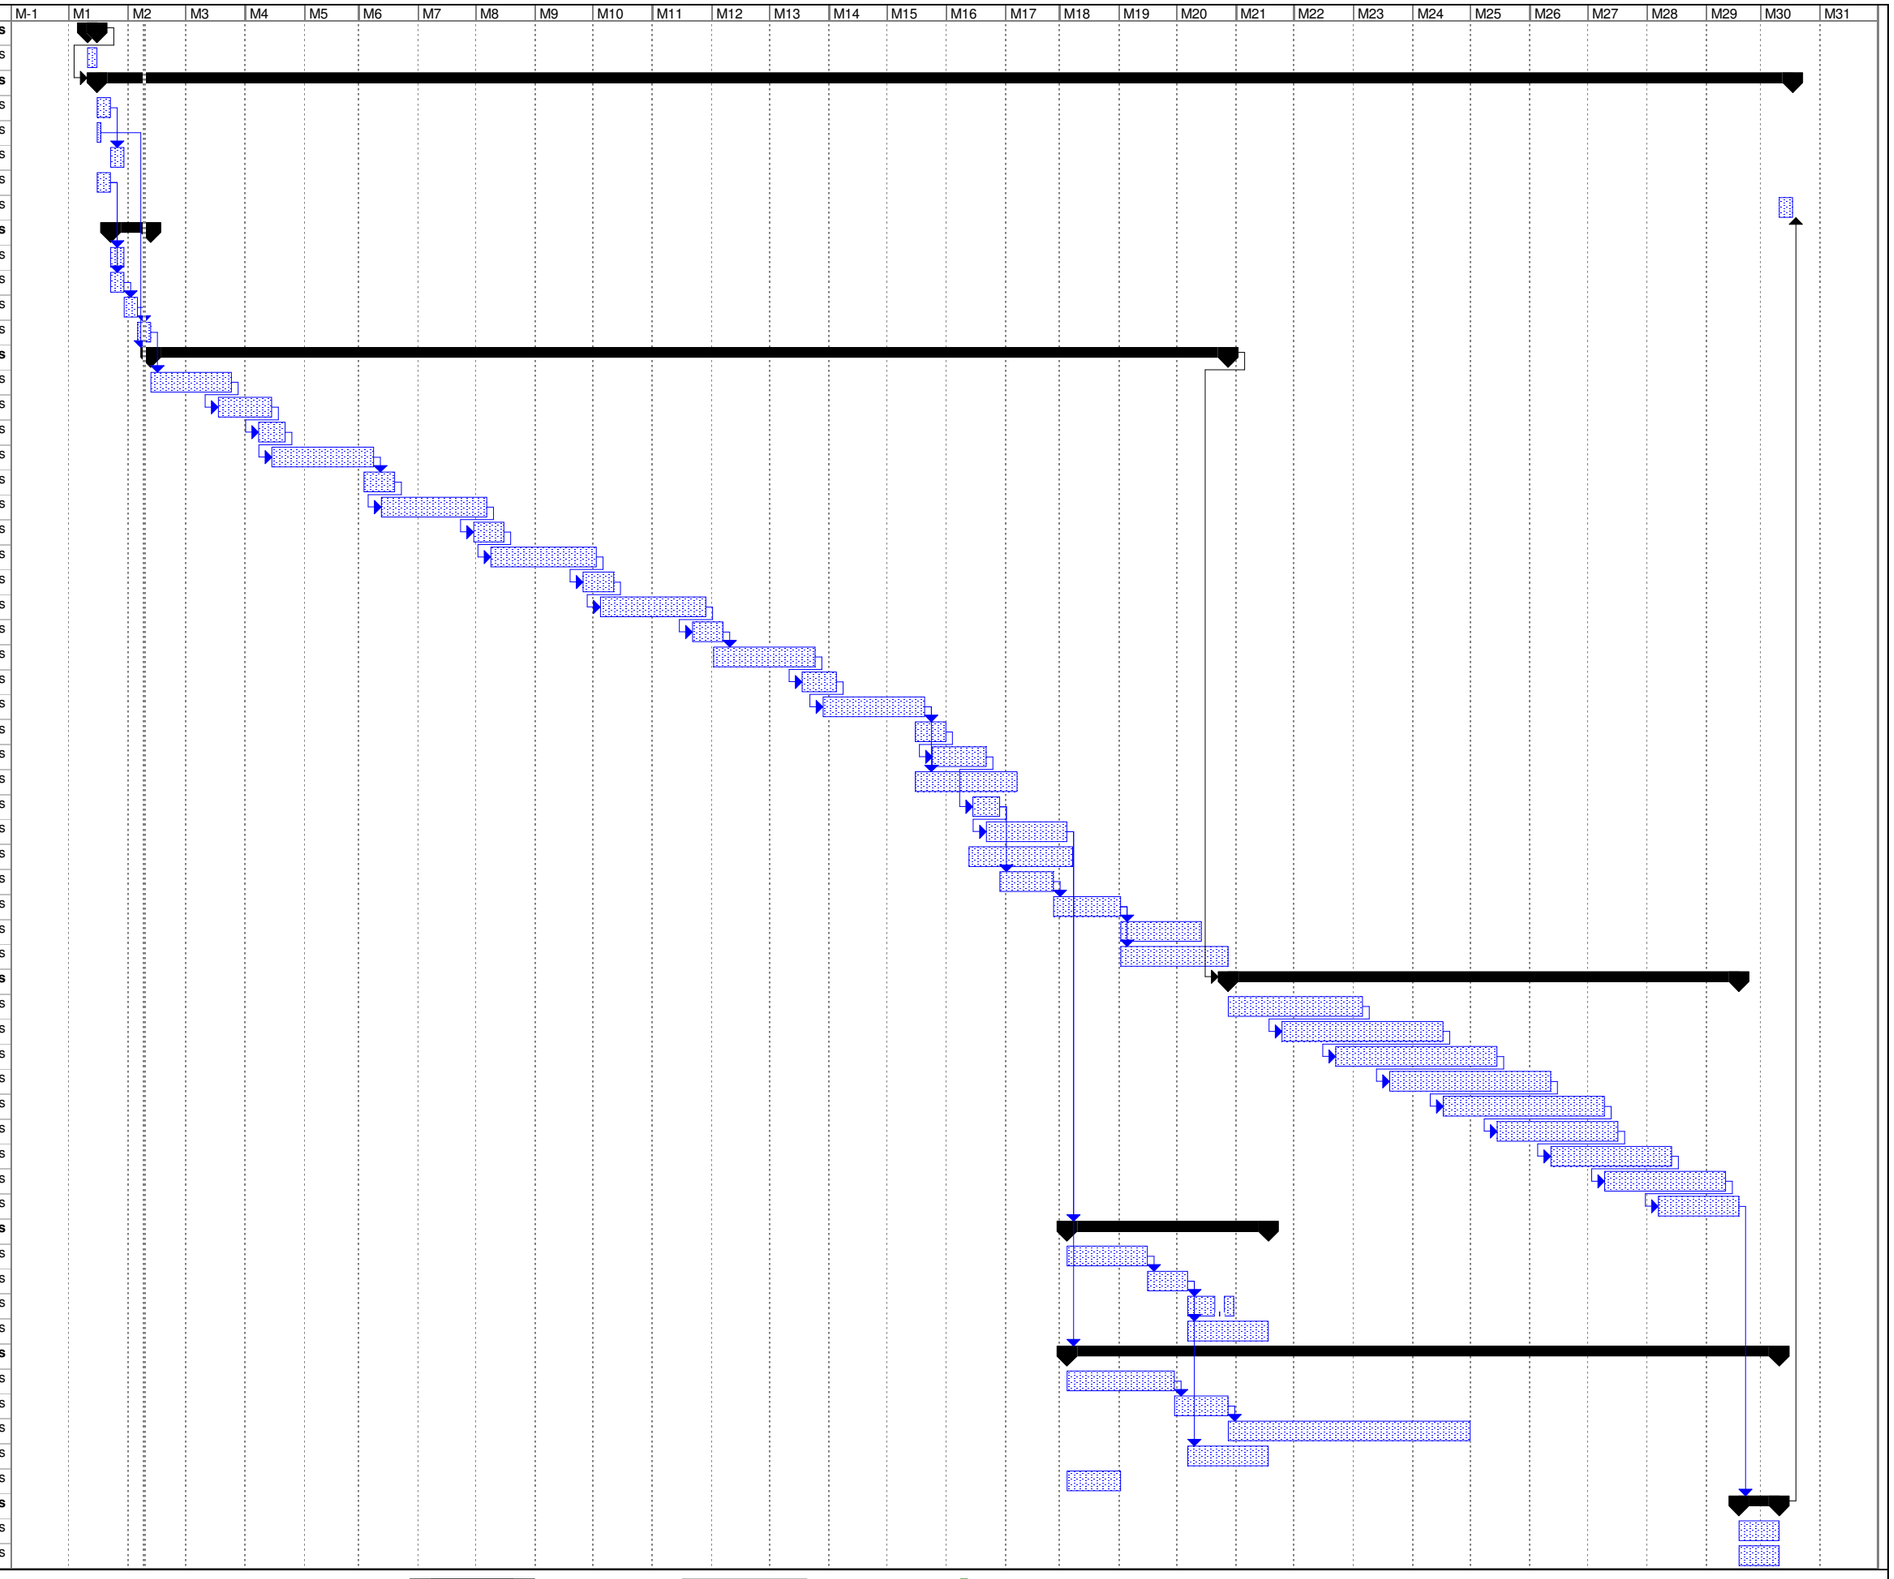

Project: fisherstreetods
Date: Fri 09/11/12

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
