Task Name	Duration	Start	Finish
Site Set-up/Hoarding & enabling Works	7 days	Mon 06/02/17	Tue 14/02/17
Scaffold phase 1 Gantry & bracing works	9 days	Tue 07/02/17	Fri 17/02/17
Demo	10 days	Wed 15/02/17	Tue 28/02/17
Groundworks, inc underpinning / drainage / new slabs / basement blockwork/brickwork	125 days	Wed 01/03/17	Tue 29/08/17
Steel frame / joistwork / blockwork / brickwork	60 days	Mon 21/08/17	Mon 13/11/17
Scaffold to follow build as required	10 days	Tue 29/08/17	Wed 25/10/17
Roof/Mansard frame	15 days	Mon 06/11/17	Fri 24/11/17
External - roofs/downpipes/balconies/railings/mansafe/plant enclosure	40 days	Mon 20/11/17	Tue 23/01/18
Rooflight/Windows	15 days	Mon 11/12/17	Tue 09/01/18
Internal stairs/balustrade	20 days	Mon 04/09/17	Tue 30/01/18
Partitions/ceilings/plastering	60 days	Mon 04/12/17	Tue 06/03/18
Strike Scaffold	4 days	Mon 29/01/18	Thu 01/02/18
First fix Elec	30 days	Tue 02/01/18	Mon 12/02/18
First fix Plumbing	28 days	Mon 15/01/18	Wed 21/02/18
Boxings/ductwork etc	16 days	Mon 05/02/18	Mon 26/02/18
Tiling/stonework	30 days	Mon 26/02/18	Tue 10/04/18
Internal joinery, doors	36 days	Mon 26/02/18	Wed 18/04/18
Second fix Elec	20 days	Mon 12/03/18	Tue 10/04/18
Second fix Plumbing	18 days	Tue 03/04/18	Thu 26/04/18
Kitchens	18 days	Mon 09/04/18	Wed 02/05/18
Decorating	34 days	Tue 03/04/18	Mon 21/05/18
Flooring	14 days	Tue 08/05/18	Fri 25/05/18
Snagging/Commisioning and handover	8 days	Tue 22/05/18	Fri 01/06/18

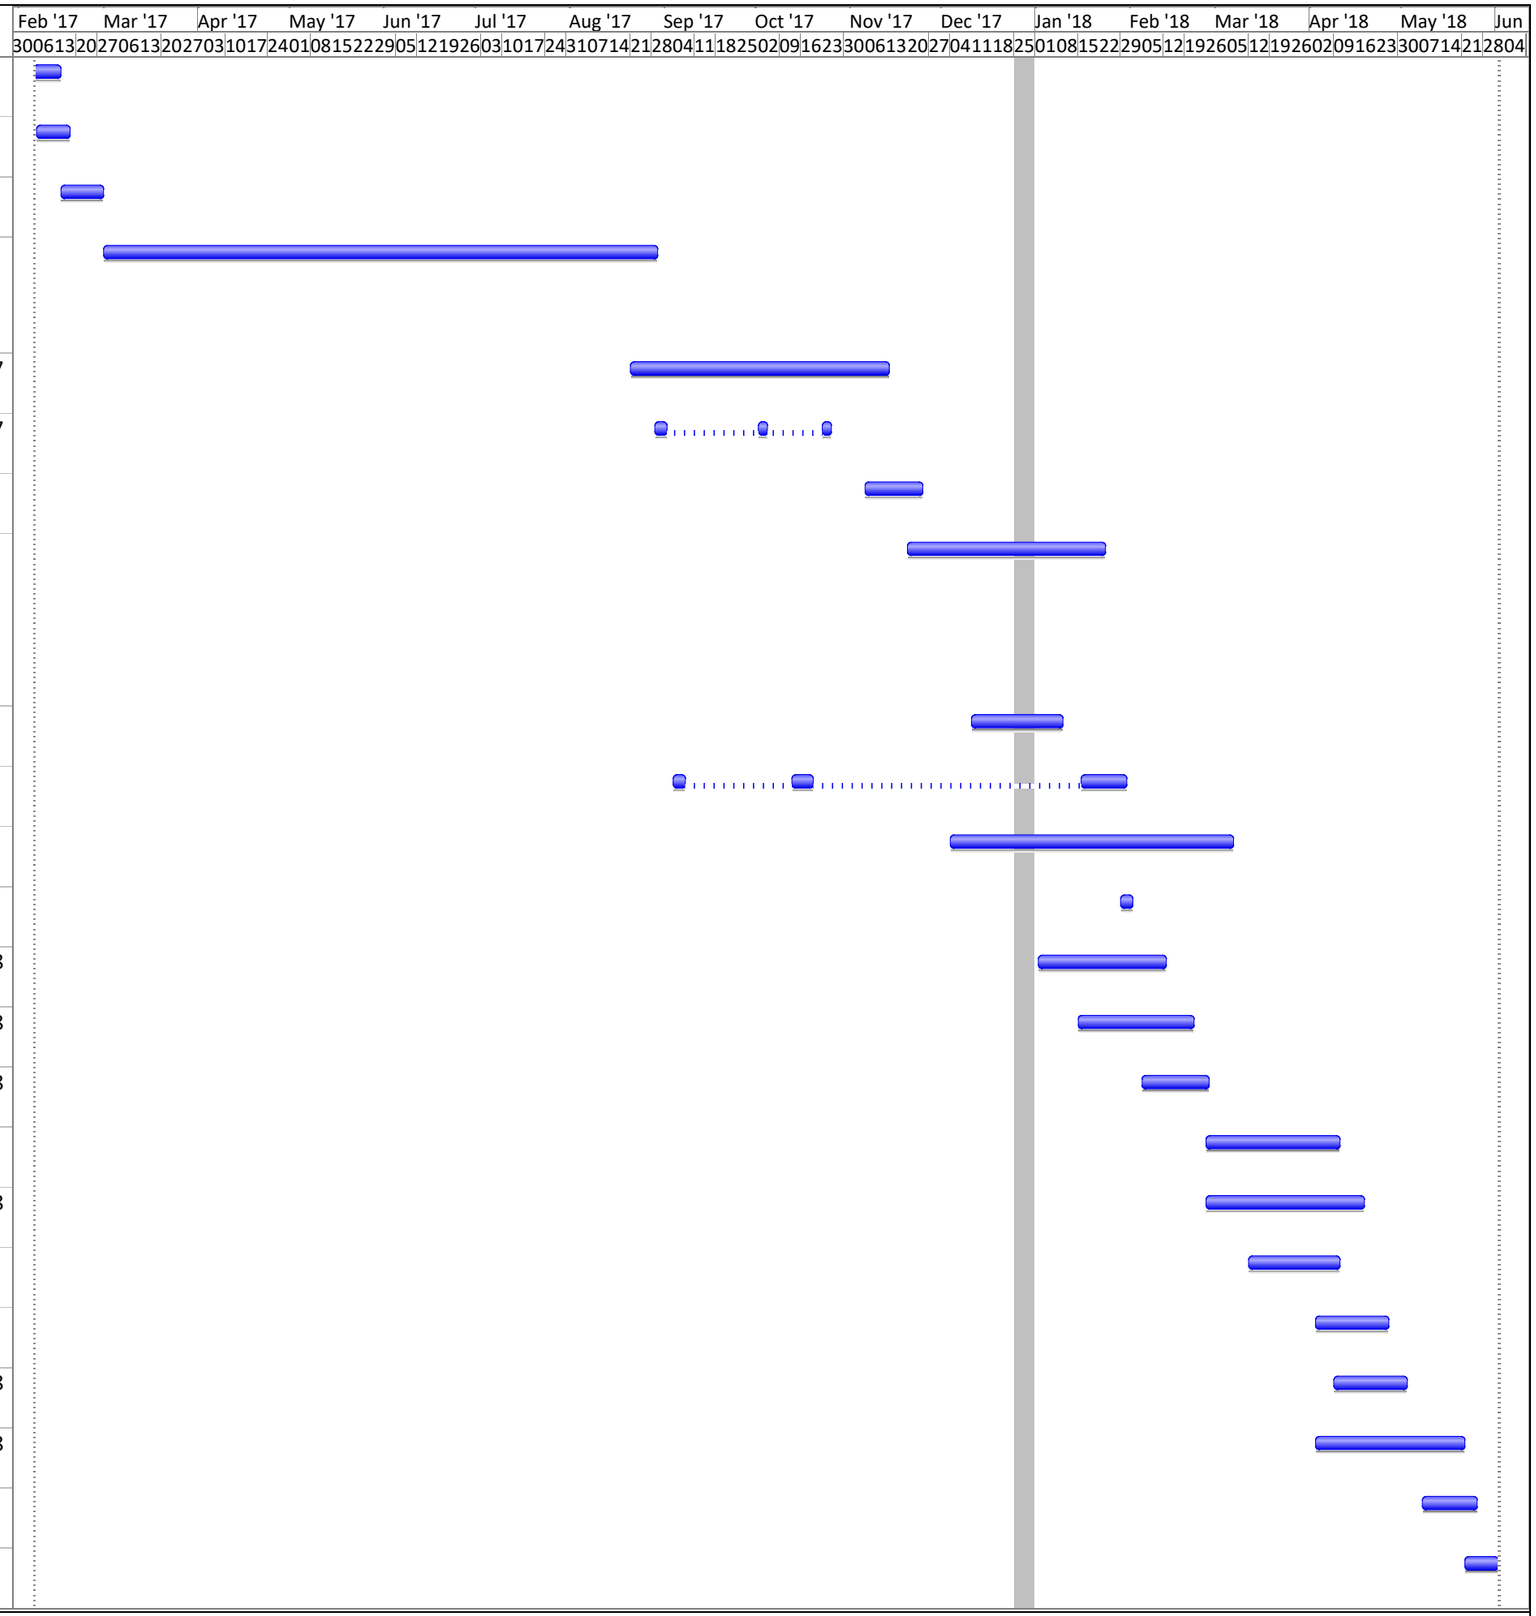

20-21 Kings Mews - Programme 1
01/12/2016

Task | Split | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline | Progress
